


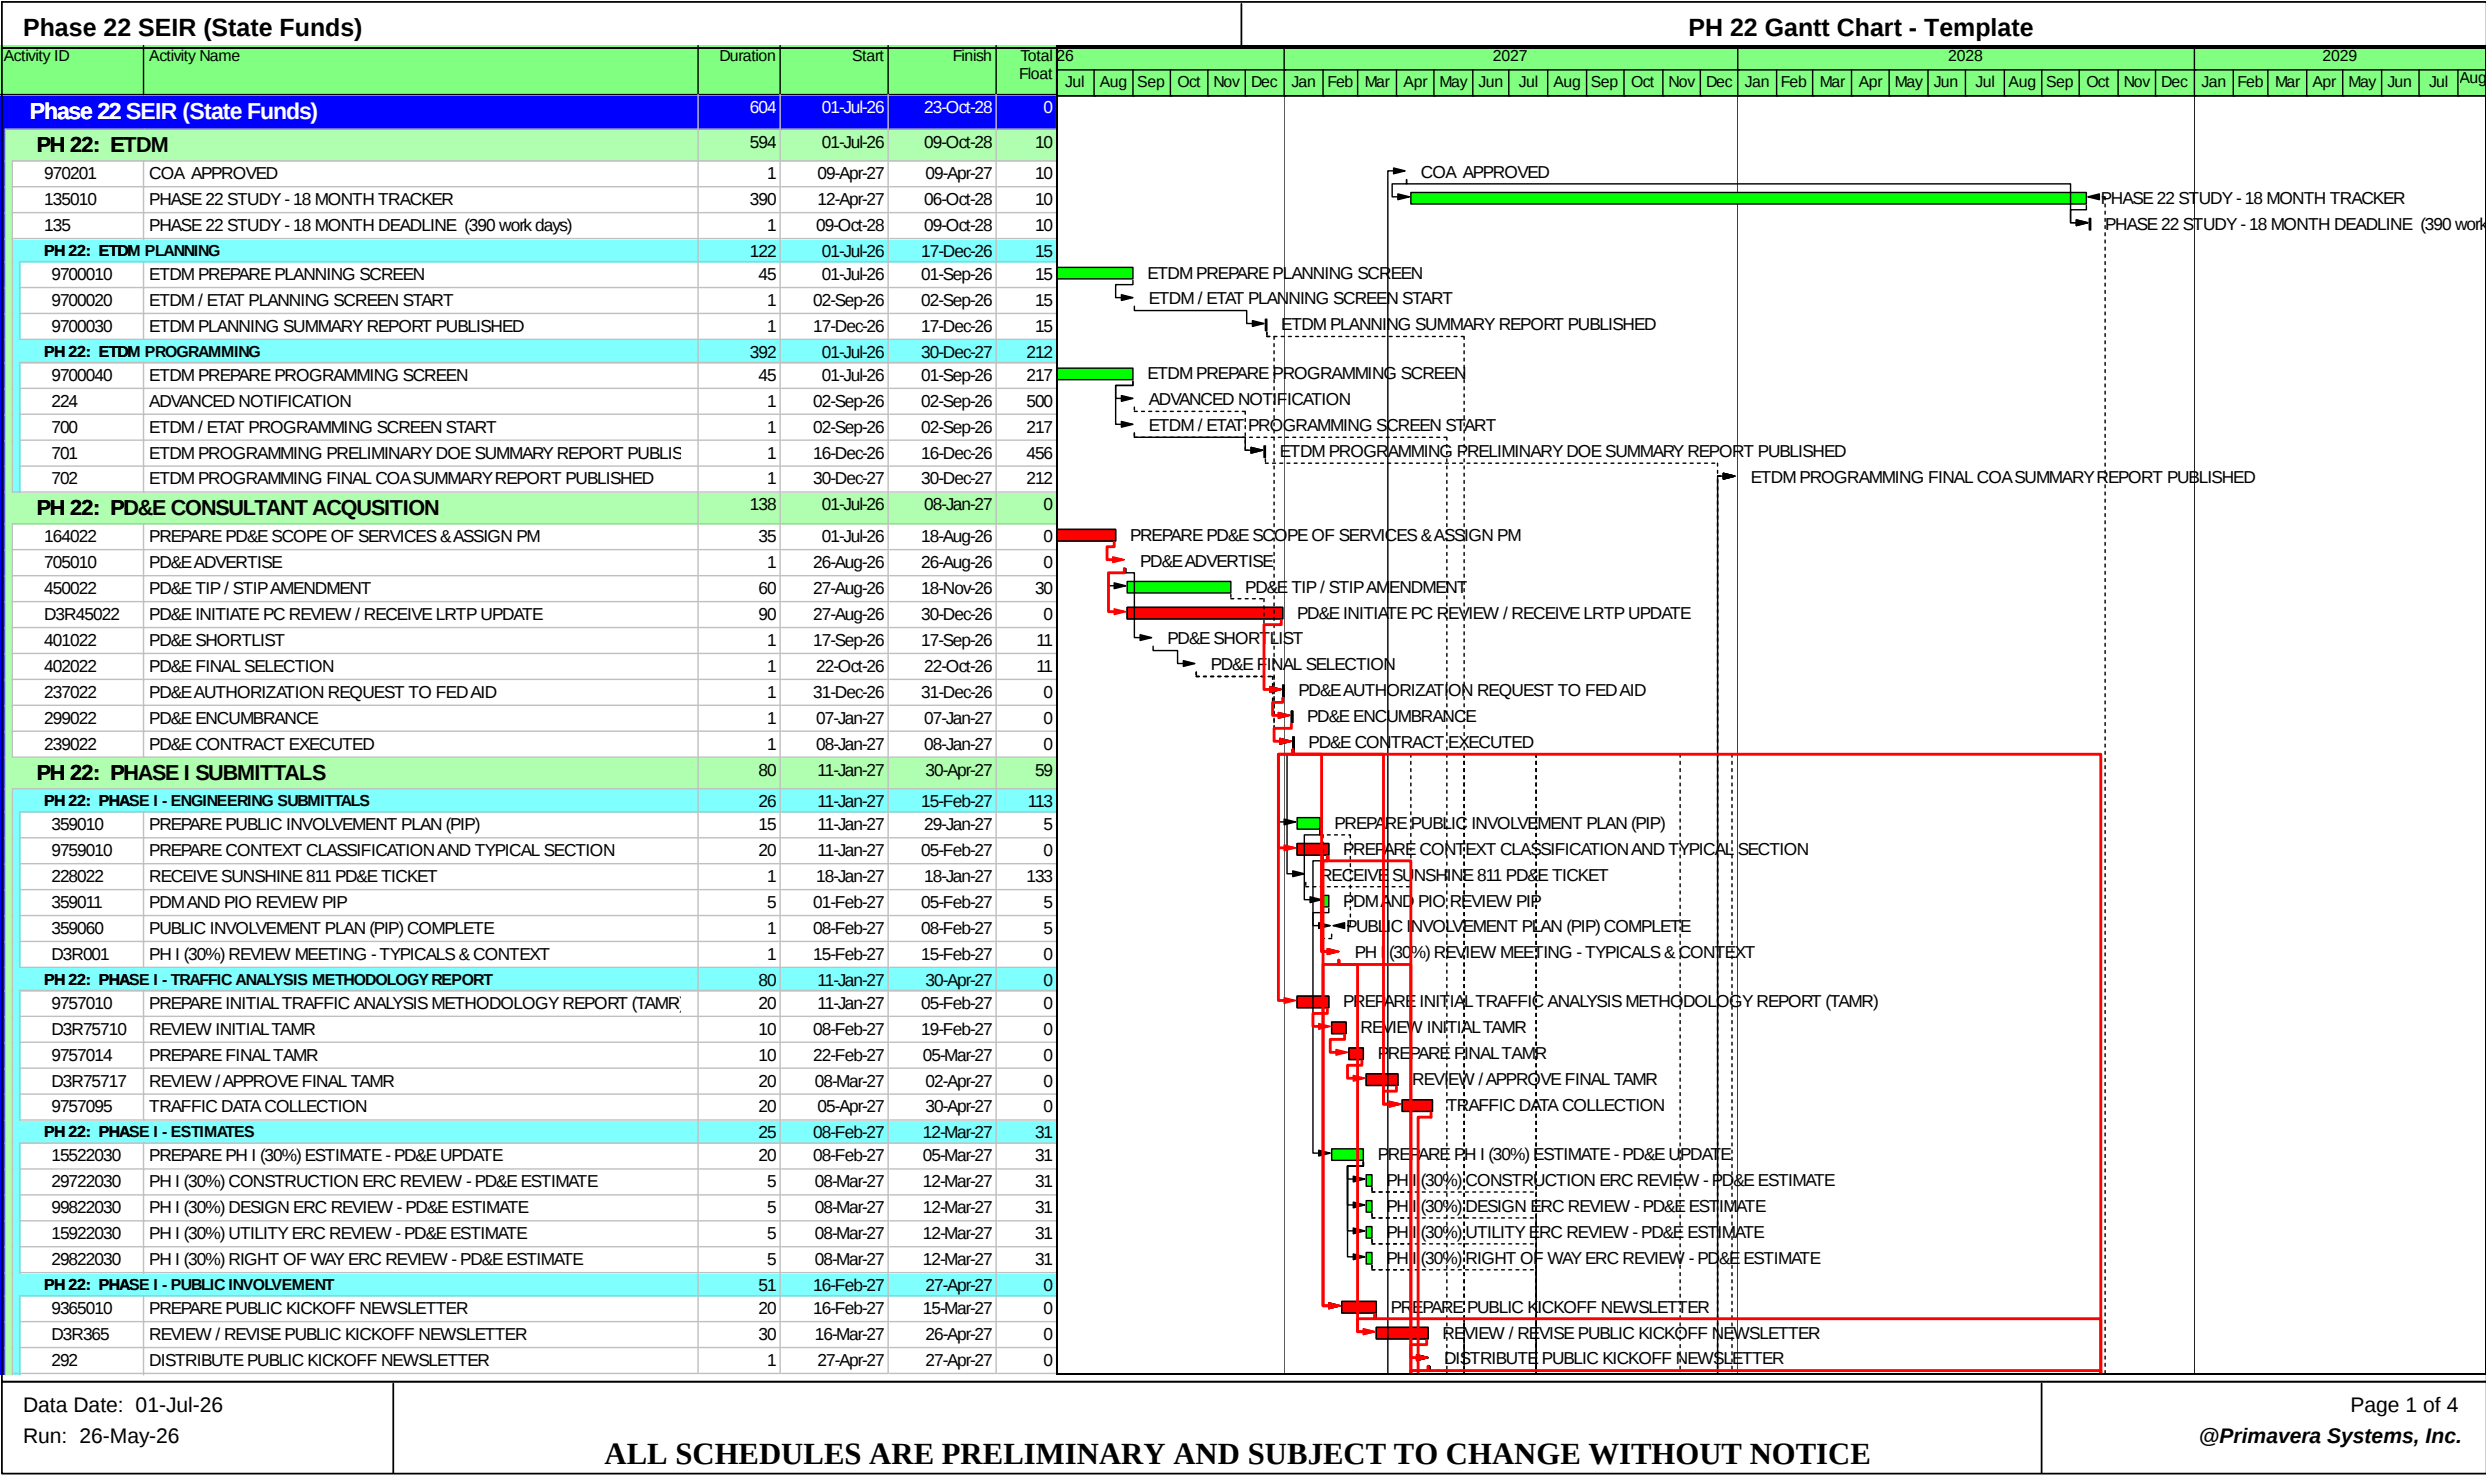

Phase 22 SEIR (State Funds)							PH 22 Gantt Chart - Template																																					
Activity ID		Activity Name	Duration	Start	Finish	Total Float	2027												2028												2029													
							Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
PH 22: PHASE II SUBMITTALS			134	28-Apr-27	01-Nov-27	229																																						
PH 22: PHASE II - ENGINEERING SUBMITTALS			73	28-Apr-27	06-Aug-27	81																																						
1002220	PREPARE HYDRAULIC REPORT(S) & SLIP STUDY		20	28-Apr-27	25-May-27	62																																						
2712210	PREPARE GEOTECH REPORT		20	28-Apr-27	25-May-27	62																																						
159000	PREPARE / SUBMIT UTILITY PACKAGE		20	28-Apr-27	25-May-27	62																																						
1092220	POND DATA COLLECTION		20	28-Apr-27	25-May-27	30																																						
1192210	PREPARE INITIAL CONCEPTUAL DESIGN PLANS		30	28-Apr-27	08-Jun-27	0																																						
1092210	STORMWATER MANAGEMENT ALTERNATIVES REPORT (SMART)		2	26-May-27	27-May-27	30																																						
1092230	PREPARE POND SITING REPORT (PSR) / CONCEPTUAL DRAINAGE DESIGN REPORT (CDDR)		30	28-May-27	08-Jul-27	30																																						
9710	PREPARE PLANNING CONSISTENCY REPORT		10	09-Jun-27	22-Jun-27	54																																						
D3R002	PH II (60%) REVIEW MEETING -TYPICALS & CONCEPTS		1	16-Jun-27	16-Jun-27	0																																						
9730	REVIEW PLANNING CONSISTENCY REPORT		20	23-Jun-27	20-Jul-27	54																																						
D3R3651	REVIEW / REVISE PHASE II - ENGINEERING SUBMITTAL		20	09-Jul-27	05-Aug-27	30																																						
274	BRIDGE HYDRAULIC REPORT COMPLETE		1	06-Aug-27	06-Aug-27	30																																						
100	LOCATION HYDRAULIC REPORT COMPLETE		1	06-Aug-27	06-Aug-27	30																																						
271	GEOTECH REPORT COMPLETE		1	06-Aug-27	06-Aug-27	30																																						
109	POND SITING REPORT COMPLETE		1	06-Aug-27	06-Aug-27	81																																						
PH 22: PHASE II - PROJECT TRAFFIC ANALYSIS REPORT (PTAR)			75	03-May-27	13-Aug-27	76																																						
9757020	PREPARE INITIAL PROJECT TRAFFIC ANALYSIS REPORT (PTAR)		30	03-May-27	11-Jun-27	0																																						
D3R7571	REVIEW INITIAL PTAR		20	14-Jun-27	09-Jul-27	0																																						
9757011	PREPARE FINAL PTAR		20	12-Jul-27	06-Aug-27	76																																						
757	APPROVE FINAL PTAR		5	09-Aug-27	13-Aug-27	76																																						
PH 22: PHASE II - ESTIMATES			25	09-Jul-27	12-Aug-27	286																																						
15522060	PREPARE PH II (60%) ESTIMATE - PD&E UPDATE		20	09-Jul-27	05-Aug-27	31																																						
29722060	PH II (60%) CONSTRUCTION ERC REVIEW - PD&E ESTIMATE		5	06-Aug-27	12-Aug-27	286																																						
15922060	PH II (60%) UTILITY ERC REVIEW - PD&E ESTIMATE		5	06-Aug-27	12-Aug-27	286																																						
29822060	PH II (60%) RIGHT OF WAY ERC REVIEW - PD&E ESTIMATE		5	06-Aug-27	12-Aug-27	286																																						
99822060	PH II (60%) DESIGN ERC REVIEW - PD&E ESTIMATE		5	06-Aug-27	12-Aug-27	286																																						
PH 22: PHASE II - ENVIRONMENTAL SUBMITTALS			88	19-May-27	17-Sep-27	0																																						
3352200	NOISE METHODOLOGY MEETING (w/ D3 Noise)		1	19-May-27	19-May-27	27																																						
1412210	PREPARE CONCEPTUAL STAGE RELOCATION PLAN (CSRP)		20	09-Jun-27	06-Jul-27	28																																						
1742210	PREPARE CONTAMINATION SCREENING EVALUATION REPORT (CSER)		20	09-Jun-27	06-Jul-27	28																																						
3352211	PREPARE / REVIEW NOISE TRAFFIC DATA SHEET (w/ D3 Noise)		20	28-Jun-27	23-Jul-27	0																																						
D3R76001	REVIEW / REVISE PHASE II - ENVIRONMENTAL SUBMITTAL		20	07-Jul-27	03-Aug-27	28																																						
3352210	PREPARE INITIAL NOISE STUDY REPORT		20	26-Jul-27	20-Aug-27	0																																						
D3R3351	REVIEW INITIAL NOISE STUDY REPORT		20	23-Aug-27	17-Sep-27	0																																						
PH 22: PHASE II - ENVIRONMENTAL SUBMITTAL - INITIAL NRE			60	09-Jun-27	31-Aug-27	13																																						
7612200	NATURAL RESOURCES EVALUATION (NRE) SURVEY		20	09-Jun-27	06-Jul-27	13																																						
7612210	PREPARE INITIAL NRE REPORT		20	07-Jul-27	03-Aug-27	13																																						
D3R7610	REVIEW INITIAL NRE REPORT		20	04-Aug-27	31-Aug-27	13																																						
PH 22: PHASE II - ENVIRONMENTAL SUBMITTAL- INITIAL CRAS			60	09-Jun-27	31-Aug-27	13																																						
333000	CULTURAL RESOURCES ASSESSMENT SURVEY (CRAS)		20	09-Jun-27	06-Jul-27	13																																						
333010	PREPARE INITIAL CRAS		20	07-Jul-27	03-Aug-27	13																																						
D3R3331	REVIEW INITIAL CRAS		20	04-Aug-27	31-Aug-27	13																																						
PH 22: PHASE II - SECTION 4(f) DETERMINATION OF APPLICABILITY (DOA)			81	28-Apr-27	18-Aug-27	22																																						
975100	SECTION 4(f) APPLICABLE (Y/N?)		1	28-Apr-27	28-Apr-27	51																																						
975105	PREPARE INITIAL SECTION 4(f) DETERMINATION OF APPLICABILITY (DOA) (SWEPT)		20	09-Jun-27	06-Jul-27	22																																						
D3R7511	REVIEW / REVISE INITIAL SECTION 4(f) DOA		20	07-Jul-27	03-Aug-27	22																																						
D3R7510	REVIEW SECTION 4(f) DOA IN SWEPT		10	04-Aug-27	17-Aug-27	22																																						
D3R7513	APPROVE 4(f) DOA (SWEPT)		1	18-Aug-27	18-Aug-27	22																																						

Phase 22 SEIR (State Funds)

PH 22 Gantt Chart - Template

Activity ID	Activity Name	Duration	Start	Finish	Total Float	2027												2028												2029													
						Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
PH 22: PHASE II - PUBLIC INVOLVEMENT																																											
9711010	PREPARE FOR ALTERNATIVES PUBLIC MEETING	30	26-May-27	06-Jul-27	8																																						
D3R7112	REVIEW ALTERNATIVES PUBLIC MEETING INFO SUBMITTAL	40	19-Jul-27	10-Sep-27	0																																						
711	HOLD ALTERNATIVES PUBLIC MEETING (VPU)	1	20-Sep-27	20-Sep-27	0																																						
9711050	PREPARE ALTERNATIVES PUBLIC MEETING COMMENTS REPORT	20	05-Oct-27	01-Nov-27	0																																						
PH 22: PHASE III SUBMITTALS																																											
PH 22: PHASE III - ENGINEERING SUBMITTALS																																											
710	PLANNING CONSISTENCY COMPLETION	1	21-Sep-27	21-Sep-27	10																																						
1192230	PREPARE FINAL CONCEPTUAL DESIGN PLANS	20	19-Oct-27	15-Nov-27	29																																						
9759020	PREPARE INITIAL TYPICAL SECTION PACKAGE	20	02-Nov-27	29-Nov-27	14																																						
D3R1190	REVIEW / REVISE PHASE III - ENGINEERING SUBMITTAL	20	30-Nov-27	27-Dec-27	78																																						
D3R003	PH III (90%) REVIEW MEETING	1	07-Dec-27	07-Dec-27	14																																						
D3R7591	DESIGN APPROVAL REQUESTS (PSEE DAR) - TYPICAL SECTION PACKAGE	20	08-Dec-27	04-Jan-28	23																																						
119	CONCEPTUAL DESIGN PLANS COMPLETE	1	29-Dec-27	29-Dec-27	78																																						
759	TYPICAL SECTION SELECTION	1	05-Jan-28	05-Jan-28	23																																						
970211	COA DETERMINATION MEETING WITH OEM	1	23-Feb-28	23-Feb-28	19																																						
PH 22: PHASE III - ENGINEERING SUBMITTAL - PER																																											
9760100	PREPARE PRELIMINARY ENGINEERING REPORT (PER)	30	05-Oct-27	15-Nov-27	40																																						
D3R7601	REVIEW / REVISE INITIAL PER	20	16-Nov-27	13-Dec-27	40																																						
PH 22: PHASE III - ESTIMATES																																											
9323080	PROVIDE WETLAND IMPACTS TO PERMITS OFFICE	1	26-Oct-27	26-Oct-27	234																																						
15522090	PREPARE PH III (90%) ESTIMATE - PD&E UPDATE	20	14-Dec-27	10-Jan-28	179																																						
29722090	PH III (90%) CONSTRUCTION ERC REVIEW - PD&E ESTIMATE	5	11-Jan-28	17-Jan-28	179																																						
15922090	PH III (90%) UTILITY ERC REVIEW - PD&E ESTIMATE	5	11-Jan-28	17-Jan-28	179																																						
29822090	PH III (90%) RIGHT OF WAY ERC REVIEW - PD&E ESTIMATE	5	11-Jan-28	17-Jan-28	179																																						
32322090	PH III (90%) MITIGATION ERC REVIEW - PD&E ESTIMATE	5	11-Jan-28	17-Jan-28	179																																						
99822090	PH III (90%) DESIGN ERC REVIEW - PD&E ESTIMATE	5	11-Jan-28	17-Jan-28	179																																						
PH 22: PHASE III - ENVIRONMENTAL SUBMITTALS																																											
1412230	PREPARE FINAL CONCEPTUAL STAGE RELOCATION PLAN	20	02-Nov-27	29-Nov-27	0																																						
3352240	PREPARE FINAL NOISE STUDY REPORT	20	02-Nov-27	29-Nov-27	0																																						
1742230	PREPARE FINAL CONTAMINATION SCREENING EVALUATION REPORT	20	02-Nov-27	29-Nov-27	0																																						
D3R14101	REVIEW / REVISE PHASE III - ENVIRONMENTAL SUBMITTAL	20	30-Nov-27	27-Dec-27	0																																						
141	CONCEPTUAL STAGE RELOCATION PLAN COMPLETE	1	28-Dec-27	28-Dec-27	79																																						
335	NOISE STUDY REPORT COMPLETE	1	28-Dec-27	28-Dec-27	79																																						
174	CONTAMINATION SCREENING EVALUATION REPORT COMPLETE	1	28-Dec-27	28-Dec-27	79																																						
PH 22: PHASE III - ENVIRONMENTAL SUBMITTAL - NRE																																											
7612240	PREPARE FINAL NRE REPORT	25	21-Sep-27	25-Oct-27	105																																						
D3R7615	REVIEW / REVISE FINAL NRE REPORT	20	26-Oct-27	22-Nov-27	105																																						
FWR7611	FWS / FWC / NMFS REVIEW / REVISE FINAL NRE REPORT	60	23-Nov-27	14-Feb-28	105																																						
752	INFORMAL USFWS CONSULTATION COMPLETE	1	15-Feb-28	15-Feb-28	105																																						
761	NATURAL RESOURCE EVALUATION (NRE) COMPLETED	1	16-Feb-28	16-Feb-28	105																																						
PH 22: PHASE III - ENVIRONMENTAL SUBMITTAL- CRAS																																											
3332210	PREPARE FINAL CRAS	20	21-Sep-27	18-Oct-27	102																																						
D3R3333	REVIEW / REVISE FINAL CRAS	20	19-Oct-27	15-Nov-27	102																																						
D3R3335	REVIEW FINAL CRAS (SWEPT)	10	16-Nov-27	29-Nov-27	102																																						
SHR3331	SHPO REVIEW / REVISE CRAS	60	30-Nov-27	21-Feb-28	102																																						
762	SHPO CONSULTATION COMPLETE	1	28-Aug-28	28-Aug-28	24																																						
PH 22: PHASE III - ENVIRONMENTAL SUBMITTAL- SECTION 4(f)																																											
9751080	PREPARE SECTION 4(f) EVALUATION	20	16-Nov-27	13-Dec-27	152																																						
D3R7515	REVIEW SECTION 4(f) EVALUATION	20	14-Dec-27	10-Jan-28	152																																						

Data Date: 01-Jul-26
Run: 26-May-26

ALL SCHEDULES ARE PRELIMINARY AND SUBJECT TO CHANGE WITHOUT NOTICE

