ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
0	Planning and PD&E (SEIR)		960 days	Mon 8/1/16	Fri 4/3/20	0 days		
1	PLANNING ACTIVITIES		251 days	Mon 8/1/16	Mon 7/17/17	0 days		
2	District SWAT Strategy Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting)	746	1 day	Mon 8/1/16	Mon 8/1/16	0 days		3FS+131 days
3	District SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted)		2 days	Wed 2/1/17	Thu 2/2/17	0 days	2FS+131 days	6FS+20 days,7FS+20 days,8FS+20 days
4	ETDM PROGRAMMING SCREEN		97 days	Fri 3/3/17	Mon 7/17/17	0 days		
5	ETDM Programming Screen Meeting		20 days	Fri 3/3/17	Thu 3/30/17	0 days		
6	ETDM Programming Screen PED		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9
7	ETDM Programming Screen Purpose and Need		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9,15,16
8	Planning Consistency Completion	710	5 days	Fri 3/3/17	Thu 3/9/17	801 days	3FS+20 days	9
9	ETDM PROGRAMMING SCREEN START/ADVANCE NOTIFICATION	700, 224	32 days	Fri 3/31/17	Mon 5/15/17	0 days	6,7,8	10,24
10	ETDM Programming Screen Responses		44 days	Tue 5/16/17	Fri 7/14/17	0 days	9	11
11	ETDM PROGRAMMING PRELIMINARY SUMMARY REPORT PUBLISHED	701	1 day	Mon 7/17/17	Mon 7/17/17	0 days	10	136,13FS+10 days,35
12	PRE-PD&E ACTIVITIES		261 days	Tue 8/1/17	Tue 7/31/18	0 days		
13	SWAT Kickoff Meeting	747	1 day	Tue 8/1/17	Tue 8/1/17	0 days	11FS+10 days	14,16
14	Assign PD&E Project Manager	704	1 day	Wed 8/2/17	Wed 8/2/17	0 days	13	16,24
15	TRAFFIC FORECAST ANALYSIS		116 days	Thu 8/3/17	Thu 1/11/18	0 days	7	
16	Traffic Methodology Meeting		1 day	Thu 8/3/17	Thu 8/3/17	0 days	7,14,13	17
17	Traffic Methodology Memorandum		10 days	Fri 8/4/17	Thu 8/17/17	0 days	16	18
18	Traffic Data Collection		20 days	Fri 8/18/17	Thu 9/14/17	0 days	17	19
19	Prepare Traffic Projections		40 days	Fri 9/15/17	Thu 11/9/17	0 days	18	20
20	Draft Project Traffic Analysis Report		20 days	Fri 11/10/17	Thu 12/7/17	0 days	19	21,27
21	FDOT Review - Draft Project Traffic Forecast Report		15 days	Fri 12/8/17	Thu 12/28/17	0 days	20	22
22	Final Project Traffic Forecast Report	757	10 days	Fri 12/29/17	Thu 1/11/18	0 days	21	102,35
23	INTERCHANGE ACCESS REQUEST		247 days	Thu 8/3/17	Fri 7/13/18	94 days		
24	Initiate IJR/IMR/SIMR or IOAR		1 day	Thu 8/3/17	Thu 8/3/17	0 days	9,14	25
25	Prepare MLOU		5 days	Fri 8/4/17	Thu 8/10/17	0 days	24	26
26	DIRC/SPO Review of MLOU		10 days	Fri 8/11/17	Thu 8/24/17	75 days	25	27
27	Develop Alternatives		30 days	Fri 12/8/17	Thu 1/18/18	0 days	20,26	28
28	Perform Operational Analysis		30 days	Fri 1/19/18	Thu 3/1/18	0 days	27	29
29	Prepare Preliminary IMR/IJR		45 days	Fri 3/2/18	Thu 5/3/18	0 days	28	30
30	DIRC/SPO Reviw of Preliminary IJR/IMR		10 days	Fri 5/4/18	Thu 5/17/18	0 days	29	31
31	Prepare Final IJR/IMR		30 days	Fri 5/18/18	Thu 6/28/18	0 days	30	32
32	DIRC/SPO Review of Final IJR/IMR		10 days	Fri 6/29/18	Thu 7/12/18	0 days	31	33
33	IJR/IMR Approval	765	1 day	Fri 7/13/18	Fri 7/13/18	94 days	32	72,92
34	DEVELOP SCOPE AND SCHEDULE		21 days	Fri 1/12/18	Fri 2/9/18	0 days		
35	Begin PD&E Scope and Schedule		20 days	Fri 1/12/18	Thu 2/8/18	0 days	11,22	36
36	PD&E SCOPE AND SCHEDULE COMPLETION	703	1 day	Fri 2/9/18	Fri 2/9/18	0 days	35	39,38
37	PROCUREMENT		122 days	Mon 2/12/18	Tue 7/31/18	0 days		
38	PD&E Advertisement	705	1 day	Mon 2/12/18	Mon 2/12/18	0 days	36	39
39	Procurement		120 days	Tue 2/13/18	Mon 7/30/18	0 days	36,38	40
40	Notice to Proceed		1 day	Tue 7/31/18	Tue 7/31/18	0 days	39	43
41	PD&E STUDY		438 days	Wed 8/1/18	Fri 4/3/20	0 days		
42	PROJECT MANAGEMENT		7 days	Wed 8/1/18	Thu 8/9/18	0 days		
43	SEIR START	709	1 day	Wed 8/1/18	Wed 8/1/18	0 days	40	48,44,45
44	Prepare Project Management Plan		5 days	Thu 8/2/18	Wed 8/8/18	0 days	43	46
45	Prepare QC Plan		5 days	Thu 8/2/18	Wed 8/8/18	0 days	43	46
46	Project Kickoff Meeting with FDOT		1 day	Thu 8/9/18	Thu 8/9/18	0 days	44,45	77,78,80,49,79,82,84,81,85
47	PUBLIC INVOLVEMENT		389 days	Thu 8/2/18	Tue 1/28/20	0 days		
48	Prepare Public Involvement Plan		20 days	Thu 8/2/18	Wed 8/29/18	31 days	43	51
49	Public Involvement Data Collection		45 days	Fri 8/10/18	Thu 10/11/18	0 days	46	51
50	Prepare for Public Kickoff Meeting	365	47 days	Fri 10/12/18	Mon 12/17/18	62 days		
51	Site Review		1 day	Fri 10/12/18	Fri 10/12/18	0 days	82FS-60 days,48,49	52,53,54
52	Newsletter		20 days	Mon 10/15/18	Fri 11/9/18	0 days	51	55
53	Newspaper Ad		20 days	Mon 10/15/18	Fri 11/9/18	0 days	51	55
54	Elected/Appointed/Property Owner Letters		20 days	Mon 10/15/18	Fri 11/9/18	0 days	51	55
55	Presentation/Display Material Review		15 days	Mon 11/12/18	Fri 11/30/18	0 days	54,52,53	56
56	Public Kickoff Meeting		1 day	Mon 12/3/18	Mon 12/3/18	0 days	82,77,78,79,80,84,55	57
57	Public Comment Period		10 days	Tue 12/4/18	Mon 12/17/18	33 days	56	59
58	Prepare for Public Information Meeting	365	76 days	Fri 2/1/19	Fri 5/17/19	0 days		
59	Site Review		1 day	Fri 2/1/19	Fri 2/1/19	0 days	100FS-60 days,57	63,60,61,62
60	Newsletter		20 days	Mon 2/4/19	Fri 3/1/19	0 days	59	63
61	Newspaper Ad		20 days	Mon 2/4/19	Fri 3/1/19	0 days	59	63
62	Elected/Appointed/Property Owner Letters		20 days	Mon 2/4/19	Fri 3/1/19	0 days	59	63
63	Presentation/Display Material Review		15 days	Mon 3/4/19	Fri 3/22/19	29 days	59,60,61,62	64
64	Public Information Meeting	292	1 day	Fri 5/3/19	Fri 5/3/19	0 days	100FS+5 days,63	65
65	Public Comment Period		10 days	Mon 5/6/19	Fri 5/17/19	0 days	64	101,102,67
66	Prepare for Public Hearing	366	101 days	Tue 9/10/19	Tue 1/28/20	0 days		
67	Site Review		20 days	Tue 9/10/19	Mon 10/7/19	0 days	65,137FS-80 days	71,68,69,70
68	Newsletter		20 days	Tue 10/8/19	Mon 11/4/19	0 days	67	71
69	Newspaper Ad		20 days	Tue 10/8/19	Mon 11/4/19	0 days	67	71
70	Elected/Appointed/Property Owner Letters		20 days	Tue 10/8/19	Mon 11/4/19	0 days	67	71
71	Presentation/Display Material Review		15 days	Tue 11/5/19	Mon 11/25/19	20 days	67,68,69,70	72,73
72	Notice of Public Availability		15 days	Tue 12/24/19	Mon 1/13/20	0 days	71,137FS-5 days,109,173	
73	Public Hearing	262	1 day	Tue 1/14/20	Tue 1/14/20	0 days	72,71	74
74	Public Comment Period		10 days	Wed 1/15/20	Tue 1/28/20	0 days	73	138,142,139,140,141
75	ENGINEERING ANALYSIS		341 days	Fri 8/10/18	Fri 11/29/19	0 days		
76	Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	113 days		
77	Roadway Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	46	56
78	Drainage Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	46	56

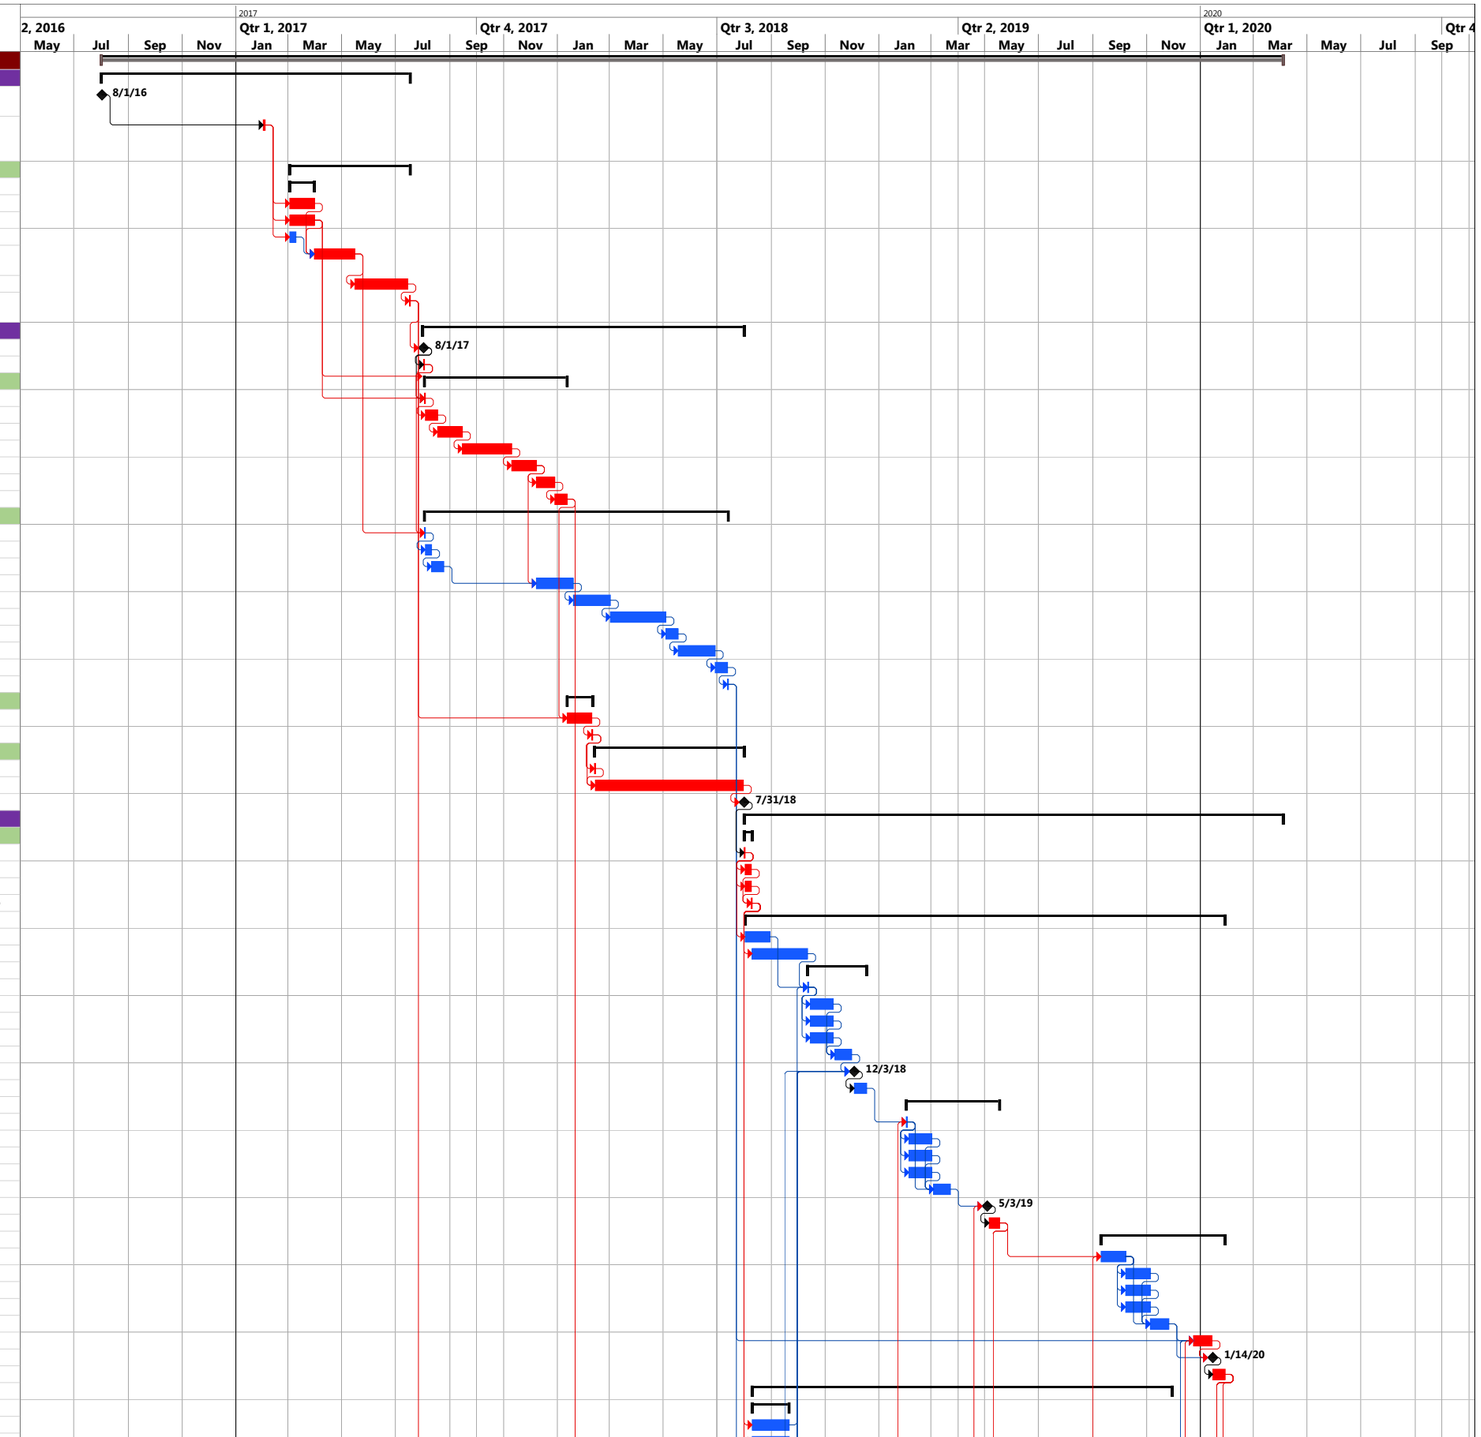

Project: Planning and PD&E (SE
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical

ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
79	Bridge Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	46	56
80	Geotechnical Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	46	56
81	Topographic Survey and ROW Mapping		30 days	Fri 8/10/18	Thu 9/20/18	401 days	46	
82	Prepare Base Map		30 days	Fri 8/10/18	Thu 9/20/18	51 days	46	56,51FS-60 days
83	Traffic Analysis		75 days	Fri 8/10/18	Thu 11/22/18	0 days		
84	Crash Data and Analysis		20 days	Fri 8/10/18	Thu 9/6/18	61 days	46	56
85	Prepare Capacity Analysis		30 days	Fri 8/10/18	Thu 9/20/18	0 days	46	92,86
86	Draft Project Traffic Analysis Report		20 days	Fri 9/21/18	Thu 10/18/18	0 days	85	87,90,91
87	FDOT Review - Draft Project Traffic Analysis Report		15 days	Fri 10/19/18	Thu 11/8/18	0 days	86	88
88	Final Project Traffic Analysis Report	757	10 days	Fri 11/9/18	Thu 11/22/18	0 days	87	92,102,93
89	Alternative Analysis		291 days	Fri 10/19/18	Fri 11/29/19	25 days		
90	Typical Sections Analysis		30 days	Fri 10/19/18	Thu 11/29/18	65 days	86	97
91	Complete Streets/Multi Modal Analysis		30 days	Fri 10/19/18	Thu 11/29/18	65 days	86	97
92	Concept Development		40 days	Fri 11/23/18	Thu 1/17/19	0 days	85,88,33	97,94,95,96
93	Access Management Analysis		40 days	Fri 11/23/18	Thu 1/17/19	30 days	88	97
94	Drainage Analysis		30 days	Fri 1/18/19	Thu 2/28/19	0 days	92	97
95	Utility Coordination & Analysis		30 days	Fri 1/18/19	Thu 2/28/19	0 days	92	97
96	Railroad Coordination		30 days	Fri 1/18/19	Thu 2/28/19	0 days	92	97
97	Evaluation Matrix (1st Draft)		5 days	Fri 3/1/19	Thu 3/7/19	0 days	90,91,94,95,96,93,92	99,98,112,113,114,115,116,117
98	Construction Cost Estimates (LRE)		10 days	Fri 3/8/19	Thu 3/21/19	20 days	97	100
99	Right-of-Way Analysis		20 days	Fri 3/8/19	Thu 4/4/19	10 days	97	100
100	Evaluation Matrix (2nd Draft)		5 days	Fri 4/19/19	Thu 4/25/19	0 days	98,99,112,113,114,115	64FS+5 days,59FS-60 days
101	Refine Alternatives (based on public input)		20 days	Mon 5/20/19	Fri 6/14/19	210 days	65	
102	Prepare 1st DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech,		30 days	Mon 5/20/19	Fri 6/28/19	0 days	65,22,88	103
103	FDOT Review - 1st DRAFT Engineering Reports		20 days	Mon 7/1/19	Fri 7/26/19	0 days	102	104
104	Update DRAFT Engineering Reports		15 days	Mon 7/29/19	Fri 8/16/19	0 days	103	105
105	VE Study		5 days	Mon 8/19/19	Fri 8/23/19	0 days	104	106FS+20 days
106	VE Issues Resolution		10 days	Mon 9/23/19	Fri 10/4/19	0 days	105FS+20 days	130,128,107,134,136,108,131
107	Prepare Typical Section Package		20 days	Mon 10/7/19	Fri 11/1/19	0 days	106	109,110
108	Prepare Design Variations and Exceptions		20 days	Mon 10/7/19	Fri 11/1/19	0 days	106	109
109	Typical Section Selection	759	20 days	Mon 11/4/19	Fri 11/29/19	16 days	107,108	72
110	FDOT Review - 2nd DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech, PER)		20 days	Mon 11/4/19	Fri 11/29/19	16 days	107	72
111	ENVIRONMENTAL ANALYSIS		172 days	Fri 3/8/19	Mon 11/4/19	0 days		
112	Data Collection & Cultural Resources Assessment Survey		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,120
113	Data Collection & Noise Analysis		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,122
114	Data Collection & Contamination Screen Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,121
115	Wetland Delineation and Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,119
116	Data Collection & Wildlife Survey		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,119
117	Essential Fish Habitat Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	97	100,119
118	Determination of Section 4(f)		15 days	Fri 3/8/19	Thu 3/28/19	0 days	97	123
119	Prepare 1st Draft Natural Resource Evaluation Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	115,116,117	124
120	Prepare 1st Draft Cultural Resources Assessment Survey		30 days	Fri 4/19/19	Thu 5/30/19	0 days	112	124
121	Prepare 1st Draft Contamination Screen Evaluation Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	114	124
122	Prepare 1st Draft Noise Study Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	113	124
123	Prepare Draft Section 4(f) Evaluation		30 days	Fri 3/29/19	Thu 5/9/19	15 days	118	124
124	FDOT Review 1st DRAFT Environmental Reports (NRE, CSER, CRAS, Noise, Section 4(f))		20 days	Fri 5/31/19	Thu 6/27/19	0 days	119,120,121,122,123	125
125	Update Environmental Reports		15 days	Fri 6/28/19	Thu 7/18/19	0 days	124	128,126,127
126	Finalize Cultural Resources Assessment Survey	333	10 days	Fri 7/19/19	Thu 8/1/19	46 days	125	128
127	Finalize Natural Resource Evaluation Report	761	10 days	Fri 7/19/19	Thu 8/1/19	46 days	125	130,131
128	Submit CRAS to OEM		20 days	Mon 10/7/19	Fri 11/1/19	0 days	125,106,126	129
129	SHPO Consultation Complete	762	1 day	Mon 11/4/19	Mon 11/4/19	0 days	128	136
130	Submit NRE to USFWS		1 day	Mon 10/7/19	Mon 10/7/19	0 days	106,127	132
131	Submit NRE to NMFS		1 day	Mon 10/7/19	Mon 10/7/19	0 days	106,127	133
132	Informal USFWS Consultation Complete	752	10 days	Tue 10/8/19	Mon 10/21/19	10 days	130	136
133	Informal NMFS Consultation Complete	763	10 days	Tue 10/8/19	Mon 10/21/19	10 days	131	136
134	Prepare Conceptual Relocation Plan		20 days	Mon 10/7/19	Fri 11/1/19	1 day	106	136
135	FINAL SEIR DOCUMENTS		109 days	Tue 11/5/19	Fri 4/3/20	0 days		
136	Prepare DRAFT SEIR		20 days	Tue 11/5/19	Mon 12/2/19	0 days	106,11,129,132,133,13	137
137	FDOT Review DRAFT SEIR	713	20 days	Tue 12/3/19	Mon 12/30/19	0 days	136	72FS-5 days,67FS-80 days
138	Finalize Engineering & Environmental Reports	756	10 days	Wed 1/29/20	Tue 2/11/20	5 days	74	143
139	Finalize Section 4(f) Evaluation	751	5 days	Wed 1/29/20	Tue 2/4/20	0 days	74	142
140	Finalize Noise Study Report	335	5 days	Wed 1/29/20	Tue 2/4/20	0 days	74	142
141	Finalize Preliminary Engineering Report	760	5 days	Wed 1/29/20	Tue 2/4/20	10 days	74	143
142	Prepare FINAL SEIR		10 days	Wed 2/5/20	Tue 2/18/20	0 days	74,139,140	143
143	Submit FINAL SEIR to District OEM		20 days	Wed 2/19/20	Tue 3/17/20	0 days	142,138,141	144FS+2 days
144	District Secretary Approval of SEIR	722	0 days	Thu 3/19/20	Thu 3/19/20	0 days	143FS+2 days	145FS+10 days
145	Pass the Torch Meeting		1 day	Fri 4/3/20	Fri 4/3/20	0 days	144FS+10 days	

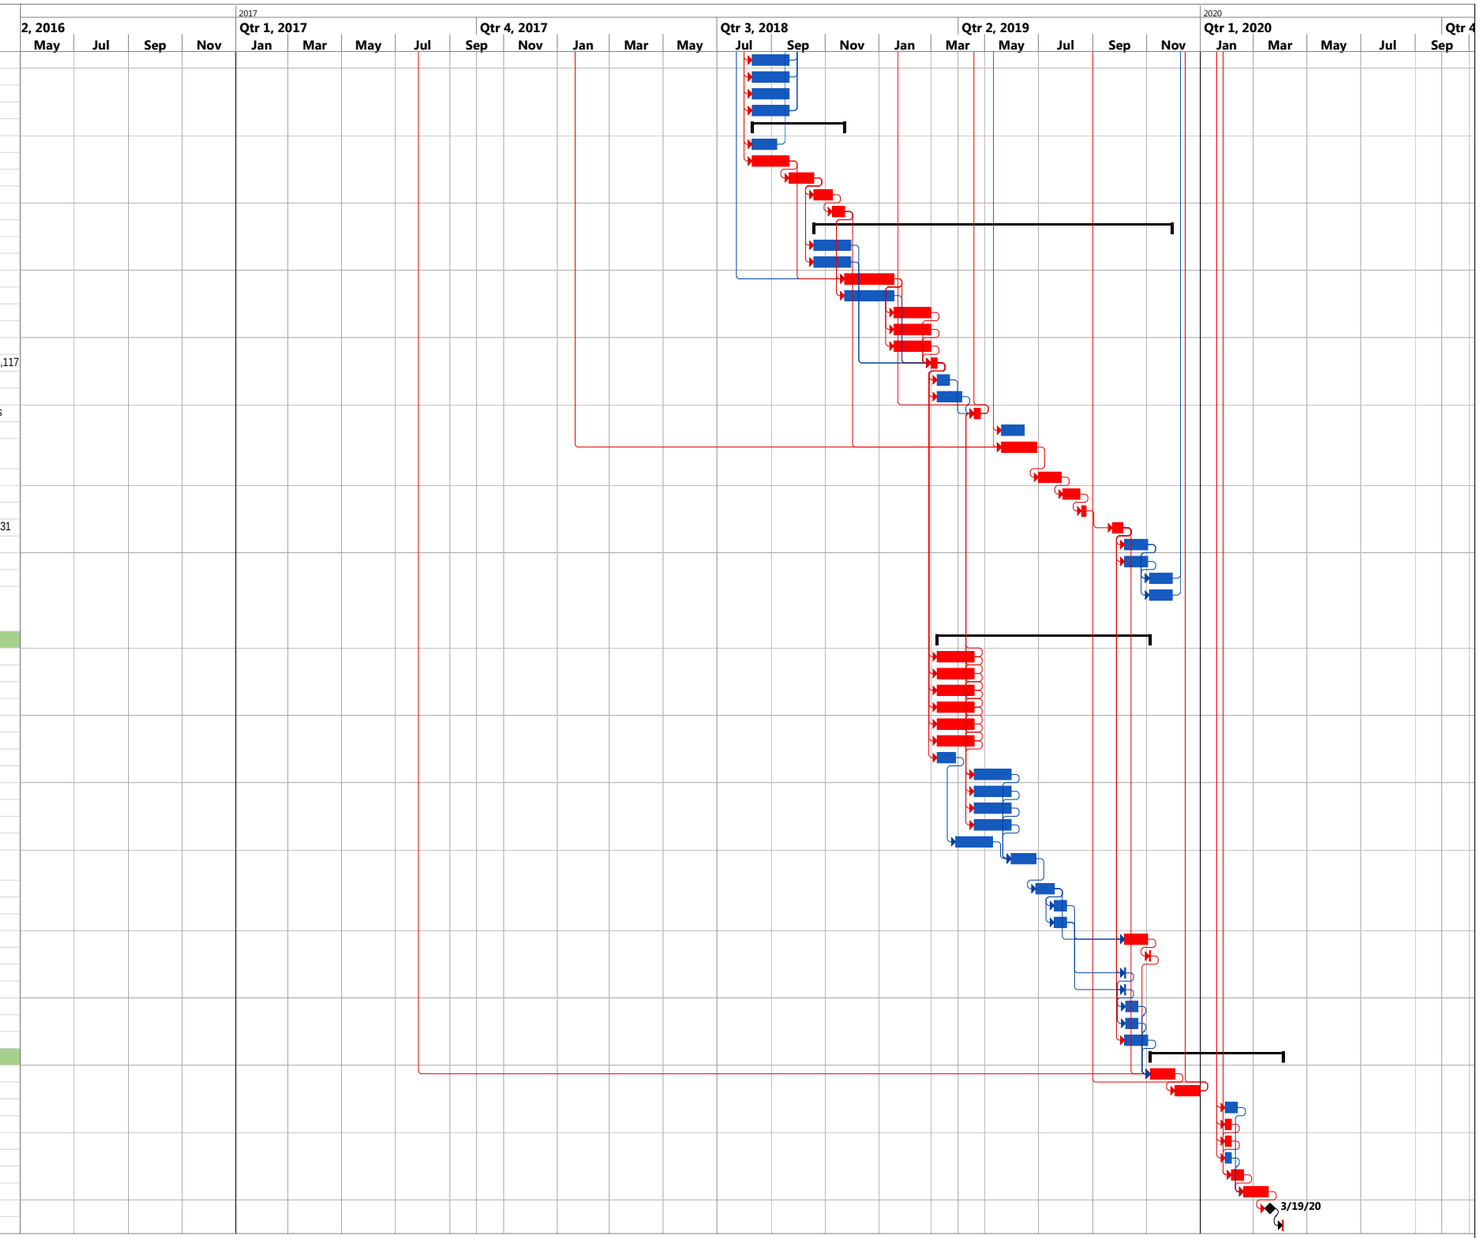

Project: Planning and PD&E (SE
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical
