


| Activity ID | PSM Code | Activity Name | Start | Finish | Total Float | Predecessors | Successors |
|-----------------------------------------------|----------|---------------------------------------------------------------------------------------------------------------------|------------|-----------|-------------|------------------|---------------------|
| EA (Planning, PD&E).mpp | | | | | | | |
| PLANNING & PRE-PD&E ACTIVITIES | | | | | | | |
| 74600 | 746 | SWAT Planning Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting) | 21-Sep-17* | 21-Sep-17 | 0 | | E1040, E1050, 77000 |
| 77000 | 770 | SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted) | 26-Mar-18 | 26-Mar-18 | 0 | 74600, E1080 | 70400, E1090, E1100 |
| 70400 | 704 | Assign PD&E Project Manager | 27-Mar-18 | 27-Mar-18 | 19 | 77000 | E1090, 70000, 22400 |
| 74700 | 747 | SWAT Kickoff Meeting | 20-Sep-18 | 20-Sep-18 | 0 | 70200 | 16401 |
| ETDM PLANNING SCREEN | | | | | | | |
| E1040 | | ETDM Planning Screen PED | 06-Oct-17 | 02-Nov-17 | 23 | 74600 | E1060 |
| E1050 | | ETMD Planning Screen Purpose and Need | 06-Oct-17 | 02-Nov-17 | 23 | 74600 | E1060 |
| E1060 | | ETDM Planning Screen Start | 03-Nov-17 | 18-Dec-17 | 23 | E1040, E1050 | E1070 |
| E1070 | | ETDM Planning Screen Responses | 19-Dec-17 | 19-Feb-18 | 23 | E1060 | E1080 |
| E1080 | | ETDM Planning Summary Screen Report Published | 20-Feb-18 | 20-Feb-18 | 23 | E1070 | 77000 |
| ETDM PROGRAMMING SCREEN | | | | | | | |
| E1090 | | ETDM Programming Screen PED | 24-Apr-18 | 21-May-18 | 0 | 77000, 70400 | 70000, 22400 |
| E1100 | | ETDM Programming Screen Purpose and Need | 24-Apr-18 | 21-May-18 | 0 | 77000 | 70000, 22400 |
| 70000 | 700 | ETDM Programming Screen Start | 22-May-18 | 04-Jul-18 | 0 | E1090, E1100, 70 | E1120 |
| 22400 | 224 | Advance Notification | 22-May-18 | 28-May-18 | 27 | 70400, E1090, E1 | E1120 |
| E1120 | | ETDM Programming Screen Responses | 05-Jul-18 | 04-Sep-18 | 0 | 70000, 22400 | 70200 |
| 70200 | 702 | ETDM Programming Final Summary Report Published | 05-Sep-18 | 05-Sep-18 | 0 | E1120 | 74700, 16401, E2310 |
| DEVELOP SCOPE AND SCHEDULE | | | | | | | |
| 16401 | 164 | Initial PD&E Scope (Stage 1) and Schedule Complete | 21-Sep-18 | 18-Oct-18 | 0 | 70200, 74700 | 70500 |
| PROCUREMENT | | | | | | | |
| 70500 | 705 | PD&E Advertisement | 19-Oct-18 | 19-Oct-18 | 0 | 16401 | E1170 |
| E1170 | | Procurement | 22-Oct-18 | 05-Apr-19 | 0 | 70500 | 16403 |
| 16403 | 164 | Final PD&E Scope (Stage 3) | 08-Apr-19 | 12-Apr-19 | 0 | E1170 | 23900, 23400 |
| 23900 | 239 | PD&E Contract Executed | 15-Apr-19 | 15-Apr-19 | 0 | 16403 | 23400 |
| 23400 | 234 | Notice to Proceed | 16-Apr-19* | 16-Apr-19 | 0 | 16403, 23900 | 70700 |
| PD&E STUDY | | | | | | | |
| PROJECT MANAGEMENT | | | | | | | |
| 70700 | 707 | EA Start | 16-Apr-19 | 16-Apr-19 | 0 | 23400 | E1220, E1230, 74800 |
| E1220 | | Prepare Project Management Plan | 17-Apr-19 | 23-Apr-19 | 0 | 70700 | E1240 |
| E1230 | | Prepare QC Plan | 17-Apr-19 | 23-Apr-19 | 0 | 70700 | E1240 |
| E1240 | | Project Kickoff Meeting with FDOT | 24-Apr-19 | 24-Apr-19 | 0 | E1220, E1230 | E1260, E1490, E1500 |
| PUBLIC INVOLVEMENT | | | | | | | |
| 74800 | 748 | Prepare Public Involvement Plan | 17-Apr-19 | 14-May-19 | 90 | 70700 | 36501 |
| E1260 | | Public Involvement Data Collection | 25-Apr-19 | 26-Jun-19 | 59 | E1240 | 36501 |
| Prepare for Public Kickoff Meeting | | | | | | | |
| 36501 | 365 | Site Review / Prepare for Public Kickoff Meeting | 27-Jun-19 | 27-Jun-19 | 59 | 74800, E1260 | E1280, E1290, E1300 |
| E1280 | | Newsletter | 28-Jun-19 | 25-Jul-19 | 59 | 36501 | E1310 |
| E1290 | | Prepare Newspaper/ FAR/ FDOT Website Notice | 28-Jun-19 | 25-Jul-19 | 59 | 36501 | E1310 |
| E1300 | | Prepare Elected/Appointed/Property Owner Letters | 28-Jun-19 | 25-Jul-19 | 59 | 36501 | E1310 |
| E1310 | | Presentation/Display Material Review | 26-Jul-19 | 15-Aug-19 | 59 | E1300, E1280, E1 | 29201 |
| 29201 | 292 | Public Kickoff Meeting | 16-Aug-19 | 16-Aug-19 | 59 | E1540, E1310 | E1330 |
| E1330 | | Public Comment Period | 19-Aug-19 | 30-Aug-19 | 59 | 29201 | 36502, E1670, E1780 |
| Prepare for Public Information Meeting | | | | | | | |



█ Actual Level of Effort
 █ Remaining Work
 ◆ Milestone
█ Actual Work
 █ Critical Remaining Work
 ⇨ summary

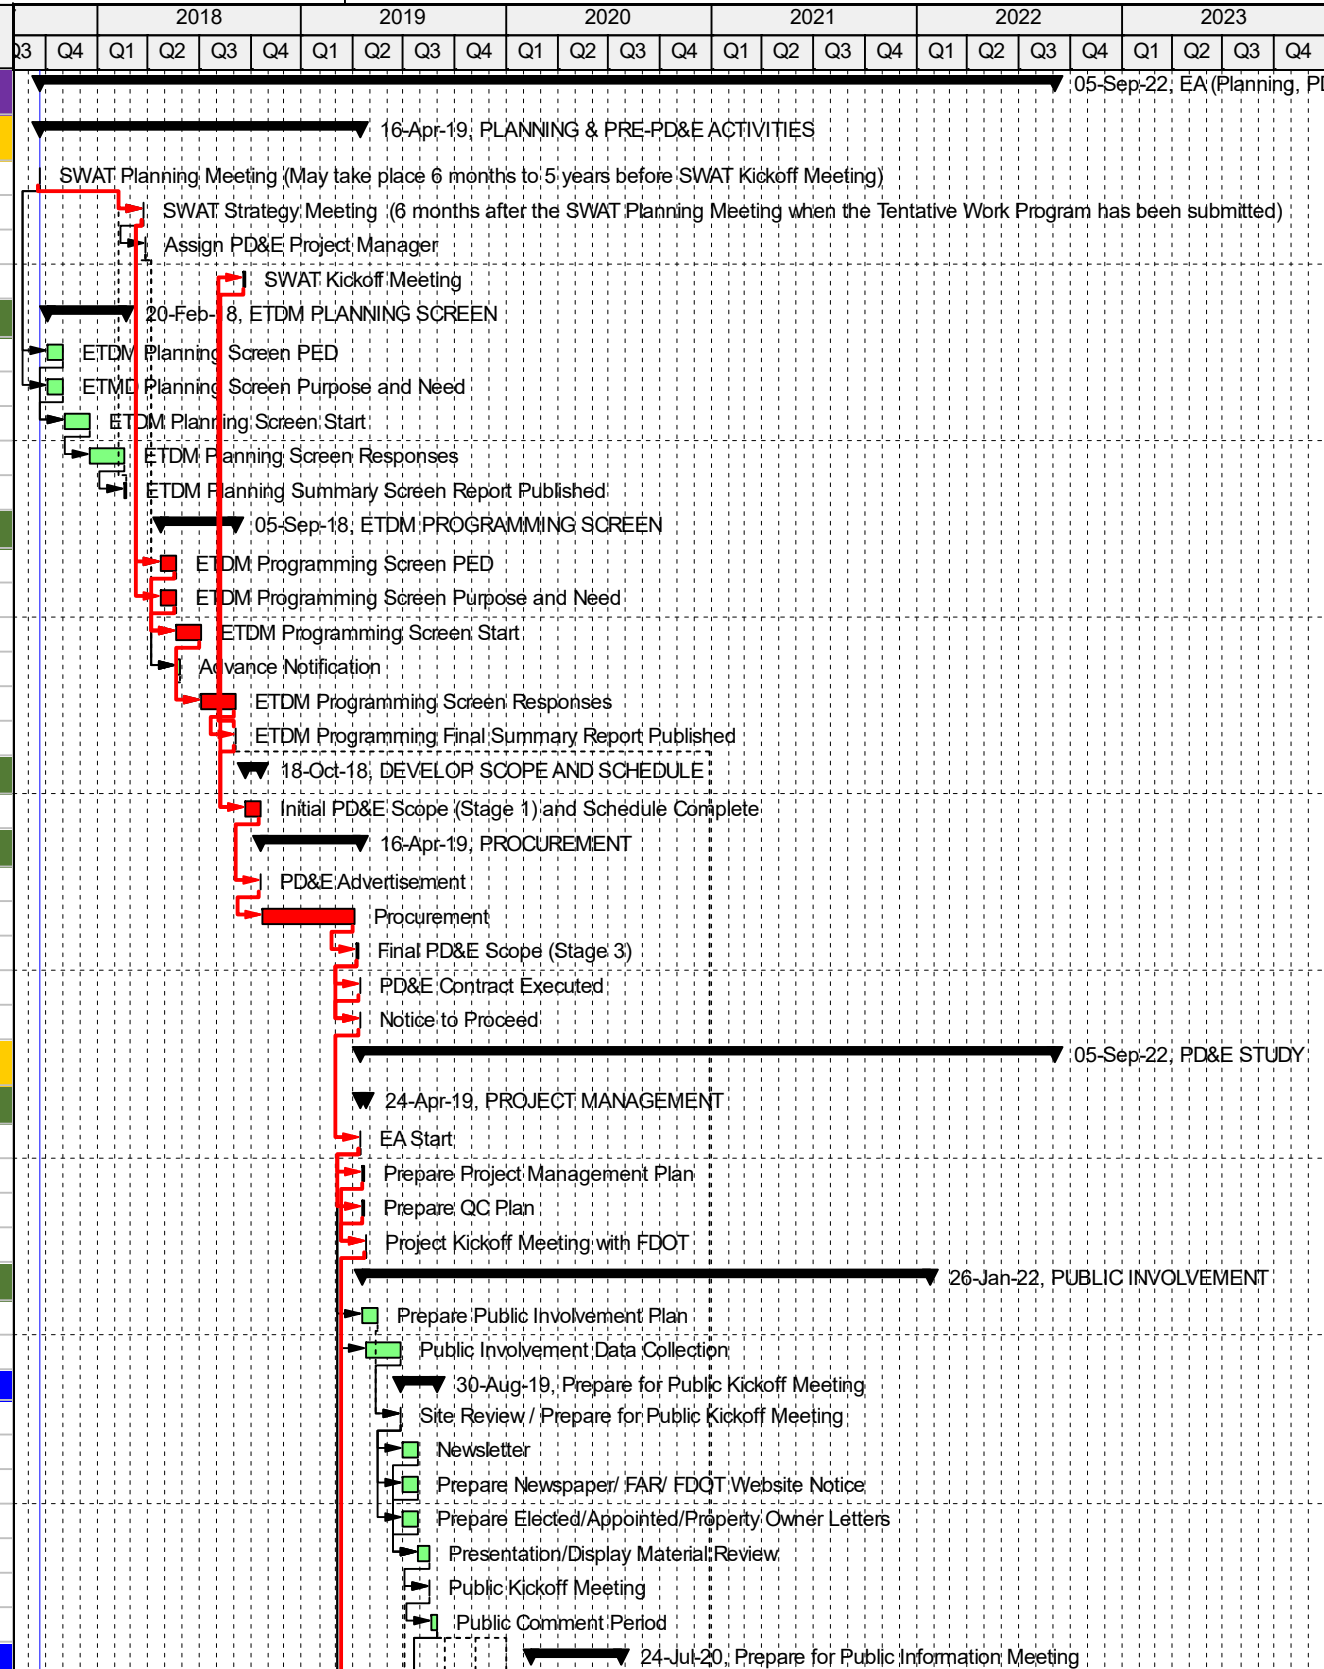
