


Activity ID	PSM Code	Activity Name	Start	Finish	Total Float	Predecessors	Successors
<b>EIS-ROD (Planning, PD&amp;E).mpp</b>							
<b>PLANNING &amp; PRE-PD&amp;E ACTIVITIES</b>							
74600	746	SWAT Planning Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting)	21-Sep-17*	21-Sep-17	0		E1010, E1020, 77000
77000	770	SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted)	26-Mar-18	26-Mar-18	0	74600, E1050	70400, E1080, E1090
70400	704	Assign PD&E Project Manager	27-Mar-18	27-Mar-18	19	77000	E1080, 70000, 22400
74700	747	SWAT Kickoff Meeting	20-Sep-18	20-Sep-18	0	70200	16401
<b>ETDM PLANNING SCREEN</b>							
E1010		ETDM Planning Screen PED	06-Oct-17	02-Nov-17	23	74600	E1030
E1020		ETMD Planning Screen Purpose and Need	06-Oct-17	02-Nov-17	23	74600	E1030
E1030		ETDM Planning Screen Start	03-Nov-17	18-Dec-17	23	E1010, E1020	E1040
E1040		ETDM Planning Screen Responses	19-Dec-17	19-Feb-18	23	E1030	E1050
E1050		ETDM Planning Summary Screen Report Published	20-Feb-18	20-Feb-18	23	E1040	77000
<b>ETDM PROGRAMMING SCREEN</b>							
E1080		ETDM Programming Screen PED	24-Apr-18	21-May-18	0	77000, 70400	70000, 22400
E1090		ETDM Programming Screen Purpose and Need	24-Apr-18	21-May-18	0	77000	70000, 22400
70000	700	ETDM/ETAT Programming Screen Start/Advance Notifi	22-May-18	04-Jul-18	0	70400, E1080, E1	E1110
22400	224	Advance Notification	22-May-18	04-Jul-18	0	70400, E1080, E1	E1110
E1110		ETDM Programming Screen Responses	05-Jul-18	04-Sep-18	0	70000, 22400	70200
70200	702	ETDM Programming Final Summary Report Published	05-Sep-18	05-Sep-18	0	E1110	74700, 16401, E2260
<b>DEVELOP SCOPE AND SCHEDULE</b>							
16401	164	Initial PD&E Scope (Stage 1) and Schedule Complete	21-Sep-18	18-Oct-18	0	74700, 70200	70500
<b>PROCUREMENT</b>							
70500	705	PD&E Advertisement	19-Oct-18	19-Oct-18	0	16401	E1160
E1160		Procurement	22-Oct-18	05-Apr-19	0	70500	16400
16400	164	Final PD&E Scope (Stage 3)	08-Apr-19	12-Apr-19	0	E1160	23900, 23400
23900	239	PD&E Contract Executed	15-Apr-19	15-Apr-19	0	16400	23400
23400	234	Notice to Proceed	16-Apr-19*	16-Apr-19	0	16400, 23900	E1200, E1210, 74800
<b>PD&amp;E STUDY</b>							
<b>PROJECT MANAGEMENT</b>							
E1200		Prepare Project Management Plan	17-Apr-19	23-Apr-19	0	23400	E1230
E1210		Prepare QC Plan	17-Apr-19	23-Apr-19	0	23400	E1230
E1230		Project Kickoff Meeting with FDOT	24-Apr-19	24-Apr-19	0	E1200, E1210	E1240, E1250, E1450
E1240		Prepare Draft NOI	25-Apr-19	01-May-19	121	E1230	E1320
E1320		District Review of NOI	02-May-19	08-May-19	121	E1240	72300
72300	723	OEM NOI Approval Final Review	09-May-19	29-May-19	121	E1320	70800
70800	708	NOI - EIS Start	10-Jun-19	02-Jul-19	121	72300	74100, E1420, E2260
<b>PUBLIC INVOLVEMENT</b>							
74800	748	Prepare Public Involvement Plan	17-Apr-19	14-May-19	155	23400	74100, 36501
E1250		Public Involvement Data Collection	25-Apr-19	26-Jun-19	124	E1230	74100, 36501
74100	741	EIS Scoping Meeting	03-Jul-19	03-Jul-19	136	74800, E1250, 70	E1450, E1460, E1470
<b>Prepare for Public Kickoff Meeting</b>							
36501	365	Site Review / Prepare for Public Kickoff Meeting	27-Jun-19	27-Jun-19	124	74800, E1250	E1380, E1390, E1400
E1380		Newsletter	28-Jun-19	25-Jul-19	124	36501	E1500
E1390		Prepare Newspaper/ FAR/ FDOT Website Notice	28-Jun-19	25-Jul-19	124	36501	E1500
E1400		Prepare Elected/Appointed/Property Owner Letters	28-Jun-19	25-Jul-19	124	36501	E1500



█ Actual Level of Effort   
 █ Remaining Work   
 ◆ Milestone  
█ Actual Work   
 █ Critical Remaining Work   
 ⇨ summary



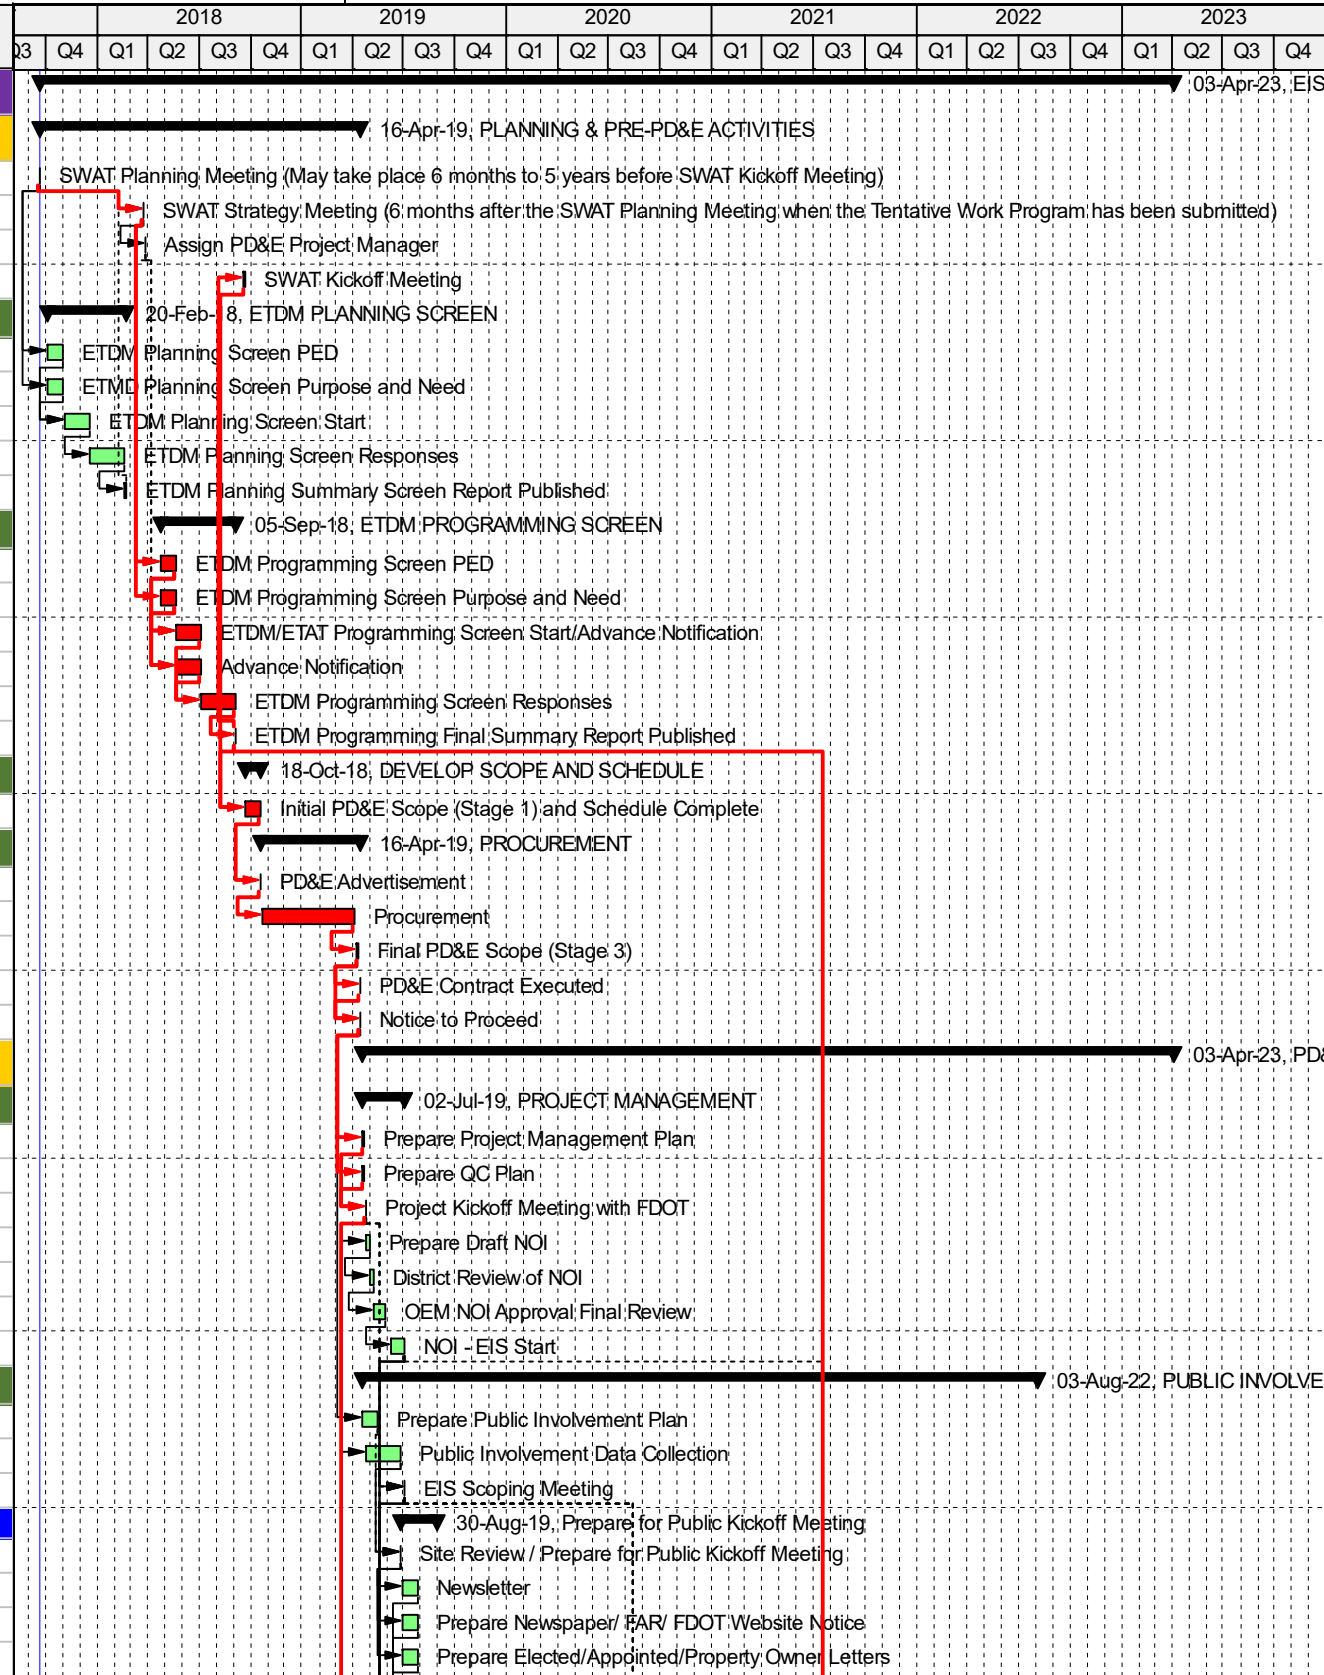



