


Activity ID	PSM Code	Activity Name	Start	Finish	Total Float	Predecessors	Successors
Type 2 CE (Planning, PD&E).mpp							
PLANNING & PRE-PD&E ACTIVITIES							
74600	746	SWAT Planning Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting)	21-Sep-17*	21-Sep-17	0		77000
77000	770	SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted)	26-Mar-18	26-Mar-18	0	74600	70400, C2120, C2220
70400	704	Assign PD&E Project Manager	27-Mar-18	27-Mar-18	19	77000	C2120, 70000, 22400
74700	747	SWAT Kickoff Meeting	20-Sep-18	20-Sep-18	0	70200	16401
ETDM PROGRAMMING SCREEN							
C2120		ETDM Programming Screen PED	24-Apr-18	21-May-18	0	77000, 70400	70000, 22400
C2220		ETDM Programming Screen Purpose and Need	24-Apr-18	21-May-18	0	77000	70000, 22400
70000	700	ETDM/ETAT Programing Screen Start	22-May-18	04-Jul-18	0	70400, C2120, C2	C1000
22400	224	Advance Notification	22-May-18		32	70400, C2120, C2	C1000
C1000		ETDM Programming Screen Responses	05-Jul-18	04-Sep-18	0	70000, 22400	70200
70200	702	ETDM Programming Final Summary Report Published	05-Sep-18	05-Sep-18	0	C1000	74700, 16401, C1440
DEVELOP SCOPE AND SCHEDULE							
16401	164	Initial PD&E Scope (Stage 1) and Schedule Complete	21-Sep-18	18-Oct-18	0	74700, 70200	70500
PROCUREMENT							
70500	705	PD&E Advertisement	19-Oct-18	19-Oct-18	0	16401	C1620
C1620		Procurement	22-Oct-18	05-Apr-19	0	70500	16403
16403	164	Final PD&E Scope (Stage 3)	08-Apr-19	12-Apr-19	0	C1620	23900, 23400
23900	239	PD&E Contract Executed	15-Apr-19	15-Apr-19	0	16403	23400
23400	234	Notice to Proceed	16-Apr-19*	16-Apr-19	0	16403, 23900	70600
PD&E STUDY							
PROJECT MANAGEMENT							
70600	706	TYPE 2 CE Start	16-Apr-19	16-Apr-19	0	23400	C1690, C1700, 74800
C1690		Prepare Project Management Plan	17-Apr-19	23-Apr-19	0	70600	C1710
C1700		Prepare QC Plan	17-Apr-19	23-Apr-19	0	70600	C1710
C1710		Project Kickoff Meeting with FDOT	24-Apr-19	24-Apr-19	0	C1690, C1700	C1730, C1990, C2000
PUBLIC INVOLVEMENT							
74800	748	Prepare Public Involvement Plan	17-Apr-19	14-May-19	31	70600	36501
C1730		Public Involvement Data Collection	25-Apr-19	26-Jun-19	0	C1710	36501
Prepare for Public Kickoff Meeting							
36501	365	Site Review / Prepare for Public Kickoff Meeting	27-Jun-19	27-Jun-19	0	74800, C1730	C1760, C1770, C1780
C1760		Newsletter	28-Jun-19	25-Jul-19	0	36501	C1790
C1770		Prepare Newspaper/ FAR/ FDOT Website Notice	28-Jun-19	25-Jul-19	0	36501	C1790
C1780		Prepare Elected/Appointed/Property Owner Letters	28-Jun-19	25-Jul-19	0	36501	C1790
C1790		Presentation/Display Material Review	26-Jul-19	15-Aug-19	0	C1780, C1760, C1	29201
29201	292	Public Kickoff Meeting	16-Aug-19	16-Aug-19	0	C2070, C1790, C2	C1810
C1810		Public Comment Period	19-Aug-19	30-Aug-19	0	29201	36502, C2180, C2300
Prepare for Public Information Meeting							
36502	365	Site Review / Prepare for Public Information Meeting	31-Oct-19	31-Oct-19	36	C1030, C1810	C1830, C1850, C1860
C1830		Newsletter	01-Nov-19	28-Nov-19	36	36502	C1870
C1850		Prepare Newspaper/ FAR/ FDOT Website	01-Nov-19	28-Nov-19	36	36502	C1870
C1860		Prepare Elected/Appointed/Property Owner Letters	01-Nov-19	28-Nov-19	36	36502	C1870
C1870		Presentation/Display Material Review	29-Nov-19	19-Dec-19	36	36502, C1830, C1	29202
29202	292	Public Information Meeting	10-Feb-20	10-Feb-20	0	C1030, C1870, C2	C1890
C1890		Public Comment Period	11-Feb-20	24-Feb-20	0	29202	36600, C1050, C1060

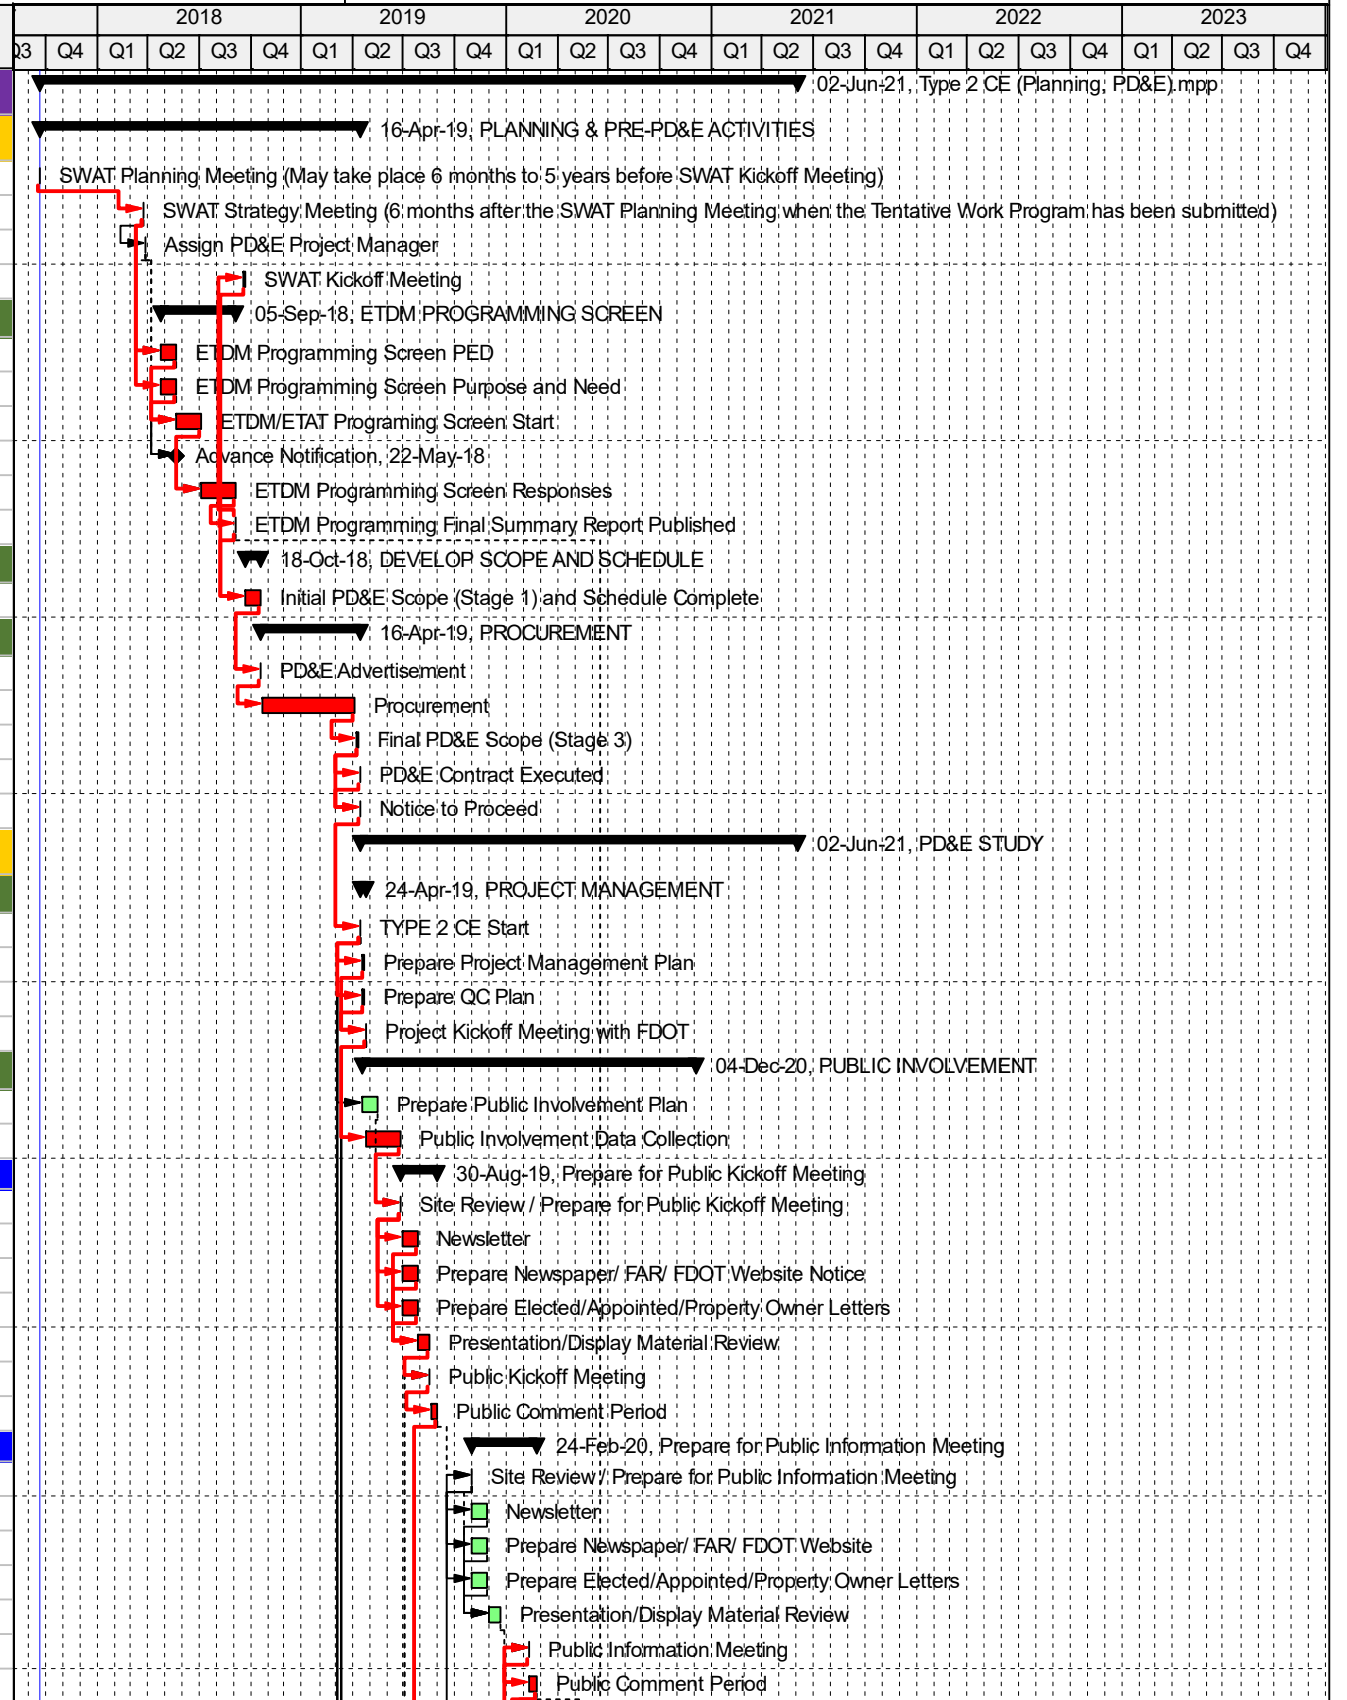

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ─── summary

Activity ID	PSM Code	Activity Name	Start	Finish	Total Float	Predecessors	Successors	2018												2019				2020				2021				2022				2023			
								Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		
Prepare for Public Hearing																																							
36600	366	Site Review / Prepare for Public Hearing	24-Jun-20	21-Jul-20	37	C1890, 71300	C1910, C1920, C1930																																
C1910		Newsletter	22-Jul-20	18-Aug-20	37	36600	C1950																																
C1920		Prepare Newspaper/ FAR/ FDOT Website Notice	22-Jul-20	18-Aug-20	37	36600	C1950																																
C1930		Prepare Elected/Appointed/Property Owner Letters	22-Jul-20	18-Aug-20	37	36600	C1950																																
C1950		Presentation/Display Material Review	19-Aug-20	08-Sep-20	37	36600, C1910, C1	C1960, 26200																																
C1960		Document Available for Public Review	30-Oct-20	19-Nov-20	0	C1950, 71300, 77	26200																																
26200	262	Public Hearing	20-Nov-20	20-Nov-20	0	C1960, C1950	C1980																																
C1980		Public Comment Period	23-Nov-20	04-Dec-20	0	26200	C1460, 75100, 33500																																
ENGINEERING ANALYSIS																																							
Data Collection																																							
C1990		Roadway Data Collection	25-Apr-19	05-Jun-19	76	C1710	C2300, C2310, C2330																																
C2000		Drainage Data Collection	25-Apr-19	05-Jun-19	76	C1710	C2300, C2310, C2330																																
C2010		Bridge Data Collection	25-Apr-19	05-Jun-19	76	C1710	C2300, C2310, C2330																																
C2020		Geotechnical Data Collection	25-Apr-19	05-Jun-19	76	C1710	C2300, C2310, C2330																																
C2030		Topographic Survey and ROW Mapping	25-Apr-19	05-Jun-19	76	C1710	C2300, C2310, C2330																																
C2040		Prepare Base Map	25-Apr-19	05-Jun-19	51	C1710	29201, C2330, C2340																																
Traffic Analysis																																							
C2050		Traffic Methodology Meeting	17-Apr-19	17-Apr-19	61	70600	C2060																																
C2060		Traffic Methodology Memorandum	18-Apr-19	01-May-19	61	C2050	C2100																																
C2070		Forecasting and Analysis	25-Apr-19	27-May-19	3	C1710	29201, C2080																																
C2080		Prepare Traffic Projections	28-May-19	24-Jun-19	3	C2070	C2090																																
C2090		Prepare Capacity Analysis	25-Jun-19	22-Jul-19	3	C2080	C2100, C2360																																
C2100		Draft Traffic Analysis Report	23-Jul-19	19-Aug-19	3	C2090, C2060	C2110, C2330, C2340																																
C2110		District Review - Draft Traffic Analysis Report	20-Aug-19	09-Sep-19	3	C2100	75700																																
75700	757	Final Traffic Analysis Report	10-Sep-19	16-Sep-19	3	C2110	C2360, C2370, C1060																																
Interchange Access Request																																							
C2140		Initiate IAR	17-Apr-19	17-Apr-19	52	70600	C2150																																
C2150		Prepare MLOU	18-Apr-19	01-May-19	52	C2140	C2160																																
C2160		DIRC/SPO Review of MLOU	02-May-19	22-May-19	52	C2150	C2170																																
C2170		FHWA Review of MLOU	23-May-19	19-Jun-19	52	C2160	C2180																																
C2180		Develop Alternatives	02-Sep-19	11-Oct-19	0	C1810, C2170	C2190																																
C2190		Perform Operational Analysis	14-Oct-19	08-Nov-19	0	C2180	C2200																																
C2200		Prepare Preliminary IAR	11-Nov-19	06-Dec-19	0	C2190	C2210																																
C2210		DIRC/SPO Review of Preliminary IAR	09-Dec-19	20-Dec-19	0	C2200	C2230																																
C2230		Comment Resolution & Update Preliminary IAR	23-Dec-19	10-Jan-20	0	C2210	C2240																																
C2240		FHWA Review of Preliminary IAR	13-Jan-20	07-Feb-20	0	C2230	29202, C2250																																
C2250		Prepare Final IAR	10-Feb-20	21-Feb-20	143	C2240	C2260																																
C2260		DIRC/SPO Review of Final IAR	24-Feb-20	06-Mar-20	143	C2250	C2270																																
C2270		Comment Resolution & Update Final IAR	09-Mar-20	13-Mar-20	143	C2260	C2280																																
C2280		FHWA/SPO Review of IAR	16-Mar-20	10-Apr-20	143	C2270	C2290																																
C2290		Safety Operations & Engineering Approval	13-Apr-20	13-Apr-20	143	C2280	C1960, 76500																																
Alternative Analysis																																							
C2310		Structure Analysis	06-Jun-19	17-Jul-19	106	C1990, C2000, C2	C2420																																
C2340		Complete Streets/Multi Modal Analysis	20-Aug-19	30-Sep-19	53	C2100, C2040, C1	C2420																																
C2350		Transit Analysis	20-Aug-19	30-Sep-19	53	C1990, C2000, C2	C2420																																
C2300		Roadway Analysis	02-Sep-19	11-Oct-19	44	C1990, C2000, C2	C2420																																

█ Actual Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ── summary

Type 2 CE (Planning, PDE).mpp		Classic Schedule Layout							31-Dec-19 15:33																							
Activity ID	PSM Code	Activity Name	Start	Finish	Total Float	Predecessors	Successors	2018				2019				2020				2021				2022				2023				
								Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
C1430		Prepare Conceptual Stage Relocation Plan	29-Jun-20	24-Jul-20	40	33900	C1440																									
75200	752	Informal USFWS Consultation Complete	30-Jun-20	29-Jul-20	37	C1400	C1440																									
76300	763	Informal NMFS Consultation Complete	30-Jun-20	29-Jul-20	37	C1400	C1440																									
FINAL ENGINEERING & TYPE 2 CE DOCUMENTATION																																
71000	710	Planning Consistency Complete	17-Apr-19	17-Apr-19	372	70600	C1440																									
C1440		Prepare DRAFT Type 2 CE for Public Availability	30-Jul-20	26-Aug-20	37	33900, 70200, 76:	71300																									
71300	713	District Review Draft Environmental Document	27-Aug-20	15-Sep-20	37	C1440	36600, C1960																									
C1460		Finalize Engineering & Environmental Reports	07-Dec-20	18-Dec-20	0	C1980	C1520																									
75100	751	Finalize Section 4(f)	07-Dec-20	11-Dec-20	5	C1980	C1520																									
33500	335	Finalize PD&E NSR	07-Dec-20	11-Dec-20	5	C1980	C1520																									
76000	760	Finalize PER	07-Dec-20	18-Dec-20	10	C1980	C1530																									
C1520		Prepare DRAFT Type 2 CE for OEM Signature	21-Dec-20	01-Jan-21	0	C1980, 75100, 33:	C1530																									
C1530		District Review DRAFT Type 2 CE	04-Jan-21	15-Jan-21	0	76000, C1520	C1540, 72200, 72600																									
C1540		District Consultant Resolution	18-Jan-21	18-Jan-21	0	C1530	72200, 72600																									
72200	722	TYPE 2 CE OEM Initial Review	19-Jan-21	18-Feb-21	0	C1530, C1540	77302																									
72600	726	Type 2 CE Cooperating Agency Initial Review	19-Jan-21	18-Feb-21	18	C1530, C1540	77302																									
77302	773	District Prepares Responses	19-Feb-21	08-Mar-21	0	72200, 72600	77402																									
77402	774	OEM/District Comments Resolution	09-Mar-21	08-Apr-21	0	77302	73300																									
73300	733	Type 2 CE OEM Final Review	09-Apr-21	24-May-21	0	77402	26300, 73600																									
26300	263	Location Design Concept Acceptance	25-May-21	25-May-21	0	73300	73600, 76500																									
73600	736	Location Design Concept Acceptance Public Notice	26-May-21	26-May-21	4	73300, 26300	C1630																									
76500	765	Interchange Access Request Approval	26-May-21	01-Jun-21	0	26300, C2290	C1630																									
C1630		Pass the Torch Meeting	02-Jun-21	02-Jun-21	0	73600, 76500																										

█ Actual Level of Effort █ Remaining Work █ Actual Work █ Critical Remaining Work
◆ Milestone ▶ summary
