

# **District One**

## **Presentation of the Consultant Acquisition Plan for Fiscal Year 2024-2025**

**Work Groups 2.0, 3.1, 3.2, 4.2.3, and 4.4**

**Benjamin Clayton, P.E.**

**District Consultant Project Management Engineer**

**Abra Horne**

**District Environmental Administrator**

## Housekeeping

- Restrooms
- Silence phones
- Questions during the presentation
  - You can type questions that you have during the presentation, and we will do our best to answer them.
  - If you have a project specific question, please include the FPID and project manager's name associated with the project.

## Agenda

- Welcome to District One
  - Procurement Information
  - ISD Staff Introductions and New Project Information
  - District Issues
  - Tips from DEMO
  - PD&E Staff Introductions and New Project Information
  - Consultant Project Management Staff Introductions and New Project Information
-



**Welcome to District One**

**Nicole Mills, PE**

**Director of Transportation Development**



**Jamie Reyes**  
**Professional Services/  
Design Build Supervisor**



## Contact Information

NAME	TITLE	PHONE NUMBER
Elizabeth Ayers	Procurement Services Manager	(863) 519-2901 (O) (863) 512-7032 (C)
Jamie Reyes	Professional Services Supervisor	(863) 519-2301
Jhoanna Garces de Beltre	Contract Analyst III (Design Build)	(863) 519-2279
Savannah Dorminy	Contract Analyst III	(863) 519-2722
Ulises Valles	Contract Analyst III	(863) 519-2467
Rebecca Lycans	Contract Analyst II	(863) 519-2302
Renee Arocho	Contract Analyst II	(863) 519-2440
Harmonee Peterman	Contract Analyst I (CITS Coordinator)	(863)519-2624
Heather Burkmier	Contract Analyst I	(863) 519-2421
Emalee Bell	Contract Analyst I	(863)519-2330
Cabrina Donaldson	Contract Analyst I	(863) 519-2444
Tricia Tucker	In-House Consultant-Professional Services	(863)519-2809

## Upcoming Change to Project Information

### District 1 Consultant Marketing Home

Procurement Services Administrator  
Elizabeth Ayers

Procurement Office:

801 N. Broadway Ave. Bartow, FL 33830  
Tel: (863) 519-2901

The following counties are located in District One: Charlotte, Collier, DeSoto, Glades, Hardee, Hendry, Highlands, Lee, Manatee, Okeechobee, Polk and Sarasota.

[Expand all](#)

D1 Procurement Related Documents

#### Most Requested Items

[Marketing Links](#)

[Consultant Acquisition Plan](#)

[Prequalification](#)

[Advertisements](#)

[Staff Directory](#)

[Regional Meetings](#)

[Additional Design Project Info.](#)

[FTP Directory](#)



[FY24-25](#)

- Beginning FY25, project-related *Professional Services* information will be placed on the District One Marketing Site and **NOT** the FTP (per Central Office direction).

[Professional Services Marketing D1 \(fdot.gov\)](#)



## DBE/SBE Reminders

- DBE Utilization
  - D1 DBE Coordinator, Tricia Tucker
  - DBE goal is 10.65%
  - Report DBE payments in Equal Opportunity Compliance System *timely*
- BDI Contracts
  - Statewide Goal is still 15%
- Questions?
  - DBE Commitments Contact Tricia Tucker (863) 519-2809
  - EOC Website Contact EEO (850) 414-4747



## **SBE/BDI Program**

District One BDI Program Advisor: Jamie Reyes

D1 Small Business Town Hall Date: TBD  
(will be advertised on D1 Marketing Site and  
email invite to SBE Firms)

## D1 ACEC-FL Liaison Committee

- ACEC-FL Liaison Committee
  - District One ACEC-FL Liaison Committee has been meeting quarterly
  - FDOT Members – LK Nandam, John Kubler, Nicole Mills, Kevin Ingle, Jon Sands, Elizabeth Ayers, Ben Clayton
  - Consultant Members – David Coleman, Sean Donahoo, Jason Lyle, Joe Lauk, Randy Prescott
  - Members serve five years, and their firms must be active members of the ACEC-FL Transportation Committee
  - One member rotates off of the committee every year





## Eligibility Requests

- Be proactive-send request as soon as possible to allow time for Department review of information
- Include very detailed information about your role on project
- Letters will get kicked back for more details, which may affect your teaming



- New Conflict of Interest Determination Request Form
- Located on D1 Marketing Site [Professional Services Marketing D1 \(fdot.gov\)](http://Professional Services Marketing D1 (fdot.gov))
- Submit form to [D1.DesignBuild@dot.state.fl.us](mailto:D1.DesignBuild@dot.state.fl.us)

Submit via email to [D1.DesignBuild@dot.state.fl.us](mailto:D1.DesignBuild@dot.state.fl.us)

---

**CONFLICT OF INTEREST (COI)  
DETERMINATION REQUEST**

Date:  Requestor/Contact Person:

Firm:  Office No.:  Mobile No.:

Email:

**Current District One Contract Requiring COI Determination:**

Contract No./Financial ID	Work Type
	2.0 Project Development and Environmental Studies
Role	Project Type
Prime <input type="checkbox"/> Subconsultant <input type="checkbox"/> Staff Positions: <input type="text"/> <input type="text"/> Scope of Work: <input type="text"/> <input type="text"/>	<input type="checkbox"/> Design-Build <input type="checkbox"/> Construction, Engineering and Inspection <input type="checkbox"/> Design <input type="checkbox"/> General Engineering Consultant <input type="checkbox"/> Project Development & Environment <input type="checkbox"/> Other (list project type) <input type="text"/> <input type="text"/>
Fee Received (\$)	% of Total Contract
<input type="text"/>	<input type="text"/>

**Potential Project Pursuit Description:**

Financial Project ID No.(s):  Formal Advertisement Date:

Advertisement No.:

**Potential Pursuit Type (please select one):**

Design-Build     General Engineering Consultant

Design     Project Development & Environment

Construction, Engineering and Inspection     Other (list project type) Type:

**Potential Project Pursuit Role (please select one):**


Prime

Subconsultant

---

- 1 - D112122023

- Letters of Response & Expanded Letters of Response
  - Be sure to use the most current versions. Do not reuse forms!
  - Do not wait to submit your letter (or Technical Proposals)!
  - Do not use abbreviations for sub-consultants unless you've spelled it out somewhere else.
  - Do not recreate any Official DOT Form or add your company logo.

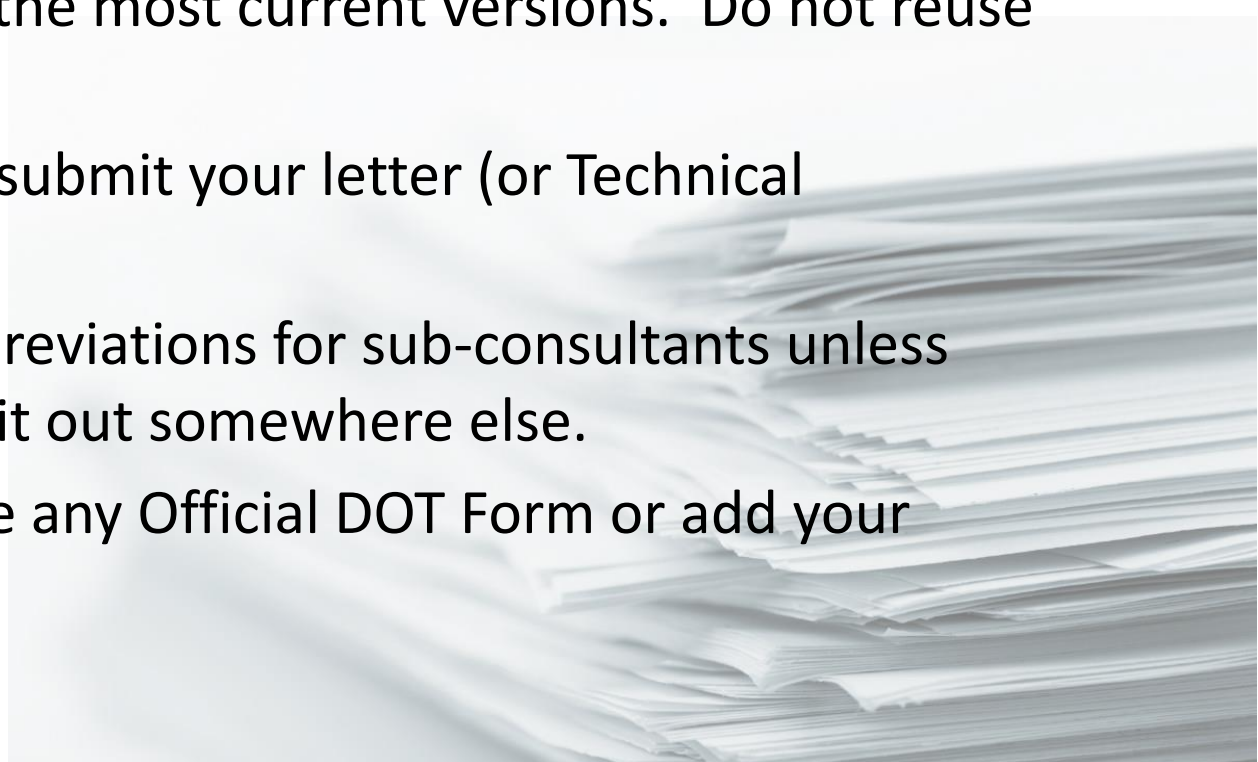



- Presentations
  - What you present must match with Presentation Slides submitted to PSU
  - TRC to grade slides submitted, not presented
  - Cannot include TBD slides or placeholder slides
  - Slides and technical proposals are due at the same time



## Request for Fee Proposal

- Resumes-should include all information necessary to properly classify personnel, including:
  - Education, certifications, applicable licensure (PE License #, state of license and year obtained)
  - Dates/years of experience to support proposed classification



Longer procurement  
schedules, effective  
mid-point FY23-24.  
Target=5 months





- Request for Fee Proposal
  - Due one week after Final Selection
  - Use most current AFP on the internet EVERY TIME.
  - Due dates cannot be extended to allow firms to give raises/allow pay cycles to reflect raises. Payroll must support rates that are in effect the due date of RFFP.
- Resumes
  - Personnel must be classified in HIGHEST classification qualified for
  - Do not recycle incorrect information! Once notified of an error, update resume for future submittals.
- Negotiations
  - Review Negotiations emails carefully to reduce corrective action and avoid invoice delays.

- Not receiving email blasts with important project information?
  - Email addresses are pulled from the qualification packages sent annually to:  
Carliayn Kell, Qualifications Administrator  
FDOT Procurement Office  
850-414-4597  
[Carliayn.kell@dot.state.fl.us](mailto:Carliayn.kell@dot.state.fl.us)





## Consultant Acquisition Plans

- D1 no longer provides CAP to industry
- Firms can run automated CAP:
  - [Consultant Acquisition Plan](#)

---

District Consultant Acquisition Plans

Current Consultant Acquisition Plans

[Professional Services Consultant Acquisition Plans](#)

[Design-Build Acquisition Plan](#)

- Will capture all projects on Planned Ads



**Bessie Reina**

**Intermodal System Development Administrator**

---

## Charlene Ross

- Modal Project Manager
- 8 years with FDOT
  - 4 years ISD Transit, and 1.5 years in current role
- [Charlene.Ross@dot.state.fl.us](mailto:Charlene.Ross@dot.state.fl.us)
- (863) 519-2390




## Ad 24161 – Polk County SunRail Expansion PD&E Study

- FPID: 450899-2
- Project managers:
  - Charlene Ross, FDOT
  - Scott Pringle, WSP (Consultant PM)
- Current ad date: January 26, 2024
- Execution month: June 2024
- TRC members:
  - Abra Horne
  - Libertad Acosta-Anderson, P.E.
  - Charlene Ross



# FPID 450899-2 - Polk County SunRail Expansion PD&E Study

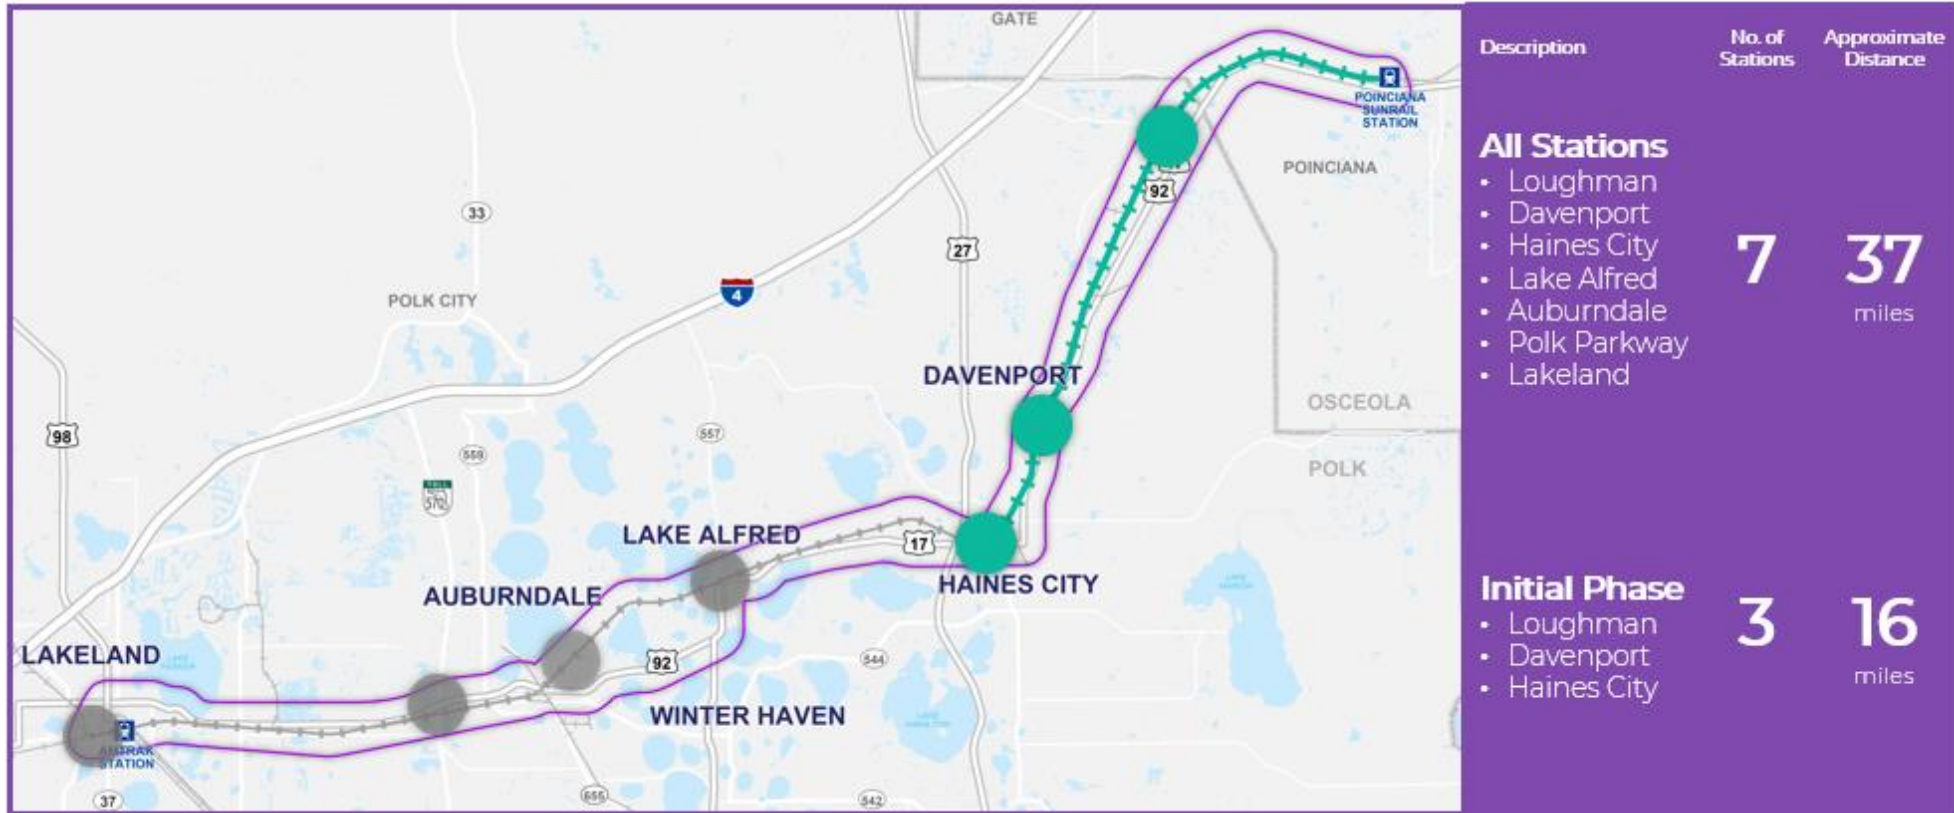





# **Benjamin Clayton, P.E.**

**District Consultant Project Management Engineer**

## District Issues

- Marketing Meetings, Letters of Interest, and Interviews
  - Responsiveness
  - Project Schedules
-

## Marketing Meetings

- Questions/clarification (approx. 15-20 minutes)
  - Encouraged to schedule marketing meetings to discuss project specific questions
    - Link in advertisement for automated scheduling
  - Consultant's time to ask questions
    - TRC will not restate information from recorded webinar
    - TRC will not be responsible for filling the time.
    - Do you have an out of the box idea? Run it by the TRC in the marketing meeting to see their reaction.
  - If you have no questions, there is no need for you to schedule a meeting

## Marketing Meetings

- Pay attention to special notes on advertisements
  - TRC calendars are being held for marketing meetings
  - Link to book time slots is in the advertisement
  - Dates published on planned advertisement under special notes
  - Planned advertisements will state which location the project will be managed from
  - Advertisements will include all projects included in contract for bundles

## Letters of Interest – Design

- Stakeholder contacts
  - No contact prior to or during the Letter of Interest (LOI) preparation
    - This includes, but is not limited to, public agencies, regulatory agencies, schools, churches, utilities (public and private)
  - Goals
    - Reduce efforts/impacts to stakeholders and consultants
    - Eliminate conflicting messages to public/stakeholders
  - Property owners shall NOT be contacted at any time
    - Contact by FDOT only

## Letters of Interest – Design

- Stakeholder contacts
  - Identification of stakeholders is encouraged
  - FDOT Project Manager will state which stakeholders are allowed to be contacted and when, typically after shortlisting
  - It is acceptable to contact FDOT offices prior to advertisement

## Letters of Interest – Design

- Technical Approach
  - LISTEN TO YOUR TRC
    - Between the project specific webinar & marketing meetings, the TRC will be clear in what they are looking for in the letter
  - KNOW THE PROJECT: Identification of project issues is encouraged
    - Review of existing data
    - Field observations
    - Based on personal experience
  - DISTRICT EXPERIENCE NOT A FACTOR
    - Demonstration of applicable project experience is a key criteria, not a firm's experience with the District or FDOT.

## Letters of Interest – Design

- Technical Approach
  - Place emphasis on approach to solving project issues and accomplishing goals
    - Show us your thought process, but remember not to waste space trying to explain every detail
  - Do not repeat the information provided by the TRC. We already know that information, we want to see what you have come up with.



## Interviews – Design

- Answer the Questions
  - Do not try to fit a pre-determined response into interview question responses
  - Pay attention to the questions being asked and provide a complete answer
  - Questions are intended to challenge

## **Debrief, debrief, debrief**

- The Department is willing to set time aside to debrief the consultants on Letters of Interest, Interviews or Presentations
- The TRC may begin meeting with consultants 72 hours after final selection
- Do not delay setting up a debrief meeting

## Responsiveness

- Responsiveness to Department questions is critical!
- Pay attention to scheduled due dates, especially Specifications and Mailing – **BE AVAILABLE for plans / specs changes during this time.**
  - This includes subconsultants
- Request for information (RFI) response delays can affect construction activities – delays in a response can result in errors and omissions (E&O) if time is an issue

## Project Schedules

- No scheduled lettings in 4th quarter
- Schedule definition meeting at NTP
- Ensure commitments are achievable
- Do not assume the letting date will move out
- Do not assume Department review times or activity times will be reduced
- Keep the PM involved – especially when tasks are delayed
- Pavement cores need 90-day turnaround
- **Positive float belongs to the department**

# Abra Horne

**District Environmental Administrator**



## Tips from DEMO



- **Our goals**
  - Keep ***community at the center*** of what we do
    - Communicate often and clearly – ***What is our story?***
    - The development of successful solutions is **collaborative**
  - Evaluate **new ideas** – safety, technology, resiliency, and supply chain
    - **How have we done better?**
  - Prepare **high-quality** environmental documents
    - **Use the OEM checklists** + comply with PD&E Manual, OEM, NEPA, and FDM

## Tips from DEMO



- **Preparing for pursuits**

- Check [www.fdot.gov/procurement](http://www.fdot.gov/procurement) - *things change!*

- **Listen to the TRC**

- *Ask the TRC meaningful questions to understand more about the project*

- **Ask FDOT first before you contact project stakeholders**

- Local agencies, property owners, and other partners

- The choice is yours for the **organization chart**

## Tips from DEMO



- PD&E **schedules are important** – 18 to 24 months
  - Keep a **production** mindset and be proactive
  - Identify completion dates that will impact future phases
- PD&E Progress Meetings
  - Meet **every** month
  - **Proactive agendas a week before** – action items, meetings, and next steps
  - Identify **key discussion** topics and FDOT staff who need to be there
  - Discuss **opportunities to advance** the schedule
  - *Report out on **your risk registers** and mitigation strategies*



## Tips from DEMO

*Best marketing tool is quality work*

- **Conducting projects**

- **Change is constant**

- Stay familiar with the **latest** regulations/guidance

- Comment resolution

- **Clean and track changes** versions with written responses for *all comments*

- Coordinate methodologies and scopes **before you do the work**

- Stakeholder communication needs to be led by FDOT staff

## Tips from DEMO

- **Progress meetings**
  - **Balance all considerations and discuss at progress meetings**
    - Engineering, right-of-way
    - Minimization and avoidance of impacts
    - Public input, neighborhood cohesion, and community character
  - Discuss analysis and **planned submittal dates**
    - *We will **plan ahead** to avoid overwhelming reviewers*
  - **Invite** environmental and subject matter experts (**ours and yours**)




## Tips from DEMO

- **Compliance**

- Review the **OEM website regularly**
  - Updates to the PD&E Manual
  - Environmental permitting requirements
  - Procedures and templates
- SWEPT updates occur regularly
  - **Coordinate PM/EPM**
- Species requirements **change over time.**
  - **Meet with DEMO** prior to species work for the latest guidance and methodology



# District One Environmental Management Office (PD&E)

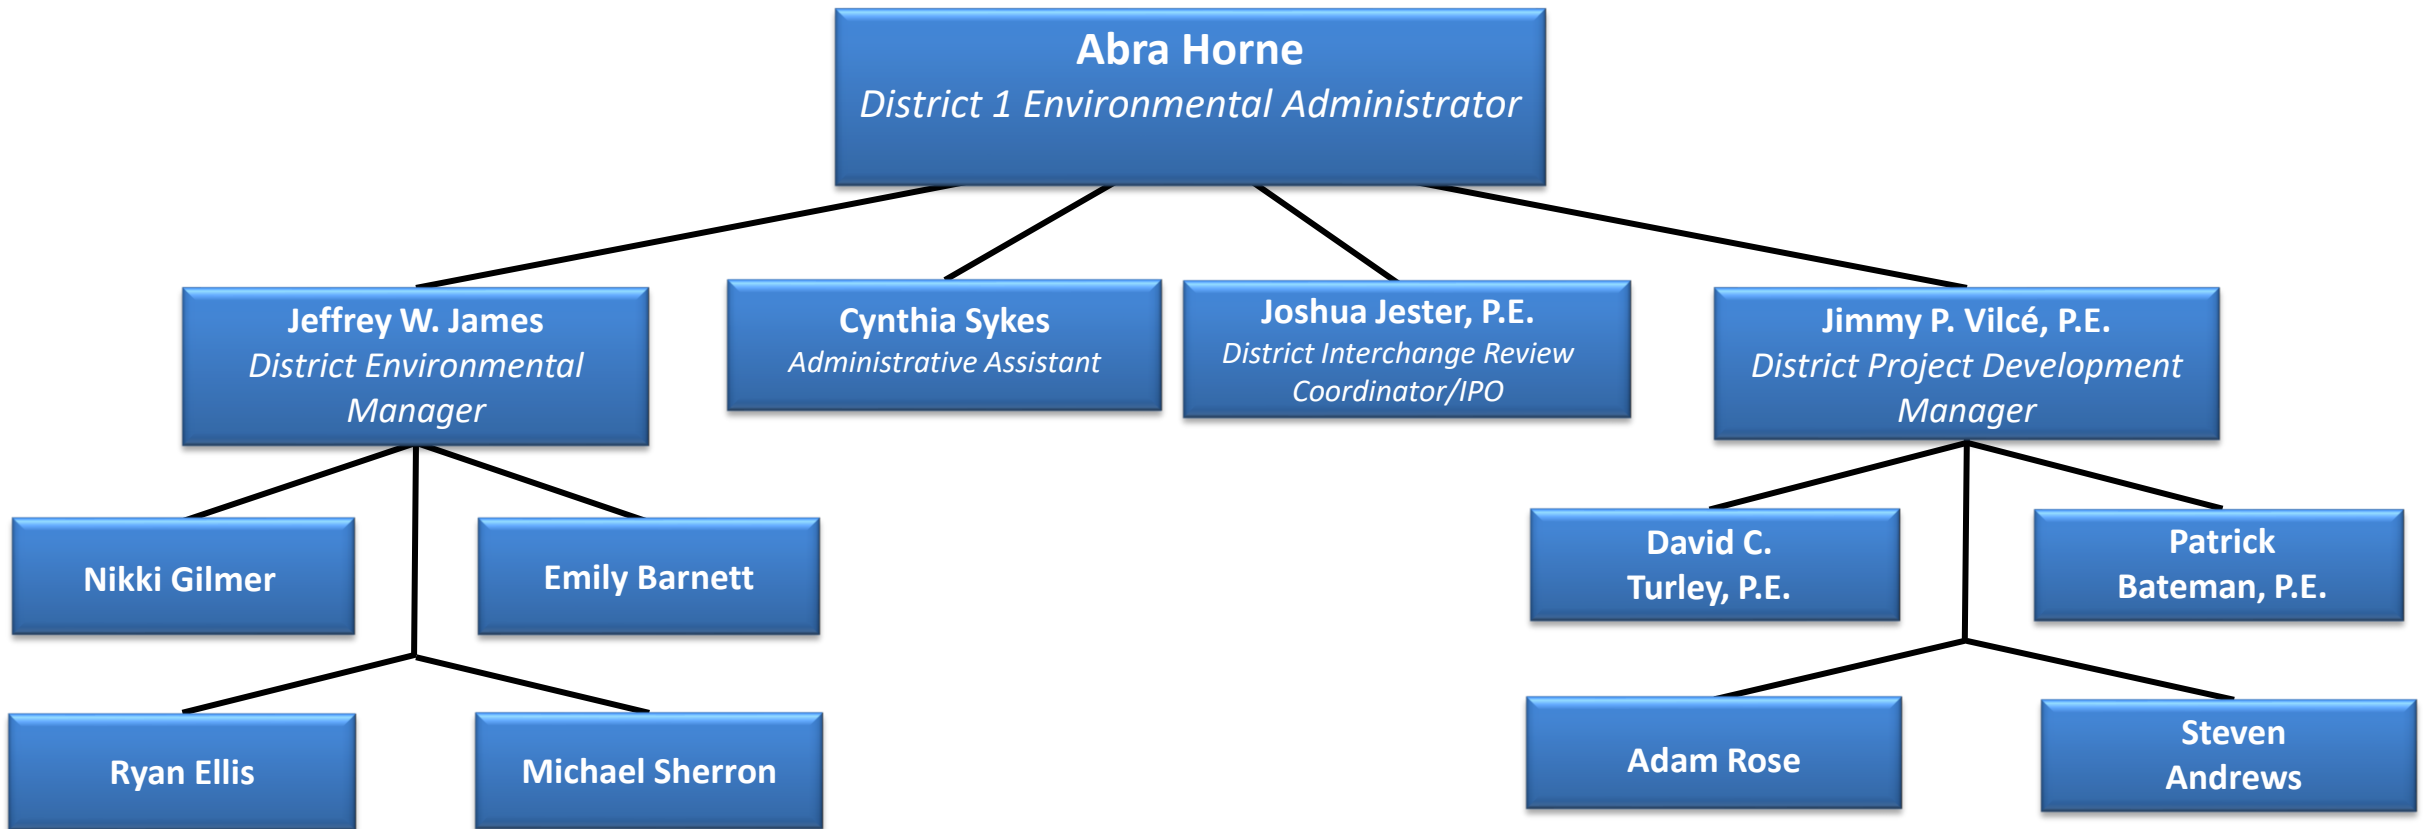


## Abra Horne

- District Environmental Administrator
- 25+ years experience
- NEPA, PD&E, multimodal, and MPO
- [Abra.Horne@dot.state.fl.us](mailto:Abra.Horne@dot.state.fl.us)
- 863-519-2239
- Preferences – responsiveness, transparency, proactive consulting, and quality work



## Jeffrey W. James

- District Environmental Manager
- 17 years with FDOT
- 27 years of professional experience in the environmental field
- Jeffrey.James@dot.state.fl.us
- 863-519-2625
- Preferences – following instructions & the PD&E Manual, error free documents, and meeting all expectations - especially deadlines

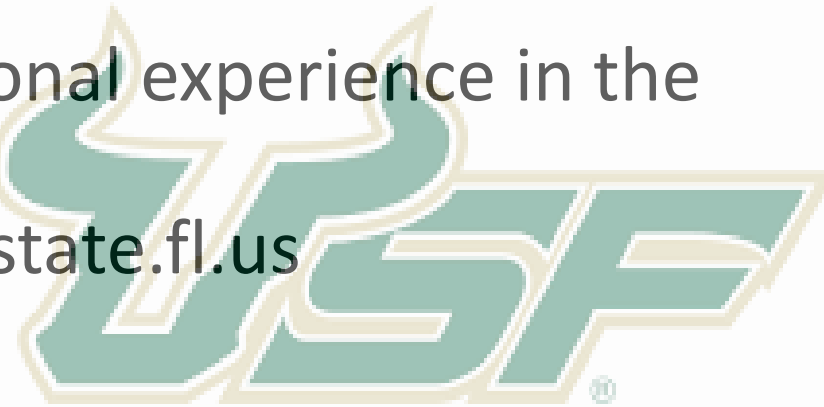

## Nikki Gilmer

- Environmental Project Manager
- ETDM Coordinator
- 1.5 years with FDOT
- 3 years as a Site Manager with FDEP's Petroleum Restoration Program
- [Nikki.Gilmer@dot.state.fl.us](mailto:Nikki.Gilmer@dot.state.fl.us)
- 863-519-2375
- Preferences – timeliness, communication when issues arise, and professional grade documents



## Emily Barnett

- Environmental Project Manager
- 10 months with FDOT
- 5 years of environmental experience in the public and private sector
- [Emily.Barnett@dot.state.fl.us](mailto:Emily.Barnett@dot.state.fl.us)
- 863-519-2805
- Preferences – quality documents, communication, and timeliness





## Ryan Ellis

- Environmental Project Manager
- Environmental Scientist with 4 years of experience at SWFWMD and a non-profit.
- 3 months with FDOT
- [Ryan.Ellis@dot.state.fl.us](mailto:Ryan.Ellis@dot.state.fl.us)
- 863-519-2505
- Preferences – responsive, timely, follows PD&E guidance, and thoroughness.




## Michael Sherron

- District Contamination Impact Coordinator
- 2 months with FDOT
- 1.5 years as an Environmental Project Manager in the private sector
- Michael.Sherron@dot.state.fl.us
- 863-519-2495
- Preferences – punctuality and efficient communication



## Cynthia Sykes

- Administrative Assistant
- 33 years with FDOT
- Title VI Coordinator for District One
- [Cynthia.Sykes@dot.state.fl.us](mailto:Cynthia.Sykes@dot.state.fl.us)
- 863-519-2287

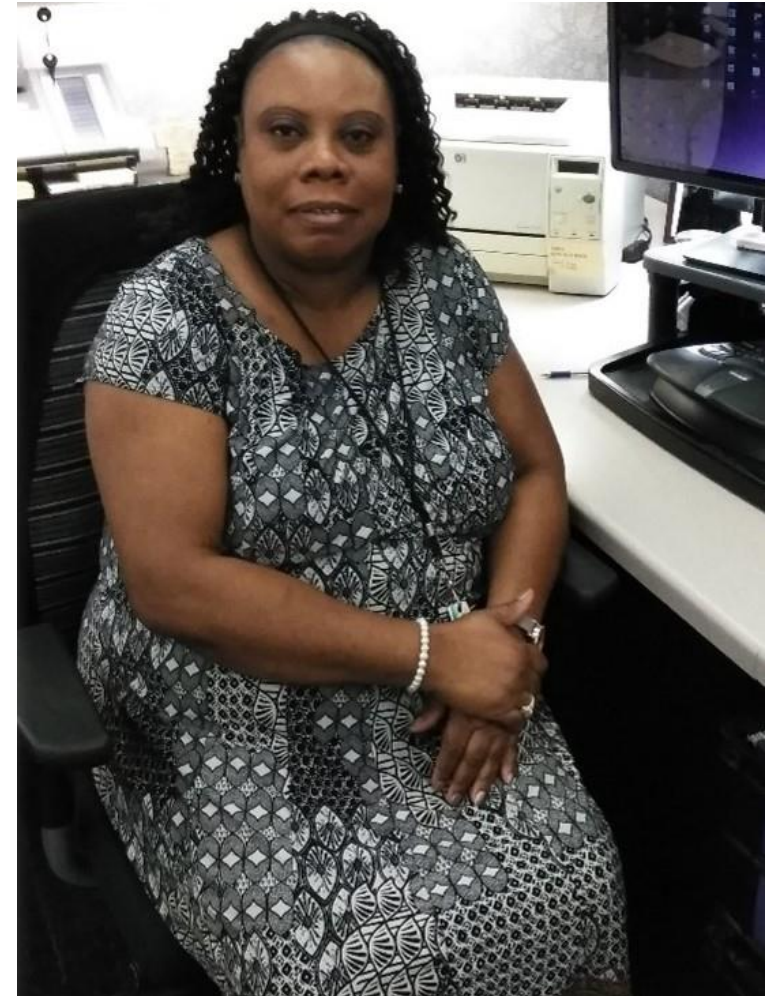

## Joshua Jester, P.E.

- Interstate Project Manager
- 6 years with FDOT
- [Joshua.Jester@dot.state.fl.us](mailto:Joshua.Jester@dot.state.fl.us)
- 863-519-2251
- Preferences – responsive and “to the point”



## Jimmy P. Vilcé, P.E.

- Project Development Manager
- 8.5 years with FDOT
- [Jimmy.Vilce@dot.state.fl.us](mailto:Jimmy.Vilce@dot.state.fl.us)
- 863-519-2293
- Preferences – proactive, frequent communication, responsive, tactful



## David C. Turley, P.E., CPM

- Project Development Engineer II
- 10 years with FDOT
- 13 years of prior engineering experience
- David.Turley@dot.state.fl.us
- 863-519-2255
- Preferences – have solutions when noting problems, being creative, and being proactive



## Patrick Bateman, P.E.

- Project Manager
- 9 years with FDOT
- Patrick.Bateman@dot.state.fl.us
- 863-519-2792
- Preferences – inform FDOT of problems as soon as they are known



## Adam Rose

- Project Manager
- 4 years with FDOT
- Adam.Rose@dot.state.fl.us
- 863-519-2832
- Preferences – timeliness, early and frequent communication, innovative approaching





## Steven A. Andrews

- Project Manager
- 25 years with FDOT
- 10 years with PD&E
- Steven.Andrews@dot.state.fl.us
- 863-519-2270
- Preferences – focus on the major issues, cover all phases of PD&E, and stay within the budget




## FPID 442404 SR 600 (US 17/92) DOWNTOWN LAKE ALFRED ONE-WAY PAIR

- Project Manager: Steven Andrews
- Current AD date: May 2024 (Tentative)
- Execution month: October 2024
- TRC members:
  - Steven Andrews
  - David C. Turley, P.E.
  - Jimmy Vilcé, P.E.



## FPID 442404 SR 600 (US 17/92) DOWNTOWN LAKE ALFRED ONE-WAY PAIR

- Project manager: Steven Andrews
- 2.35 miles
- PD&E budget: \$1.7 M
- Design budget: \$9 M
- Construction budget: \$75 M

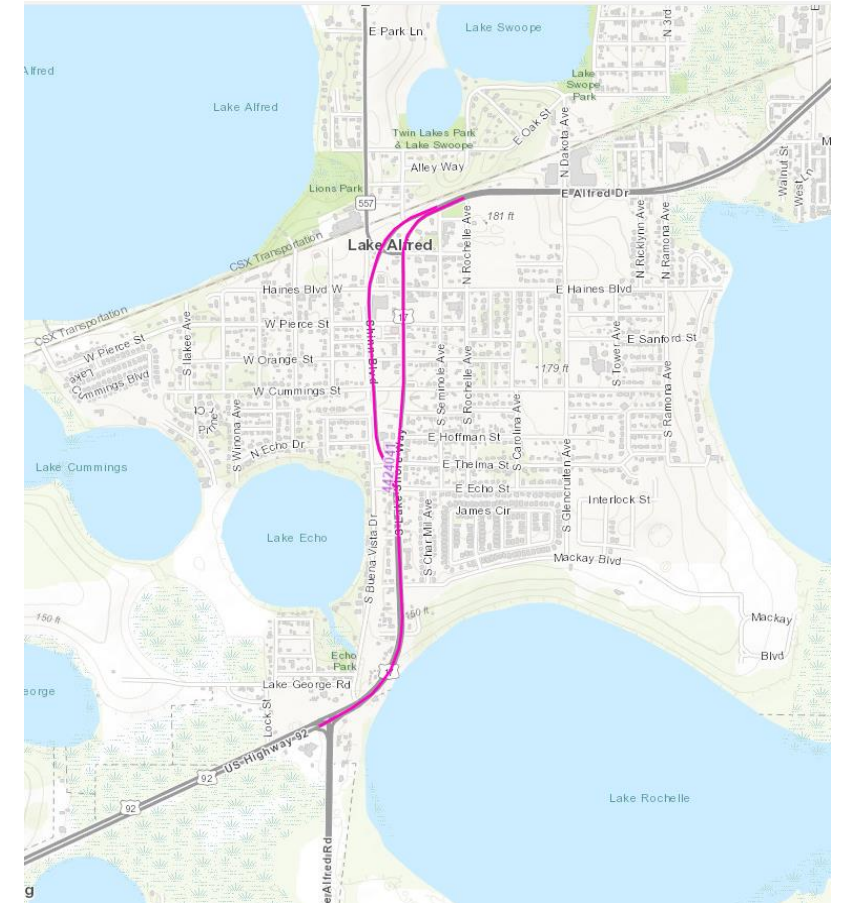

## FPID 442404 SR 600 (US 17/92) DOWNTOWN LAKE ALFRED ONE-WAY PAIR

- Scope will include
  - Conversion to two-way operations
  - Contamination
  - Cultural resources
  - Signalization
  - Floodplains
  - Section 4(f)
- Issues and concerns
  - Community outreach
  - Multimodal facilities
  - Utility coordination
  - Pedestrian safety
  - Business access

## Ad 25108 – US 98 (SR 700) bridge over Kissimmee River PD&E and Design

- FPID:
  - 445408-1
  - 445408-2
- Project manager: Patrick Bateman
- Current ad date: April 22, 2024
- Execution month: September 2024



## FPID 445408 US 98 (SR 700) bridge over Kissimmee River PD&E and Design

- Project manager: Patrick Bateman
- 0.18 miles
- PD&E budget: \$700,000
- Design budget: \$1,600,000
- Construction budget: \$14.5 million
  - FY 27



## FPID 445408 US 98 (SR 700) bridge over Kissimmee River PD&E and Design

- Scope will include
  - Assess bridge for replacement
  - Geotech
  - Survey
  - Utility coordination
  - SUE
- Issues and concerns
  - Removable span
  - FP&L
  - Kissimmee River Restoration Project
  - Fort Basinger

## AD- 25126 FPID 452680-1 SR 78 from W of US 41 to Veterans Parkway


- Project manager: David C. Turley, P.E.
- Current ad date: February 16, 2024
- Execution month: July 2024
- TRC members:
  - David C. Turley, P.E.
  - Steven Andrews
  - Ryan Ellis





## FPID 452680-1 SR 78 from W of US 41 to Veterans Parkway

- Lee County
- Intersecting facilities
  - North-south
    - Veterans Parkway
    - Chiquita Blvd
    - Santa Barbara Blvd
    - Del Prado Blvd
- Budget: \$2.3 million\*

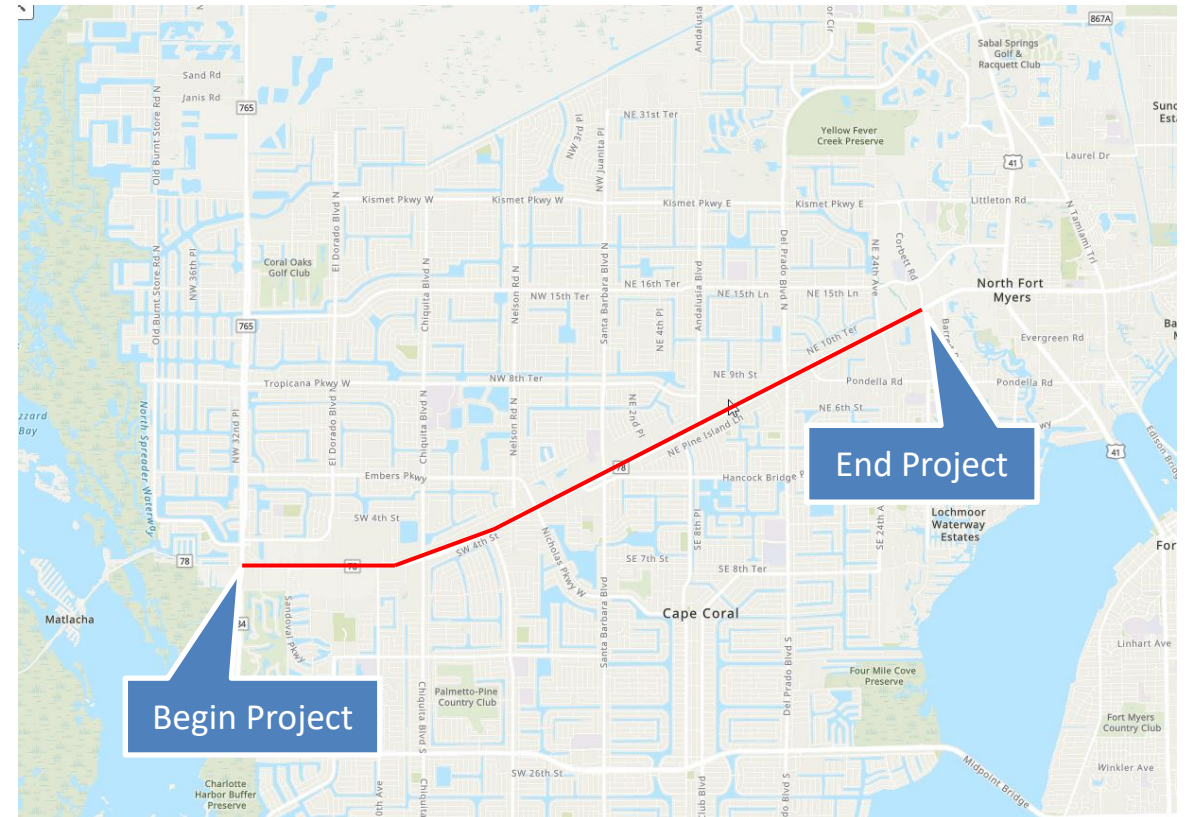

## **FPID 452680-1 SR 78 from W of US 41 to Veterans Parkway**

- Scope will include
  - Traffic operation enhancement
  - Capacity improvement
  - Community outreach
  - ICE analysis (+/- 10 intersections)
  - Structures\*
- Issues and concerns
  - Safety
  - Community
  - Capacity
  - Cultural resources


## Ad 25109 – Lost Bridge Trail at Circle Bar B Ranch to Acorn Loop Trail

- FPID: 448434-1
- Project manager: Adam Rose
- Current ad date: September 13, 2024
- Execution month: February 2025
- TRC members:
  - Adam Rose
  - Patrick Bateman, P.E.
  - Ryan Ellis



## Ad 25109 – Lost Bridge Trail at Circle Bar B Ranch to Acorn Loop Trail

- Polk County (MPO Priority)
  - SFWMD
- Off System
  - Connect Lost Bridge Trail to Acorn Loop Trail
- Budget: \$800,000
  - MPO Funds

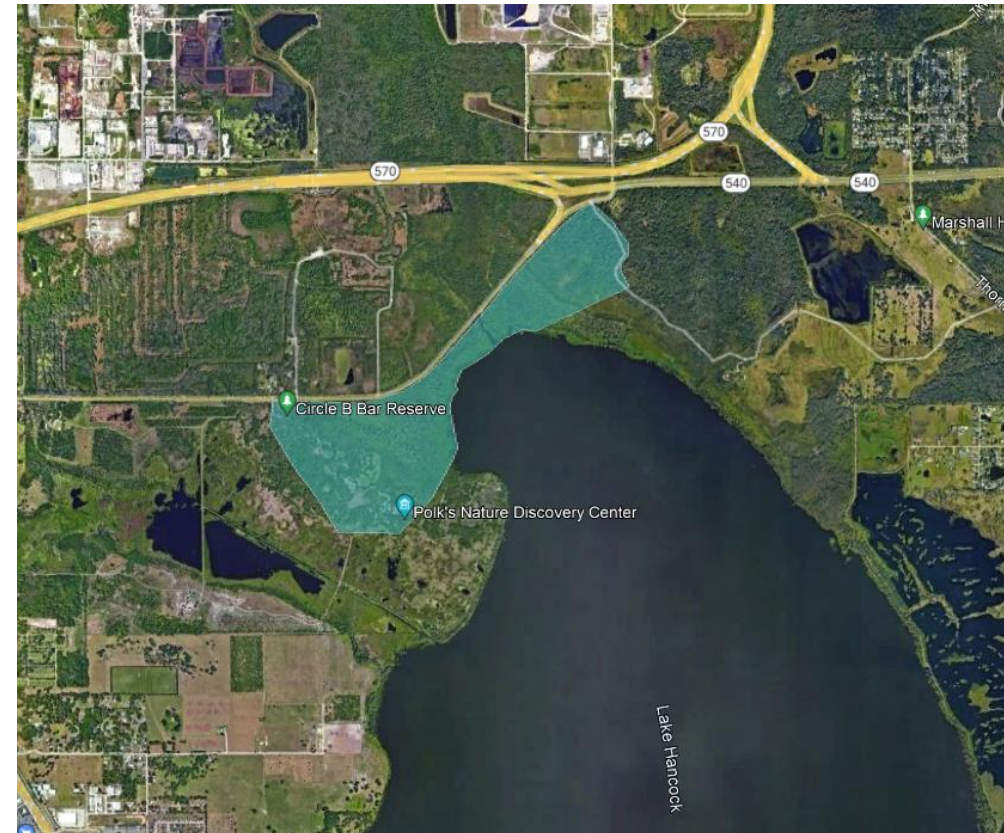

## **Ad 25109 – Lost Bridge Trail at Circle Bar B Ranch to Acorn Loop Trail**

- Scope will include
  - Feasibility study
  - PD&E study (If Needed)
- Issues and concerns
  - Wetland locations
  - Safety






# **Benjamin Clayton, P.E.**

**District Consultant Project Management Engineer**


# District One Project Management Staff

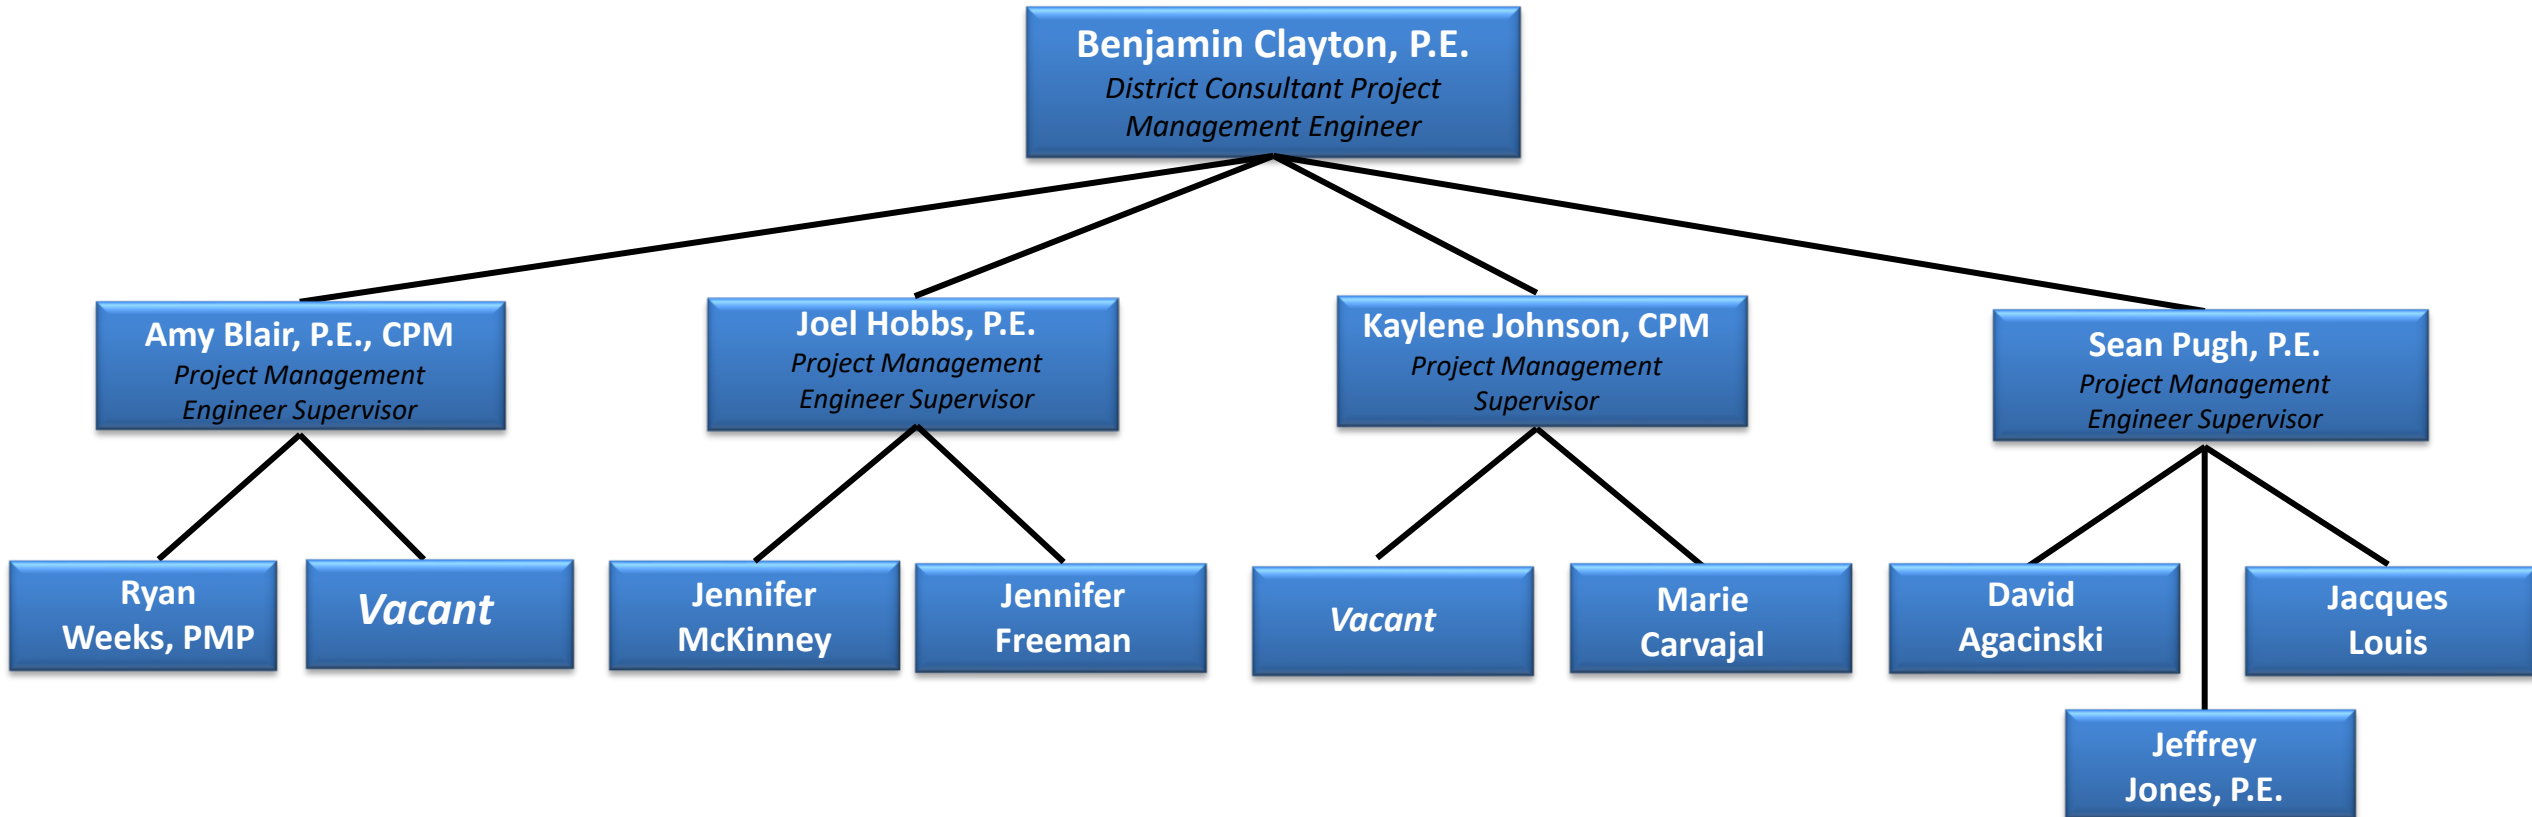



## Benjamin Clayton, P.E.

- District Consultant Project Management Engineer
- 10 years with FDOT
  - 4 years P.E. Trainee, 1 year in Drainage, 5 years in Project Management with 2.5 years in current role
- Benjamin.Clayton@dot.state.fl.us
- 863-519-2480

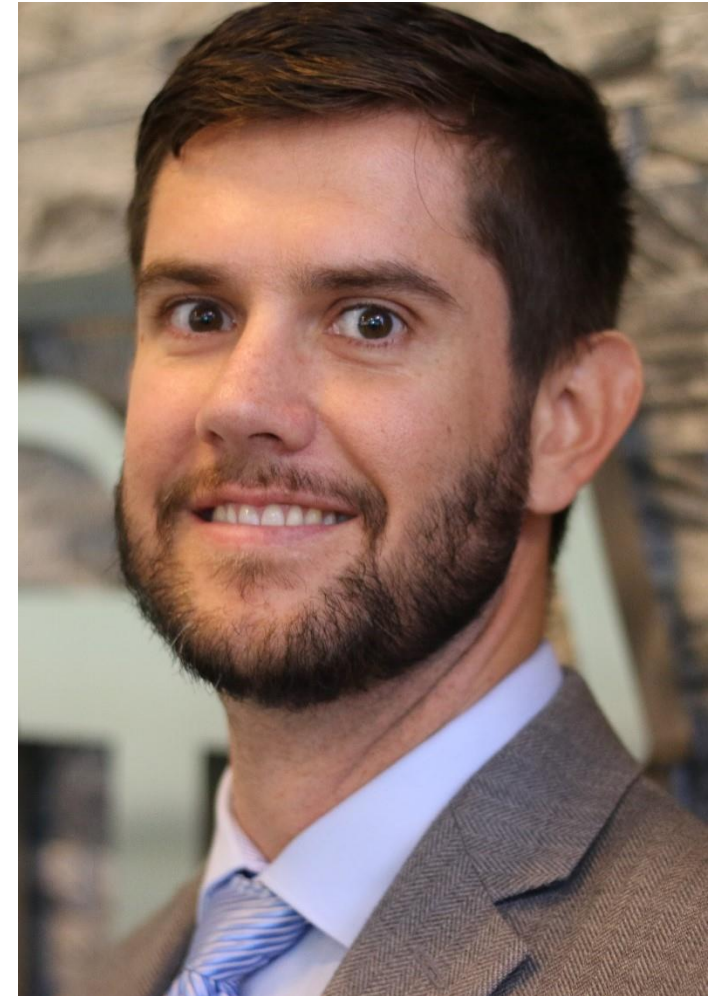


## Amy Blair, P.E., CPM

- Project Management Engineer Supervisor
- Hired through the P.E. Training Program
- Amy.Blair@dot.state.fl.us
- 863-519-2272
- I value responsiveness and open communication.



## Ryan Weeks, PMP

- Project Manager
- 16.5 years FDOT
- [Ryan.Weeks@dot.state.fl.us](mailto:Ryan.Weeks@dot.state.fl.us)
- 863-519-2837
- I value consultants who follow through on their commitments.

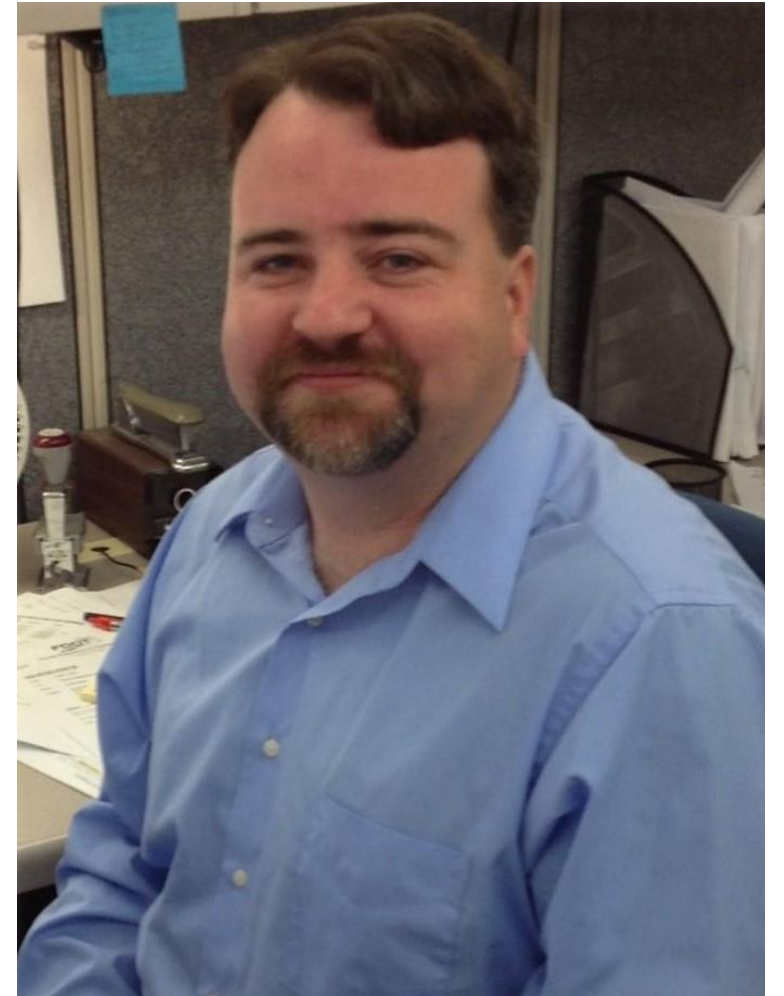

## Joel Hobbs, PE

- Project Management Engineer  
Supervisor III
- 11 years with FDOT
  - 2 years P.E. Trainee, 2 years in  
Construction, 6 years in Maintenance,  
1 year in Roadway Design, started Jan  
2024 in Project Management
- Joel.Hobbs@dot.state.fl.us
- 863-519-2376



## Jennifer McKinney, PMP

- Project Manager
- 8½ years of FDOT Experience
  - Project Management
  - LAP Design Project Management
  - Procurement Experience
- [Jennifer.McKinney@dot.state.fl.us](mailto:Jennifer.McKinney@dot.state.fl.us)
- 863-519-2482



## Kaylene Johnson, CPM

- Project Management Supervisor
- 15 years experience with FDOT
  - 2 years in Accounts Receivable, 6 years in Work Program & 7 years in Project Management
- [Kaylene.Johnson@dot.state.fl.us](mailto:Kaylene.Johnson@dot.state.fl.us)
- 863-519-2396
- I value open communication and following through on commitments.



## Jennifer Freeman

- Project Manager
- 10 years with FDOT
  - 2 years Project Management
  - 4 years District Materials
  - 4 years Financial Services
- [Jennifer.Freeman@dot.state.fl.us](mailto:Jennifer.Freeman@dot.state.fl.us)
- 863-519-2543
- I value proactive project managers who communicate possible issues early and stay on schedule.



## Marie Carvajal


- Project Manager
- 2 year FDOT as a Project Manager
- 3 years FDOT as a Contract Writer
- Marie.Carvajal@dot.state.fl.us
- 863-519-2669
- I value honest and open and communication in a good consultant.





## Sean Pugh, P.E.

- Project Management Engineer, Supervisor III
  - Located in the Southwest Area Office, Fort Myers, FL
- 5.5 years with FDOT
- 7 years with IDOT
  - 5 years in Construction
  - Materials and Design
- Sean.Pugh@dot.state.fl.us
- 239-470-9959
- I appreciate when my consultant partners are proactive and keep the Project Managers up to date with any active issues on their projects.

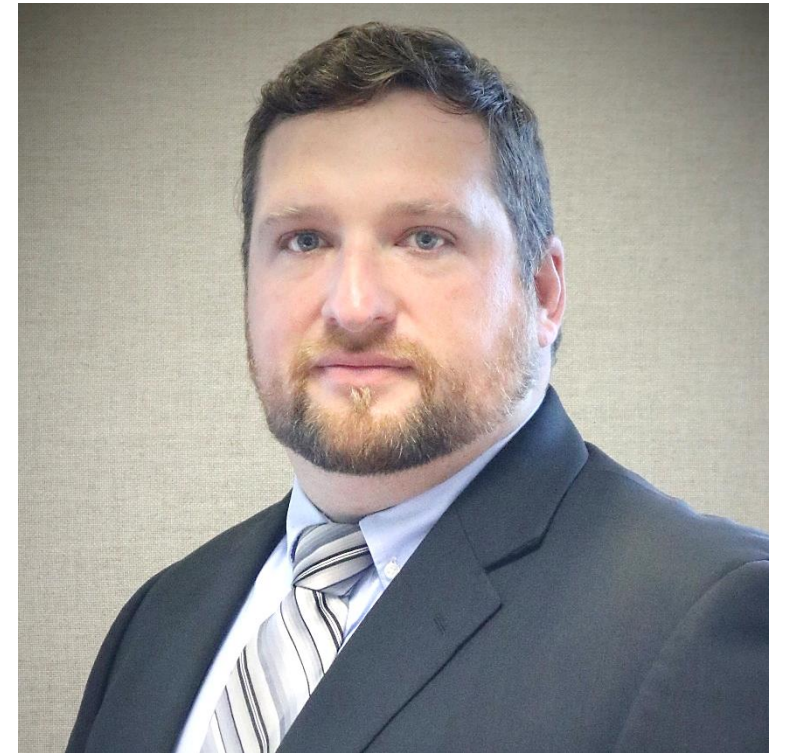


## David Agacinski

- Project Manager
  - Located in the Southwest Area Office, Fort Myers, FL
- 7.5 years with FDOT, 4.5 years with Project Management
- 30 years prior experience as a registered engineer in Wayne County, Michigan
- David.Agacinski@dot.state.fl.us
- 239-225-1924
- I value a proactive project manager.



## Jeffrey M. Jones, P.E.

- Project Management Engineer
  - Located in the Southwest Area Office, Fort Myers, FL
- 1.5 Year experience with FDOT in Project Management
- 15 years experience with the Washington State DOT in Construction, Maintenance & Design
- JeffreyM.Jones@dot.state.fl.us
- 239-225-1920
- I value when consultants alerts me of issues in a timely manner and has a solution ready.

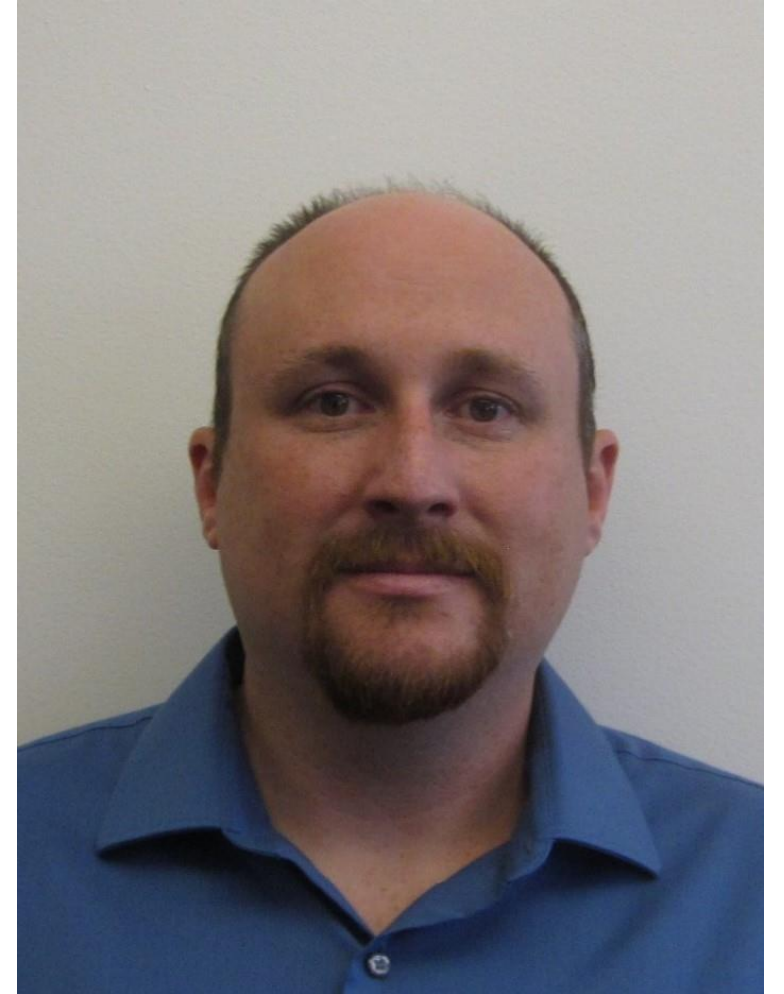

## Jacques Louis

- Project Manager
  - Located in the Southwest Area Office, Fort Myers, FL
- 4 months with FDOT as a project manager
- 10 years of hospitality management experience.
- Jacques.louis@dot.state.fl.us
- 239-225-1914
- I appreciate consultants who provide solutions to presented problems, maintain open communication and adhere to project schedules.



## Design Advertisements

- **David Agacinski**
  - 25113- BDI- SR 45 from N of Pondella Rd to N of SR 78
  - 25114- SR 29 from SR 78 to CR 74
- **Amy Blair**
  - Resurfacing Continuing Services- 2 contracts
- **Marie Carvajal**
  - 25111- BDI- SR 45 from N of Magellan Dr to N of 63<sup>rd</sup> Ave W
- **Jeffrey Jones**
  - 24164- CR 769 (Kings Hwy) from Charlotte County Line to Peace River St
  - 25121-Bundle
    - I-75 from N of Alico Rd to S of Daniels Pkwy
    - I-75 from S of SR 82 to S of Lockett Rd
- **Jennifer Freeman**
  - 25124 – SR 25 from Highlands County Line to N of SR 700
- **Jacques Louis**
  - 25112- BDI Bundle
    - Via Coconut Point Roundabout from Coconut Rd to Corkscrew Rd
    - Coconut Rd Sidewalk form Oakwild to VIA Coconut Point
- **Jennifer McKinney**
  - 25119 – SR 540 from Jim Keene Blvd to King Rd
  - 25120 – Bundle
    - I-75 from N of US 301 to N of I-275
    - I-275 from N of US 19 to N of Toll Plaza
    - I-275 from S of US 19 to N of US 190
- **Ryan Weeks**
  - 25122- SR 25 from N of Ponce de Leon Blvd to N of Lake Isis Ave

## 25113- SR 45/US 41 in Lee County resurfacing **\*BDI\***

- FPID:
  - 450726-1
- Procurement project manager:  
David Agacinski
- Current ad date: February 23, 2024
- Execution month: July 2024



**FPID 450726-1 SR 45 (US 41) from N of Pondella Rd to N of SR 78**

**\*BDI\***

- Design project manager: David Agacinski
- 1.124 miles
- Design budget: \$1.18 million
- Construction budget: \$4.7 million
  - FY 28



**FPID 450726-1 SR 45 (US 41) from N of Pondella Rd to N of SR 78**


**\*BDI\***

- Scope will include
  - Milling and resurfacing
  - Add Paved Inside Shoulder
  - Keyholes
  - Median modifications (Safety)
  - Lighting (Safety)
  - Signal upgrades (Safety)
- Issues and concerns
  - High Crash List
  - Cross Slope and Superelevation analysis




## 25114- SR 29 in Glades County - 2 New Bridges & Roadway

- FPID:
  - 449149-1
- Procurement project manager:  
David Agacinski
- Current ad date: May 24, 2024
- Execution month: October 2024

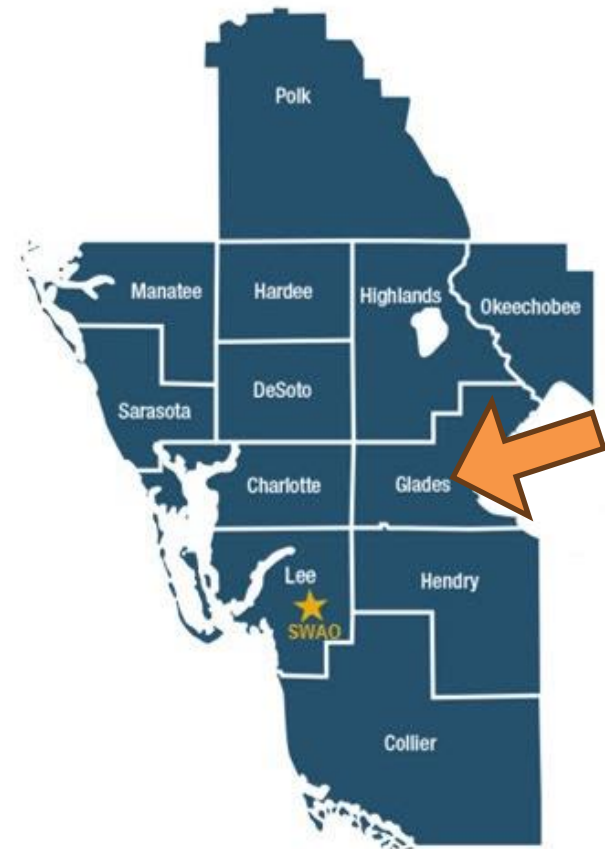

## FPID 449149-1 SR 29 from SR 78 to CR 74

- Design project manager: David Agacinski
- 7.542 miles
- Design budget: \$2.7 million
- Construction budget: \$23.2 million
  - FY 28

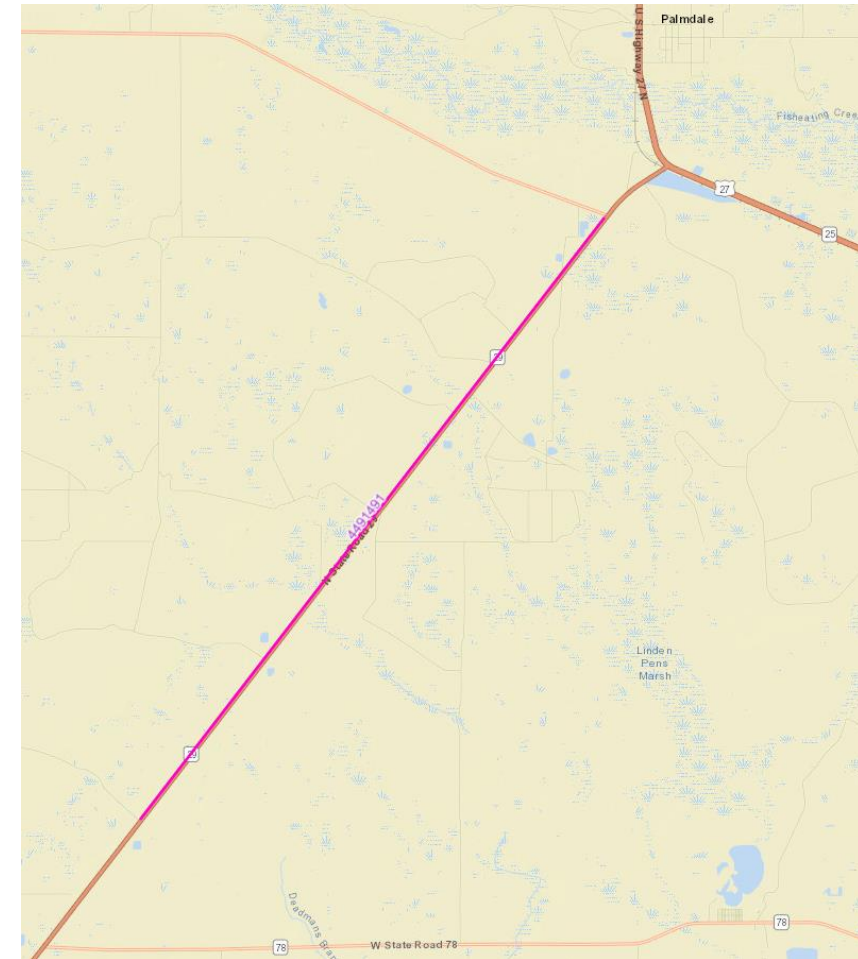


## **FPID 449149-1 SR 29 from SR 78 to CR 74**

- Scope will include
  - Replace 2 bridges & lengthen to accommodate wildlife shelves
  - Raise/Reconstruct Road 2.13 miles between bridges
  - Milling and Resurfacing outside Bridge limits
  - Drainage, Fencing, Lighting
- Issues and concerns
  - Corridor has Flooding History
  - Prevent wildlife crashes

## 25111- SR 45 (US 41) Resurfacing- Manatee County **\*BDI\***


- FPID:
  - 451026-1
- Procurement project manager:  
Marie Carvajal
- Current ad date: June 21, 2024
- Execution month: November 2024

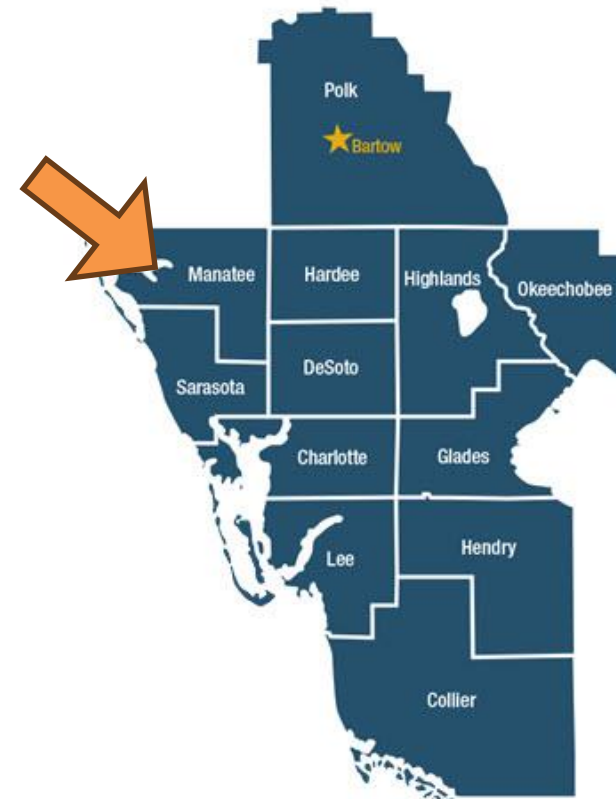

**FPID 451026-1 / Manatee County/ SR 45 (US 41) FROM N OF  
MAGELLAN DR TO N OF 63RD AVE W**

**\*BDI\***

- Design project manager: Marie Carvajal
  - 0.922 miles
  - Design budget: \$916,164
  - Construction budget: \$4.8 million
- FY 27

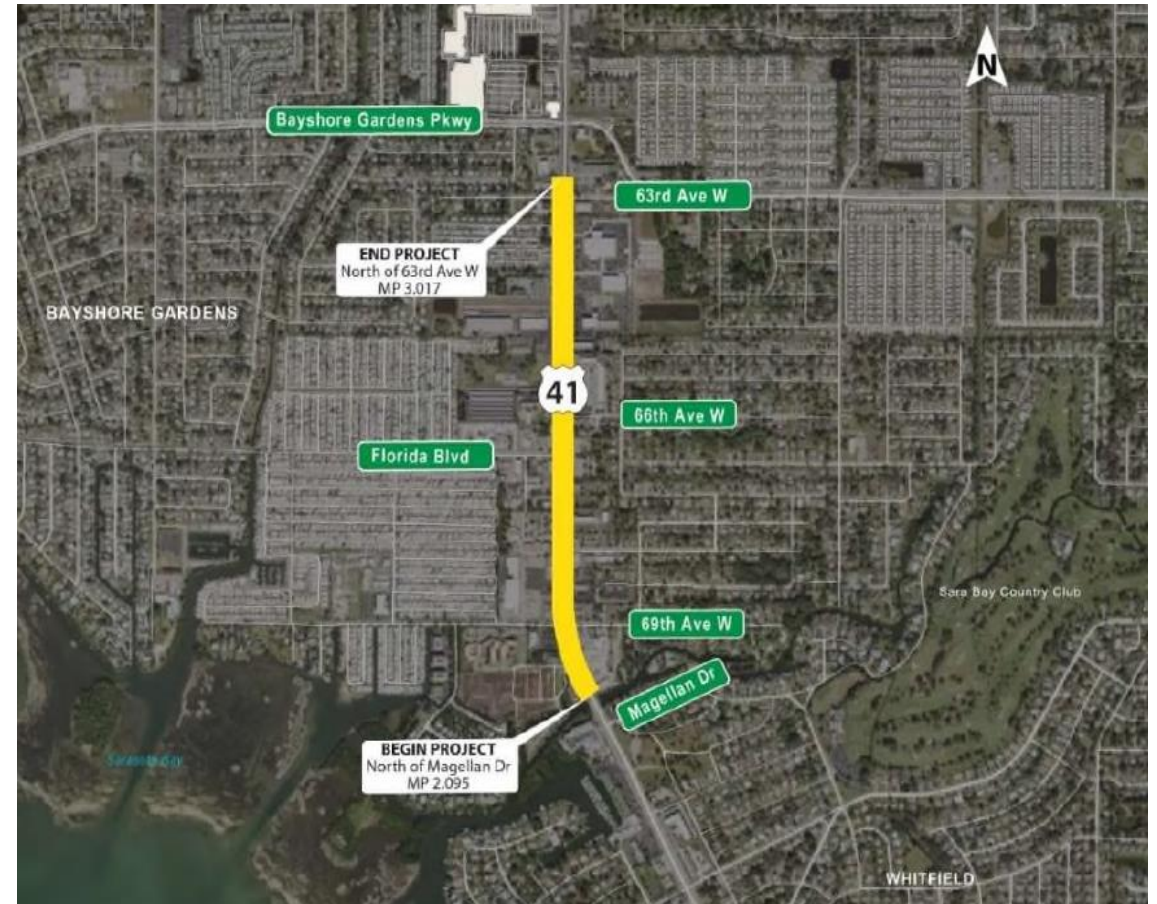

**FPID 451026-1 / Manatee County/ SR 45 (US 41) FROM N  
OF MAGELLAN DR TO N OF 63RD AVE W**

**\*BDI\***

- Scope will include
  - Milling and resurfacing
  - Signing and pavement marking
  - Signalization
  - Drainage
- Issues and concerns
  - Safety
  - Maintenance of traffic
  - Utility
  - High Crash List

## Ad 24164- Widening and Realignment CR 769 (Kings Hwy)

### FY24 ADDITIONAL PROJECT

- FPID: 440342-1
- Procurement project manager:  
Jeffrey Jones, P.E.
- Current ad date: March 15<sup>th</sup>, 2024
- Execution month: June 2024



## 440342-1– CR 769 (KINGS HWY) FROM CHARLOTTE COUNTY LINE TO PEACE RIVER ST

- Design project manager: Doug Burkhart
- 2.218 miles
- Design budget: \$4.1 million
- Construction budget: \$17.4 million
  - FY 27
  - Construction funded under FPID 440342-2
  - Only the first mile is funded for construction
  - R/W is not funded for the northern segment



PD&E Project Map



**440342-1– CR 769 (KINGS HWY) FROM CHARLOTTE COUNTY LINE TO PEACE RIVER ST**

- Scope will include
  - 3D Survey
  - Widening and Realignment
  - Signing and pavement marking
  - Miscellaneous work to be performed
- Issues and concerns
  - Maintenance of traffic
  - Community impact
  - Utilities
  - Right of Way
  - Local Coordination
  - Scope Creep


## Ad 25121- I-75 Resurfacing Bundle- Lee County

- FPID:
  - 452793-1-32-01
  - 453559-1-32-01
- Procurement project manager:  
Jeffrey Jones, P.E.
- Current ad date: March 29, 2024
- Execution month: August 2024



## FPID 452793-1 I-75 from N of Alico Rd to S of Daniels Pkwy

- Design project manager: Ryan Patterson
- 2.218 miles
- Design budget: \$1.5 million
- Construction budget: \$11.11 million
  - FY 26

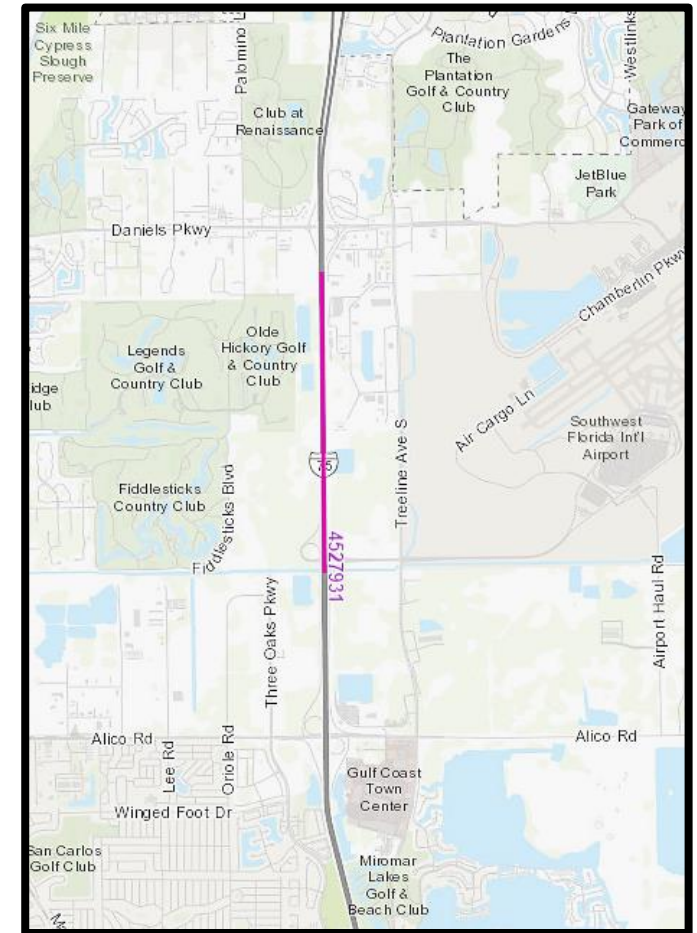


## **FPID 452793-1 I-75 from N of Alico Rd to S of Daniels Pkwy**

- Scope will include
  - 3D Survey
  - Resurfacing
  - Signing and pavement marking
  - Miscellaneous work to be performed
- Issues and concerns
  - Maintenance of traffic
  - Community impact
  - Possible utilities

## FPID 453559-1 I-75 from S of SR 82 to S of Lockett Rd

- Design project manager: Ryan Patterson
- 1.439 miles
- Design budget: \$1.35 million
- Construction budget: \$5.49 million
  - FY 26

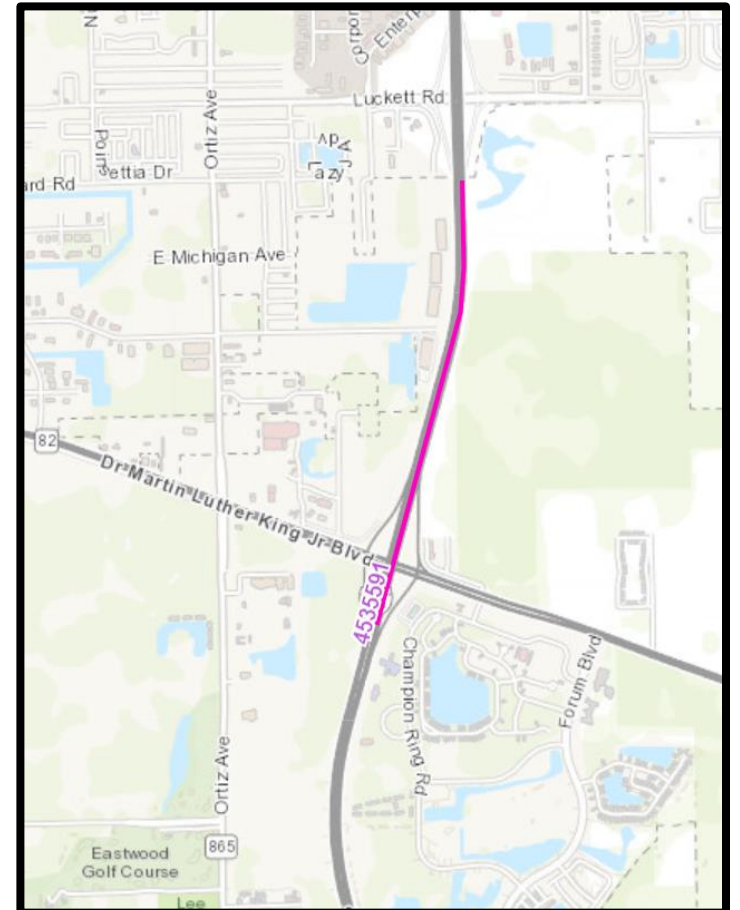

## **FPID 452793-1 I-75 from S of SR 82 to S of Lockett Rd**

- Scope will include
  - 3D Survey
  - Resurfacing
  - Signing and pavement marking
  - Miscellaneous work to be performed
- Issues and concerns
  - Maintenance of traffic
  - Community impact
  - Possible Utilities

## Ad 25124- SR 25 (US 27) Resurfacing- Polk County

- FPID:
  - 450885-1
- Procurement project manager:  
Jennifer Freeman
- Current ad date: March 29, 2024
- Execution month: August 2024



## FPID 450885-1 SR 25 (US 27) from Highlands County Line to N of SR 700 (US 98)

- Design project manager: Scott McCall
- 6.976 miles
- Design budget: \$2.1 million
- Construction budget: \$14.5 million
  - Not Funded, anticipated funding FY 28





## FPID 450885-1 SR 25 (US 27) from Highlands County Line to N of SR 700 (US 98)

- Scope will include
  - Mill and Resurfacing
  - Signing and pavement marking
  - Directional Median Openings
  - Public Involvement
  - Survey
  - Utility coordination
  - SUE
  - Guardrail replacement
- Issues and concerns
  - Maintenance of traffic
  - Community impact
  - Safety

## Ad 25112- Coconut Rd Sidewalk Bundle- Lee County **\*BDI\***


- FPID:
  - 449681-1
  - 449683-1
- Procurement project manager:  
Jacques Louis
- Current ad date: March 29, 2024
- Execution month: August 2024



**FPID 449681-1 Via Coconut Point Roundabout from Coconut Rd to Corkscrew**


**\*BDI\***

- Design project manager: Jacques Louis
- 1.000 miles
- Design budget: \$520,000
- Construction budget: \$640,000
  - FY 27

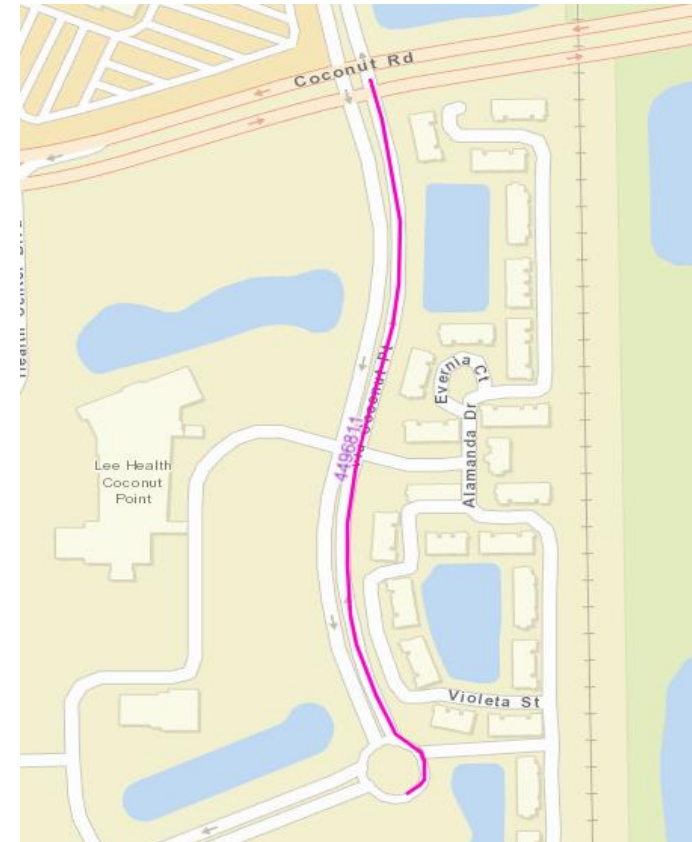

## FPID 449683-1 Coconut Rd. Sidewalk from Oakwild to via Coconut Point

- Design project manager: Jacques Louis
- 0.423 miles
- Design budget: \$320,000
- Construction budget: \$350,000
  - FY 27

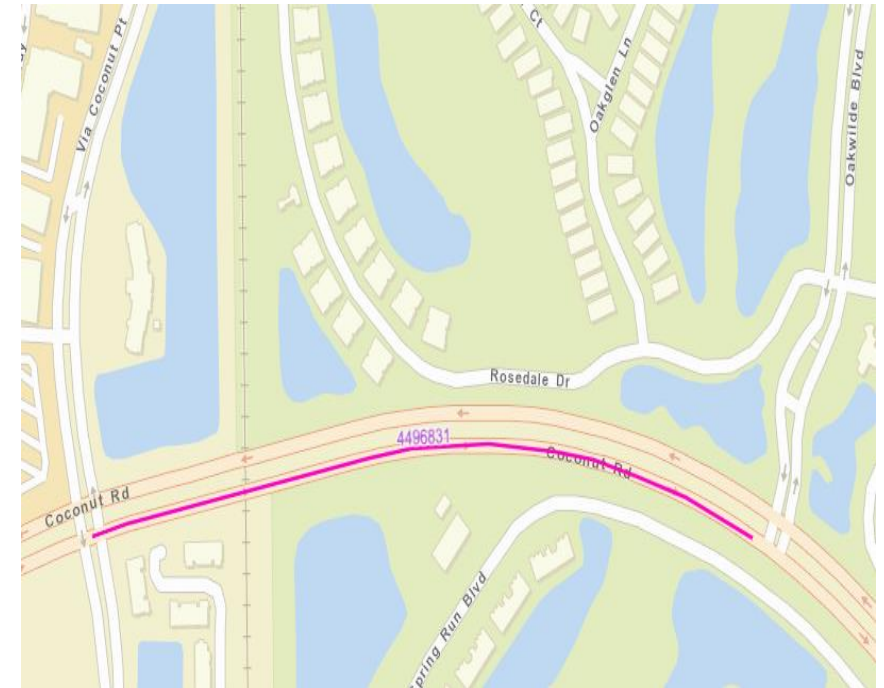

**FPID 449681-1 Via Coconut Point Roundabout from Coconut Rd to Corkscrew**  
**FPID 449683-1 Coconut Rd. Sidewalk from Oakwild to via Coconut Point**

- Scope will include
  - Improvements for RAB's
  - Pedestrian Crossing and Signing Improvements
  - Survey
  - Utility Coordination
  - SUE
- Issues and concerns
  - Community Impact
  - Rail coordination
  - Drainage


## Ad 25119- SR 540 Resurfacing- Polk County

- FPID:
  - 447435-1
- Procurement Project Manager:  
Jennifer McKinney
- Current Ad Date: May 27, 2024
- Execution Month: October 2024



## Ad 25119 – SR 540 from E. of Jim Keene Blvd. To King Rd.

- Design Project Manager
  - Jennifer McKinney
- 2.945 miles
- Design Budget: \$2.4 million
- Construction Budget: \$32.7 million
  - FY 27

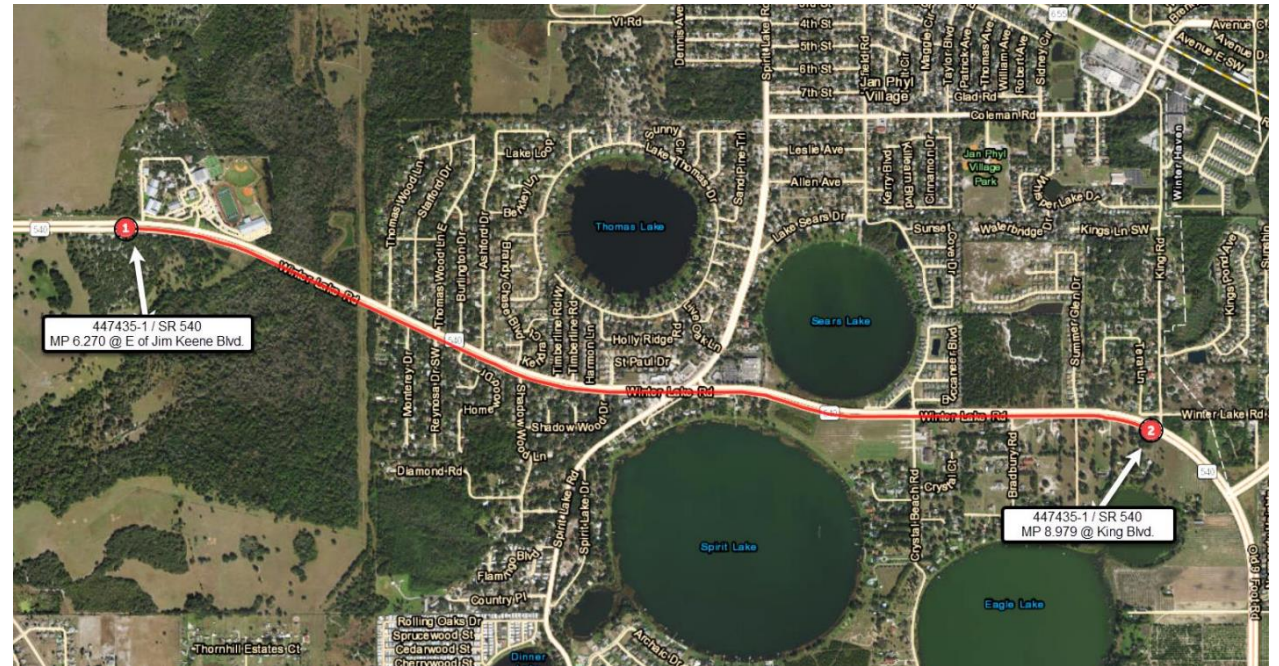


## Ad 25119 – SR 540 from E. of Jim Keene Blvd. To King Rd.

- Scope will include
  - Flexible Reconstruction
    - Reconstruct outside lanes and crossovers
  - Mill and Resurface
  - Signing and Pavement Markings
  - Survey & SUE
  - ADA Ramps
- Issues and concerns
  - Pavement Design
  - MOT
  - Safety



## Ad 25120- RRR Project Bundle – Manatee Interstates

- FPID:
  - 452794-1
  - 453560-1
  - 453561-1
- Procurement project manager:  
Jennifer McKinney
- Current ad date: February 25, 2024
- Execution month: July 2024

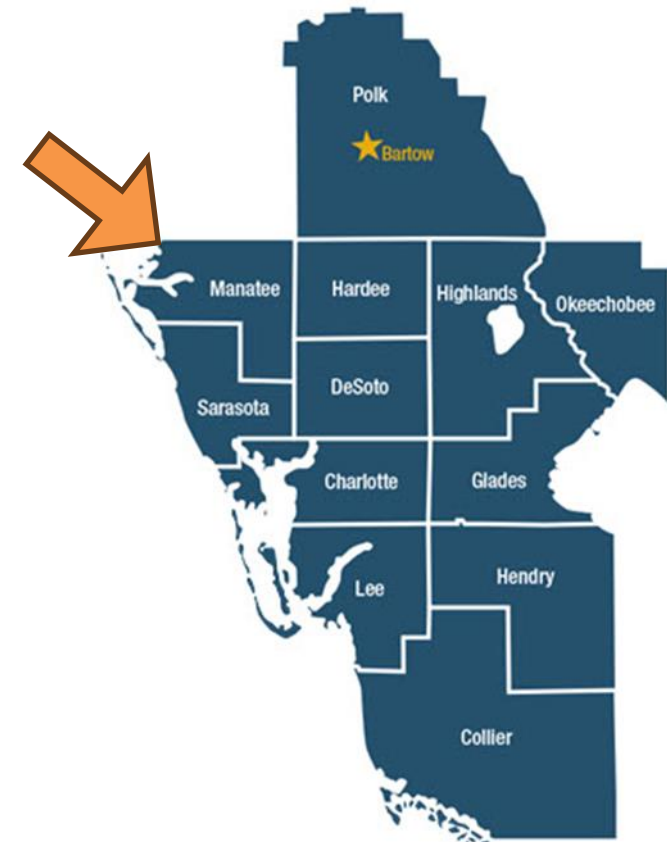

## FPID 452794-1 I-75 from N. of US 301 to N. of I-275

- Design Project Manager  
Jennifer McKinney
- 5.394 miles
- Design Budget \$3.7 million
- Construction Budget: \$17.8 million
  - FY 27



## **FPID 452794-1 I-75 from N. of US 301 to N. of I-275**

- Scope will include
  - Milling and resurfacing
    - Lanes & paved shoulders
    - Interchange ramps & Emergency-Vehicle Crossover
  - Signing and pavement markings
  - Survey & SUE
  - Update/replace Guardrail
  - Shoulder gutter replacement
- Issues and concerns
  - Evaluation of Sign Structures, Shoulder Gutter, Cable Barrier, and Guardrail
  - MOT
  - Safety

## FPID 453560-1 SR 93/US 19/I-275 from N of US 19 to N of Toll Plaza

- Design project manager: Phil Menke
- 0.811 miles
- Design budget: \$0.8 million
- Construction budget: \$4.18 million
  - FY 27




## FPID 453560-1 SR 93/US 19/I-275 from N of US 19 to N of Toll Plaza

- Scope will include
  - Milling and resurfacing of roadway and shoulders
  - Update and replace guardrail
  - Signing and pavement marking
  - Survey
  - Utility coordination
  - SUE
- Issues and concerns
  - Maintenance of traffic
  - Turnpike Enterprise coordination
  - Landscape impacts

## FPID 453561-1 I-275 from S of US 19 to N of US 19

- Design project manager: Jeff Mednick
- 1.680 miles
- Design budget: \$825,000
- Construction budget: \$3.6 million
  - FY 27

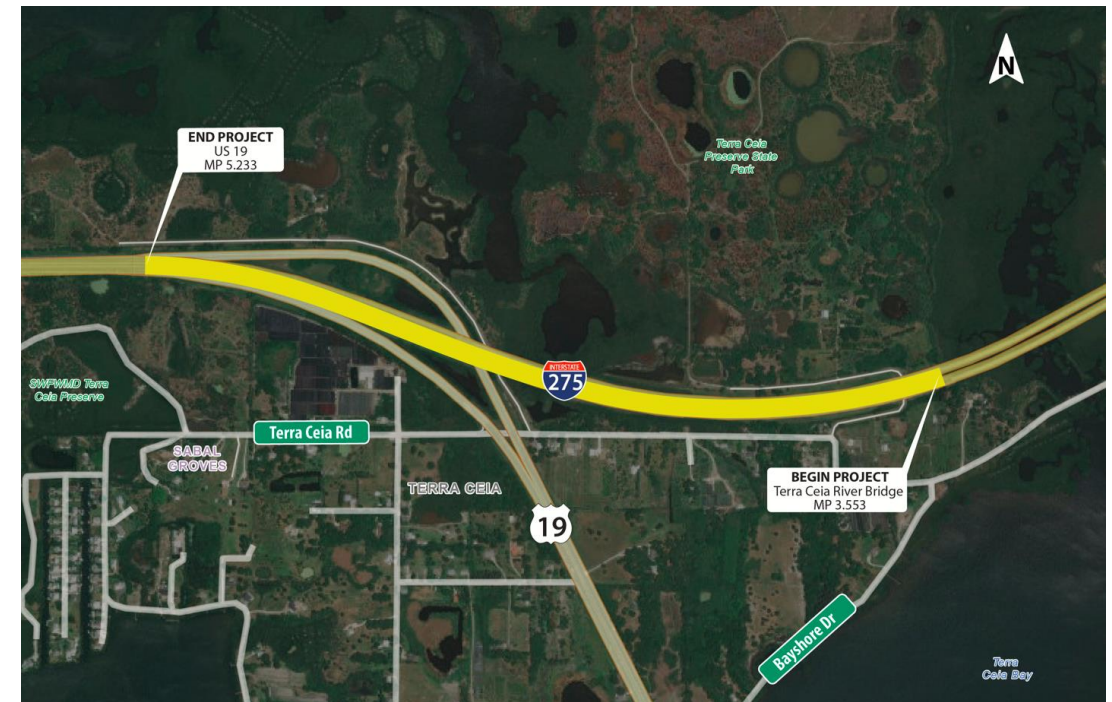


## **FPID 453561-1 I-275 from S of US 19 to N of US 19**

- Scope will include
  - Milling and resurfacing
    - Lanes & paved shoulders
    - Interchange ramps to Gore Points
  - Signing and pavement markings
  - Survey & SUE
  - Update/replace Guardrail
  - Shoulder gutter replacement
- Issues and concerns
  - Evaluation of Sign Structures, Shoulder Gutter, Cable Barrier, and Guardrail
  - Striping/Signage of Terra Ceia River Bridge
  - Evaluate Pavement SB off-ramp

## Ad 25122- SR 25 (US 27) Resurfacing- Highlands County


- FPID:
  - 451270-1
- Procurement project manager:  
Ryan Weeks
- Current ad date: March 29, 2024
- Execution month: August 2024

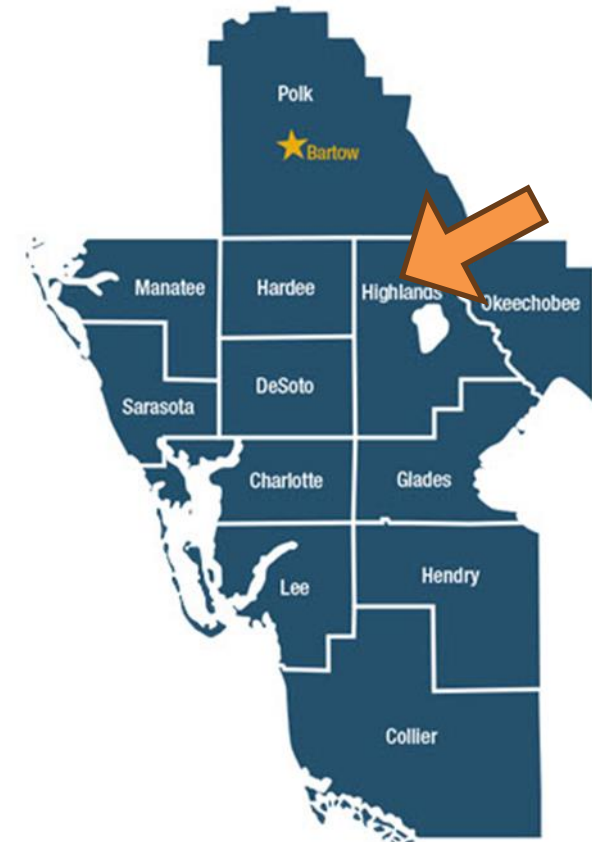



## FPID 451270-1 SR 25 (US 27) from N of Ponce De Leon Blvd to N of Lake Isis Ave

- Design project manager: Ahmad Abdellatif
- 3.674 miles
- Design budget: \$1.5 million
- Construction budget: \$12 million
  - FY 27

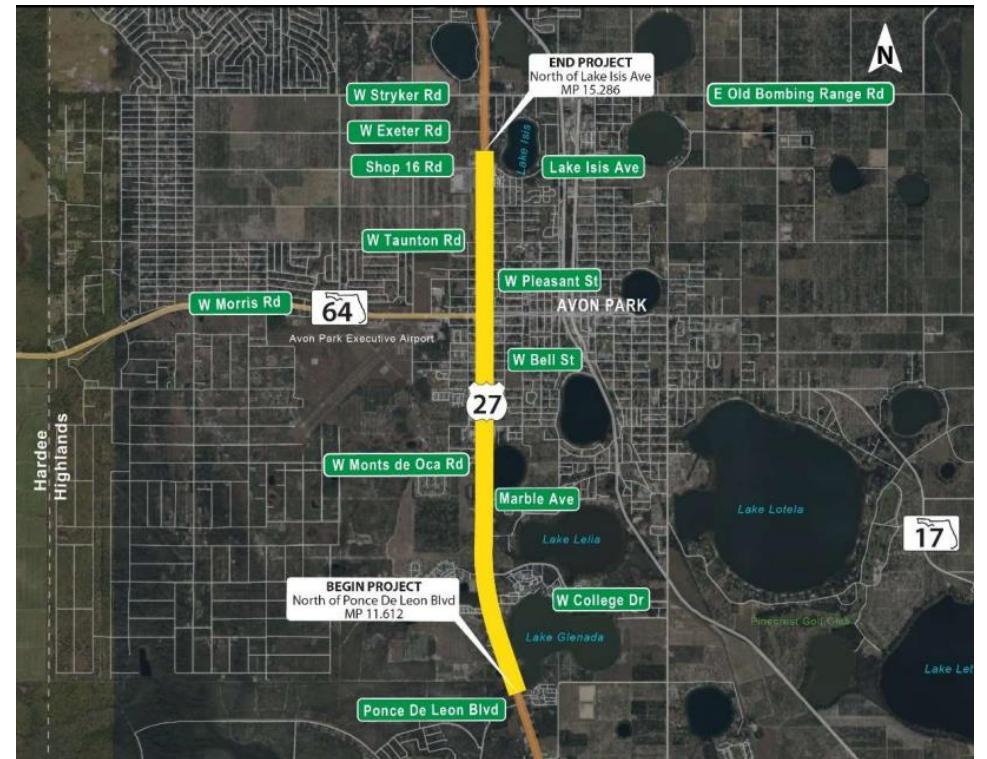

## **FPID 451270-1 SR 25 (US 27) from N of Ponce De Leon Blvd to N of Lake Isis Ave**

- Scope will include
  - Minor Highway Design
  - Traffic Signal Timing
  - Signing, Pavement Marking, & Channelization
  - Survey
  - Miscellaneous Structures

## Resurfacing Continuing Services Contracts

- Project Manager: Amy Blair
- Two (2) Zero Dollar Resurfacing Design Contracts will be awarded.
- \$5M Ceiling
- Anticipate advertisement in 2<sup>nd</sup> Quarter FY 2024





Florida Department of Transportation



# MOVE OVER OR SLOW DOWN

FOR ALL VEHICLES WITH FLASHING LIGHTS

IT'S THE LAW



KEEP FIRST RESPONDERS, ROAD RANGERS AND ROAD CREWS SAFE



Slides and recorded presentation  
will be uploaded to the  
Professional Service Marketing  
site.

<https://www.fdot.gov/procurement/marketingd1>

**Thank You  
For Attending!**

