

Dashboard

The Dashboard is the page displayed by default when accessing the PSEE application. This page displays an overview of a series of Projects as determined by customizable search criteria. To reach this page after navigating away, click on the Dashboard hyperlink in the main menu.

Search Profile Default

The Standard View screen is displayed when accessing PSEE with no Default Search Profile set. The screen displays the most recently accessed projects, bookmarked projects or any project for which the user is a Project Manager.

ProjectSuite Enterprise Edition User: MADAN ARORA &

Go To Project -

Dashboard - Project - Search - Create Project - Assignments - Reports - Help

Dashboard

You currently have no Search Profiles set up. These can be used to customize the list of Projects shown on your Dashboard. [\[Create Profile\]](#)

Project	Local Name	Status	Letting	Construction Finish	Schedule Condition	Float	Contract Class	Work Mix	County	PSEE PM	Open Statuses	Goes With
190015-1	TRAINING PROGRAM TRANSPORTATION MANAGEMENT SEMINAR	LINE ITEM COMPLETED				0	5	-	DIST/ST-WIDE		0	N
208373-2	SR 10 (US 90 WEST) FROM BROWN ROAD TO WEST OF LAKE CITY AVE	ADVERTISED	06/20/2012	01/01/2014		0	1	0213-ADD LANES & RECONSTRUCT	COLUMBIA	CHRISTOPHER DICKS	0	Y
209659-5	SR 23 (BRANNON FIELD CHAFEE RD) FROM 103RD ST TO S OF I-10	CONST.COMPLETE		08/01/2007 A		0	1	0002-NEW ROAD CONSTRUCTION	DUVAL		0	Y
217976-2	SR 30 (US 98) @ COLLEGE DR/D AVENUE INTERSECTIONS	CONST.COMPLETE		10/11/2009 A		0	1	0232-INTERSECTION (NEW)	BAY	DEAN MITCHELL	0	Y
404525-1	SR 426 FROM MITCHELL HAMMOCK RD TO PINE ST	CONST.COMPLETE	03/31/2010			0	1	0213-ADD LANES & RECONSTRUCT	SEMINOLE	SARAH VANGUNDY	0	Y

Float greater than or equal to 0 Float less than 0 and greater than or equal to -20 Float less than -20

Page 1 (Showing Items 1 to 5 of 5) Show per page 10 25 50 From: 1 To: 5 [Export Results](#)

A user can set a customized profile through the **Create Profile** link. Once a profile is created, the user can choose from a dropdown, which profile he wants to access/view.

ProjectSuite Enterprise Edition User: MADAN ARORA &

Go To Project -

Dashboard - Project - Search - Create Project - Assignments - Reports - Help

Dashboard

View Profile: (Standard View - No Profile Selected) [\[Create Profile\]](#)
 (Standard View - No Profile Selected) Construction Projects
 My Projects

Project	Local Name	Status	Letting	Construction Finish	Schedule Condition	Float	Contract Class	Work Mix	County	PSEE PM	Open Statuses	Goes With
195705-1	SR ROAD TO W OF I-75	COMPLETED	06/23/2004 A			0	1	0213-ADD LANES & RECONSTRUCT	LEE	CHANG WANG	0	N
238395-4	SR 500 (US 441) FROM MARTIN LUTHER KING TO LAKE ELLA RD	UNDER CONSTRUCTION	10/31/2011			0	1	0213-ADD LANES & RECONSTRUCT	LAKE	SARAH VANGUNDY	0	Y
238429-4	SR 50 FROM W OF HANCOCK ROAD 800' W. REMINGTON ROAD	CONST.COMPLETE	02/08/2013			0	1	0213-ADD LANES & RECONSTRUCT	LAKE	DAVID COOKE	0	Y
249941-2	SR 823/NW 57 AVENUE FROM WEST 19 STREET TO WEST 23 STREET	CONST.COMPLETE	06/25/2009 A			0	7	0213-ADD LANES & RECONSTRUCT	MIAMI-DADE	DANNY IGLESIAS	0	Y
404525-1	SR 426 FROM MITCHELL HAMMOCK RD TO PINE ST	CONST.COMPLETE	03/31/2010			0	1	0213-ADD LANES & RECONSTRUCT	SEMINOLE	SARAH VANGUNDY	0	Y

Float greater than or equal to 0 Float less than 0 and greater than or equal to -20 Float less than -20

Page 1 (Showing Items 1 to 5 of 5) Show per page 10 25 50 From: 1 To: 5 [Export Results](#)

Once a desired profile is selected, the user is displayed with the customized dashboard.

Project	Local Name	Status	Letting	Construction Finish	Schedule Condition	Float	Contract Class	Work Mix	County	PSE PM	Open Statuses	Goes With
217909-3	SR 77 FROM BAY COUNTY LINE TO NORTH OF CR 279	PRE-CONST.UNDERWAY				0	1	9982-PRELIM ENG FOR FUTURE CAPACITY	WASHINGTON	WILLIAM BARBER	0	Y
217909-7	SR 77 FROM 1 MI N WAUSAU CITY L TO S CR 276 CLAYTON ROAD	CANDIDATE LINE ITEM	07/18/2018	11/08/2018		-27	1	0213-ADD LANES & RECONSTRUCT	WASHINGTON	WILLIAM BARBER	0	Y
218605-2	SR 10 (US 90A) 9 MI FROM SR 297 PINE FOREST TO SR 95 (US 28)	PRE-CONST.UNDERWAY				0	5	2000-RIGHT OF WAY - FUTURE CAPACITY	ESCAMBIA	WILLIAM BARBER	0	N
219881-2	SR 389 (US 219) FROM WAKULLA COUNTY LINE TO L.L WALLACE ROAD	PRE-CONST.UNDERWAY				0	1	9982-PRELIM ENG FOR FUTURE CAPACITY	LEON	WILLIAM BARBER	0	Y
220663-2	SR 83 (US 331) FROM NEW ALIGN OWL'S HEAD TO EDGEWOOD CIRCLE	ROW ACQUISITION BEG.				-47	1	2000-RIGHT OF WAY - FUTURE CAPACITY	WALTON	WILLIAM BARBER	0	Y
220663-4	SR 83 (US 331) FROM NEW ALIGN OWL'S HEAD TO N NOKUSE PLANTATION	UNDER CONSTRUCTION		01/25/2013		0	5	0213-ADD LANES & RECONSTRUCT	WALTON	WILLIAM BARBER	0	Y
220663-5	SR 83 (US 331) FROM N NOKUSE PLANTATION TO EDGEWOOD CIRCLE	PRE-CONST.UNDERWAY		02/08/2013		0	5	0213-ADD LANES & RECONSTRUCT	WALTON	WILLIAM BARBER	0	Y
220773-1	SR 79 FROM N ENVIRONMENTAL ROAD TO STRICKLAND ROAD	CONST.COMPLETE		09/16/2011 A		0	1	0213-ADD LANES & RECONSTRUCT	WASHINGTON	WILLIAM BARBER	0	Y
220773-7	SR 79 FROM CR 279 PATE POND RD TO N OF CYPRESS CREEK BR.	ROW ACQUISITION BEG.				0	1	0213-ADD LANES & RECONSTRUCT	WASHINGTON	WILLIAM BARBER	0	Y
222477-1	SR 8 (I-10) FROM SR 291 DAVIS HIGHWAY TO SR 10A (US 90) SCENIC	ROW ACQUISITION BEG.	08/28/2013	05/28/2017		-111	1	0213-ADD LANES & RECONSTRUCT	ESCAMBIA	WILLIAM BARBER	0	N

Float greater than or equal to 0
 Float less than 0 and greater than or equal to -20
 Float less than -20

Page 1 2 3 4 (Showing Items 1 to 10 of 38) Show per page 10 25 50 From: 1 To: 38 [Export Results](#)

The user can set this profile as default profile by clicking on **Set as Default**.

Note: Learn more about creating and managing user profiles by reading the **User Profile- Search Profile Management** Help Document.

Dashboard Columns

The dashboard displays the user with important information about the project at a glance. The columns displayed on the dashboard are:

Project: This is the project number. The user can click on the project number hyperlink and will be directed to the Project Info details page.

Local Name: This is the commonly used descriptive name by which a roadway, airport, seaport, etc. is identified.

Status: The status column shows the current phase of the project.

Letting: This is the date when a project is Let.

Construction Finish: This is the date when the construction on a project is finished.

Schedule Condition: A weather icon shows the project schedule condition calculated by the float.

Sunny = On Time (Float greater than or equal to 0)

Sunny/Cloudy = Late (Float less than 0 and greater than or equal to -20)

Thunderstorms = Really Late (Float less than -20)

Float: This is the amount of time that a schedule activity can be delayed without delaying the early start date of any immediately following schedule activities. This is the minimum float for all the activities.

Contract Class: This is the contract class of a Line Item.

Work Mix: This code identifies the major category of work effort required on a particular Item Segment.

County: This column shows the county for the project.

PSEE-PM: This is the person responsible for the monitoring and completion of the work involved for an Item Segment.

Open Statuses: This column shows if there are any open statuses for a project. More detailed view about the status of a project can be found under the **Project Status** module or by clicking on the hyperlink.

Project	Local Name	Status	Letting	Construction Finish	Schedule Condition	Float	Contract Class	Work Mix	County	PSEE PM	Open Statuses	Goes With
194093-1	US 17 FROM N OF PEACE RIVER TO TROPICANA ROAD	CONST.COMPLETE				0	1	0218-ADD LANES & REHABILITATE PVMINT	HARDEE	CHANG WANG		N
195705-1	SR 78 (BAYSHORE) FROM E OF SLATER ROAD TO W OF I-75	LINE ITEM COMPLETED	06/23/2004 A			0	1	0213-ADD LANES & RECONSTRUCT	LEE	CHANG WANG	0	N
238395-4	SR 500 (US 441) FROM MARTIN LUTHER KING TO LAKE ELLA RD	UNDER CONSTRUCTION	10/31/2011			0	1	0213-ADD LANES & RECONSTRUCT	LAKE	SARAH VANGUNDY	0	Y
249941-2	SR 823NW 57 AVENUE FROM WEST 19 STREET TO WEST 23 STREET	CONST.COMPLETE	06/25/2009 A			0	7	0213-ADD LANES & RECONSTRUCT	MIAMI-DADE	DANNY IGLESIAS	0	Y
404525-1	SR 428 FROM MITCHELL HAMMOCK RD TO PINE ST	CONST.COMPLETE	03/31/2010			0	1	0213-ADD LANES & RECONSTRUCT	SEMINOLE	SARAH VANGUNDY	0	Y

Float greater than or equal to 0
 Float less than 0 and greater than or equal to -20
 Float less than -20

Page 1 (Showing items 1 to 5 of 5) Show per page 10 25 50 From: 1 To: 5 [Expert Results](#)

Project Info [194093-1] (Click to expand) ⓘ ⚙

Project Status (Click to collapse) ⓘ ⚙


Date:	6/4/2012	Expiration Date:	6/28/2012
Category:	Design Request	Title:	DDDD
Status:	Outstanding		
Details:	test		

Created By: CHANG WANG
 Created Date: 6/5/2012 4:56 PM
 Last Updated By: CHANG WANG
 Last Updated Date: 6/5/2012 4:56 PM

PSEE Project Status Documents (Click to collapse) ⓘ

No Documents Found

Goes with: This column displays if there are any work program related projects. If there are any related projects, it is noted as **Y**. If there are no related projects, it is noted as **N**. More detailed view about the related projects can be found under **View → Related Projects**.

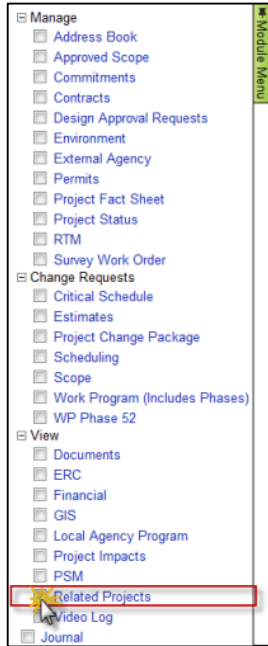

Project Info [238395-4] (Click to expand)

Related Projects (Click to collapse)

Work Program Related Projects (Click to collapse)				
Project	Relationship	County	Description	PSEE Project Manager
238395-7	PROJECT COMPONENT	SUMTER	SR 500 (US 441) FROM BUENOS AIRES TO MARION CO LINE	SUZANNE PHILLIPS
238395-8	PROJECT COMPONENT	MARION	SR 500 (US 441) FROM SUMTER CO LINE TO CR 42	ASHRAF ELMAGHRABY
238395-5	PROJECT COMPONENT	LAKE	SR 500 (US 441) FROM LAKE ELLA RD TO AVENIDA CENTRAL	SARAH VANGUNDY
238395-1	PROJECT COMPONENT	LAKE	SR 500 (US 441) FROM PICCIOLA RD TO BOONE CT/SUMTER CO L	
238395-2	PROJECT COMPONENT	SUMTER	SR 500 US 441 FROM LAKE CO LINE TO MARION CO LINE	
238395-3	PROJECT COMPONENT	MARION	SR 500 US 441 FROM SUMTER CO LINE TO CR 42	

Projects Related By Contract (Click to collapse)				
<input type="radio"/> All <input checked="" type="radio"/> Exclude B-Type Contracts				
Project	County	Description	PSEE Project Manager	Contract
237550-1	BREVARD	SR 5 US 1 FROM POST RD TO SR 404 PINEDA CSWY		DM821
237576-3	BREVARD	SR 5 (US1) INTERSECTION AT BARNES BLVD	DAVID COOKE	SJWM5
237965-1	FLAGLER	SR 100 FROM SR 5 US 1 TO 0.1MI W OF BELLE TERR		DM821
238314-1	LAKE	SR 500 US 441 FROM LAKE EUSTIS DR TO CR 44B		DM818
238315-1	LAKE	SR 500 US 441 FROM MILLS STREET TO W OF COLLEGE ROAD	JOEL MARMIE	C8003
	LAKE	SR 500 US 441 FROM MILLS STREET TO W OF COLLEGE ROAD	JOEL MARMIE	SJWM5
238394-2	LAKE	SR 500 (US 441) FROM PERKINS ST TO N OF GRIFFIN RD	SARAH VANGUNDY	DM818
	LAKE	SR 500 (US 441) FROM PERKINS ST TO N OF GRIFFIN RD	SARAH VANGUNDY	DMP00
238394-3	LAKE	SR 500 (US 441) FROM PERKINS ST TO SR 44	SARAH VANGUNDY	C8N35
	LAKE	SR 500 (US 441) FROM PERKINS ST TO SR 44	SARAH VANGUNDY	DMW19

Page 1 2 3 4 5 6 7 8 ... 12 Go To (Showing Items 1 to 10 of 118) Show per page 10 25 50
