ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
0	Planning and PD&E (EA)		1089 days	Mon 8/1/16	Thu 10/1/20	0 days		
1	PLANNING ACTIVITES		251 days	Mon 8/1/16	Mon 7/17/17	0 days		
2	District SWAT Planning Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting)	746	1 day	Mon 8/1/16	Mon 8/1/16	0 days		3FS+131 days
3	District SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted)		2 days	Wed 2/1/17	Thu 2/2/17	0 days	2FS+131 days	6FS+20 days,7FS+20 days,8FS+20 days
4	ETDM PROGRAMMING SCREEN		97 days	Fri 3/3/17	Mon 7/17/17	0 days		
5	ETDM Programming Screen Meeting		20 days	Fri 3/3/17	Thu 3/30/17	0 days		
6	ETDM Programming Screen PED		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9
7	ETDM Programming Screen Purpose and Need		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9,15,16
8	Planning Consistency Completion	710	5 days	Fri 3/3/17	Thu 3/9/17	15 days	3FS+20 days	9,143
9	ETDM PROGRAMMING SCREEN START/ADVANCE NOTIFICATION	700, 224	32 days	Fri 3/31/17	Mon 5/15/17	0 days	6,7,8	10,26
10	ETDM Programming Screen Responses		44 days	Tue 5/16/17	Fri 7/14/17	0 days	9	11
11	ETDM PROGRAMMING PRELIMINARY SUMMARY REPORT PUBLISHED	701	1 day	Mon 7/17/17	Mon 7/17/17	0 days	10	143,13FS+10 days,40
12	PRE-PD&E ACTIVITIES		294 days	Tue 8/1/17	Fri 9/14/18	0 days		
13	SWAT Kickoff Meeting	747	1 day	Tue 8/1/17	Tue 8/1/17	0 days	11FS+10 days	14,16
14	Assign PD&E Project Manager	704	1 day	Wed 8/2/17	Wed 8/2/17	0 days	13	16,26
15	Traffic Analysis		111 days	Thu 8/3/17	Thu 1/4/18	0 days	7	
16	Traffic Methodology Meeting		1 day	Thu 8/3/17	Thu 8/3/17	0 days	7,14,13	17
17	Traffic Methodology Memorandum		5 days	Fri 8/4/17	Thu 8/10/17	0 days	16	18,19
18	Traffic Data Collection		20 days	Fri 8/11/17	Thu 9/7/17	0 days	17	20
19	Crash Data and Analysis		20 days	Fri 8/11/17	Thu 9/7/17	60 days	17	22
20	Prepare Traffic Projections		30 days	Fri 9/8/17	Thu 10/19/17	0 days	18	21
21	Prepare Capacity Analysis		30 days	Fri 10/20/17	Thu 11/30/17	0 days	20	22
22	Draft Project Traffic Analysis Report		10 days	Fri 12/1/17	Thu 12/14/17	0 days	21,19	23,30
23	FDOT Review - Draft Project Traffic Analysis Report		10 days	Fri 12/15/17	Thu 12/28/17	0 days	22	24
24	Final Project Traffic Analysis Report	757	5 days	Fri 12/29/17	Thu 1/4/18	0 days	23	109,40
25	INTERCHANGE ACCESS REQUEST		292 days	Thu 8/3/17	Fri 9/14/18	74 days		
26	Initiate IJR/IMR/SIMR or IOAR		1 day	Thu 8/3/17	Thu 8/3/17	0 days	9,14	27
27	Prepare MLOU		5 days	Fri 8/4/17	Thu 8/10/17	0 days	26	28
28	DIRC/SPO Review of MLOU		10 days	Fri 8/11/17	Thu 8/24/17	0 days	27	29
29	FHWA Review of MLOU		20 days	Fri 8/25/17	Thu 9/21/17	60 days	28	30
30	Develop Alternatives		30 days	Fri 12/15/17	Thu 1/25/18	0 days	29,22	31
31	Perform Operational Analysis		30 days	Fri 1/26/18	Thu 3/8/18	0 days	30	32
32	Prepare Preliminary IMR/IJR		45 days	Fri 3/9/18	Thu 5/10/18	0 days	31	33
33	DIRC/SPO Reviw of Preliminary IJR/IMR		10 days	Fri 5/11/18	Thu 5/24/18	0 days	32	34
34	FHWA Review of Preliminary IJR/IMR		20 days	Fri 5/25/18	Thu 6/21/18	0 days	33	35,69
35	Prepare Final IJR/IMR		30 days	Fri 6/22/18	Thu 8/2/18	0 days	34	36
36	DIRC/SPO Review of Final IJR/IMR		10 days	Fri 8/3/18	Thu 8/16/18	0 days	35	37
37	FHWA Review of IJR/IMR		20 days	Fri 8/17/18	Thu 9/13/18	0 days	36	38
38	IJR/IMR Approval	765	1 day	Fri 9/14/18	Fri 9/14/18	74 days	37	99
39	DEVELOP SCOPE AND SCHEDULE		21 days	Fri 1/5/18	Fri 2/2/18	0 days		
40	Begin PD&E Scope and Schedule		20 days	Fri 1/5/18	Thu 2/1/18	0 days	11,24	41
41	PD&E SCOPE AND SCHEDULE COMPLETION	703	1 day	Fri 2/2/18	Fri 2/2/18	0 days	40	44,43
42	PROCUREMENT		122 days	Mon 2/5/18	Tue 7/24/18	0 days		
43	PD&E Advertisement	705	1 day	Mon 2/5/18	Mon 2/5/18	0 days	41	44
44	Procurement		120 days	Tue 2/6/18	Mon 7/23/18	0 days	41,43	45
45	Notice to Proceed		1 day	Tue 7/24/18	Tue 7/24/18	0 days	44	48
46	PD&E STUDY		572 days	Wed 7/25/18	Thu 10/1/20	0 days		
47	PROJECT MANAGEMENT		7 days	Wed 7/25/18	Thu 8/2/18	0 days		
48	ENVIRONMENTAL ASSESSMENT START	707	1 day	Wed 7/25/18	Wed 7/25/18	0 days	45	53,49,50
49	Prepare Project Management Plan		5 days	Thu 7/26/18	Wed 8/1/18	0 days	48	51
50	Prepare QC Plan		5 days	Thu 7/26/18	Wed 8/1/18	0 days	48	51
51	Project Kickoff Meeting with FDOT		1 day	Thu 8/2/18	Thu 8/2/18	0 days	49,50	89,82,83,85,54,84,87,90,86
52	PUBLIC INVOLVEMENT		571 days	Thu 7/26/18	Thu 10/1/20	0 days		
53	Prepare Public Involvement Plan		20 days	Thu 7/26/18	Wed 8/22/18	31 days	48	56
54	Public Involvement Data Collection		45 days	Fri 8/3/18	Thu 10/4/18	0 days	51	56
55	Prepare for Public Kickoff Meeting	365	47 days	Fri 10/5/18	Mon 12/10/18	112 days		
56	Site Review		1 day	Fri 10/5/18	Fri 10/5/18	0 days	87FS-60 days,53,54	57,58,59
57	Newsletter		20 days	Mon 10/8/18	Fri 11/2/18	0 days	56	60
58	Newspaper Ad		20 days	Mon 10/8/18	Fri 11/2/18	0 days	56	60
59	Elected/Appointed/Property Owner Letters		20 days	Mon 10/8/18	Fri 11/2/18	0 days	56	60
60	Presentation/Display Material Review		15 days	Mon 11/5/18	Fri 11/23/18	0 days	59,57,58	61
61	Public Kickoff Meeting		1 day	Mon 11/26/18	Mon 11/26/18	0 days	87,82,83,84,85,89,90,60	62
62	Public Comment Period		10 days	Tue 11/27/18	Mon 12/10/18	83 days	61	64
63	Prepare for Public Information Meeting	365	76 days	Fri 4/5/19	Fri 7/19/19	0 days		
64	Site Review		1 day	Fri 4/5/19	Fri 4/5/19	0 days	107FS-60 days,62	68,65,66,67
65	Newsletter		20 days	Mon 4/8/19	Fri 5/3/19	0 days	64	68
66	Newspaper Ad		20 days	Mon 4/8/19	Fri 5/3/19	0 days	64	68
67	Elected/Appointed/Property Owner Letters		20 days	Mon 4/8/19	Fri 5/3/19	0 days	64	68
68	Presentation/Display Material Review		15 days	Mon 5/6/19	Fri 5/24/19	29 days	64,65,66,67	69
69	Public Information Meeting	292	1 day	Fri 7/5/19	Fri 7/5/19	0 days	107FS+5 days,68,34	70
70	Public Comment Period		10 days	Mon 7/8/19	Fri 7/19/19	0 days	69	108,109,72
71	Prepare for Public Hearing	366	93 days	Tue 5/26/20	Thu 10/1/20	0 days		
72	Site Review		20 days	Tue 5/26/20	Mon 6/22/20	0 days	70,147	76,73,74,75
73	Newsletter		20 days	Tue 6/23/20	Mon 7/20/20	12 days	72	76
74	Newspaper Ad		20 days	Tue 6/23/20	Mon 7/20/20	12 days	72	76
75	Elected/Appointed/Property Owner Letters		20 days	Thu 7/9/20	Wed 8/5/20	0 days	72,155	76
76	Presentation/Display Material Review		15 days	Thu 8/6/20	Wed 8/26/20	0 days	72,73,74,75	77,78
77	Notice of Public Availability		15 days	Thu 8/27/20	Wed 9/16/20	0 days	76	78
78	Public Hearing	262	1 day	Thu 9/17/20	Thu 9/17/20	0 days	77,76	79
79	Public Comment Period		10 days	Fri 9/18/20	Thu 10/1/20	0 days	78	
80	ENGINEERING ANALYSIS		391 days	Fri 8/3/18	Fri 1/31/20	0 days		
81	Data Collection		50 days	Fri 8/3/18	Thu 10/11/18	143 days		
82	Roadway Data Collection		50 days	Fri 8/3/18	Thu 10/11/18	31 days	51	61
83	Drainage Data Collection		50 days	Fri 8/3/18	Thu 10/11/18	31 days	51	61
84	Bridge Data Collection		50 days	Fri 8/3/18	Thu 10/11/18	31 days	51	61
85	Geotechnical Data Collection		50 days	Fri 8/3/18	Thu 10/11/18	31 days	51	61
86	Topographic Survey and ROW Mapping		50 days	Fri 8/3/18	Thu 10/11/18	515 days	51	
87	Prepare Base Map		50 days	Fri 8/3/18	Thu 10/11/18	31 days	51	61,56FS-60 days
88	Traffic Analysis		105 days	Fri 8/3/18	Thu 12/27/18	0 days		
89	Traffic Data Collection		20 days	Fri 8/3/18	Thu 8/30/18	0 days	51	61,91

Project: Planning and PD&E (EA
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical

ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
90	Crash Data and Analysis		20 days	Fri 8/3/18	Thu 8/30/18	61 days	51	61
91	Prepare Traffic Projections		30 days	Fri 8/31/18	Thu 10/11/18	0 days	89	92
92	Prepare Capacity Analysis		30 days	Fri 10/12/18	Thu 11/22/18	0 days	91	99,93
93	Draft Project Traffic Analysis Report		10 days	Fri 11/23/18	Thu 12/6/18	0 days	92	94,97,98
94	FDOT Review - Draft Project Traffic Analysis Report		10 days	Fri 12/7/18	Thu 12/20/18	0 days	93	95
95	Final Project Traffic Analysis Report	757	5 days	Fri 12/21/18	Thu 12/27/18	0 days	94	99,109,100
96	Alternative Analysis		301 days	Fri 12/7/18	Fri 1/31/20	15 days		
97	Typical Sections Analysis		40 days	Fri 12/7/18	Thu 1/31/19	55 days	93	104
98	Complete Streets/Multi Modal Analysis		40 days	Fri 12/7/18	Thu 1/31/19	55 days	93	104
99	Concept Development		40 days	Fri 12/28/18	Thu 2/21/19	0 days	92,95,38	104,101,102,103
100	Access Management Analysis		40 days	Fri 12/28/18	Thu 2/21/19	40 days	95	104
101	Drainage Analysis		40 days	Fri 2/22/19	Thu 4/18/19	0 days	99	104
102	Utility Coordination & Analysis		40 days	Fri 2/22/19	Thu 4/18/19	0 days	99	104
103	Railroad Coordination		40 days	Fri 2/22/19	Thu 4/18/19	0 days	99	104
104	Evaluation Matrix (1st Draft)		5 days	Fri 4/19/19	Thu 4/25/19	0 days	97,98,101,102,103,100,99	106,105,119,120,121,122,123,1
105	Construction Cost Estimates (LRE)		10 days	Fri 4/26/19	Thu 5/9/19	30 days	104	107
106	Right-of-Way Analysis		20 days	Fri 4/26/19	Thu 5/23/19	20 days	104	107
107	Evaluation Matrix (2nd Draft)		5 days	Fri 6/21/19	Thu 6/27/19	0 days	105,106,119,120,121,122,123,12	69FS+5 days,64FS-60 days
108	Refine Alternatives (based on public input)		20 days	Mon 7/22/19	Fri 8/16/19	294 days	70	
109	Prepare 1st DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech,		30 days	Mon 7/22/19	Fri 8/30/19	0 days	70,24,95	110
110	FDOT Review - 1st DRAFT Engineering Reports		20 days	Mon 9/2/19	Fri 9/27/19	0 days	109	111
111	Update DRAFT Engineering Reports		15 days	Mon 9/30/19	Fri 10/18/19	0 days	110	112
112	VE Study		5 days	Mon 10/21/19	Fri 10/25/19	0 days	111	113FS+20 days
113	VE Issues Resolution		10 days	Mon 11/25/19	Fri 12/6/19	0 days	112FS+20 days	137,135,114,141,143,115,138
114	Prepare Typical Section Package		20 days	Mon 12/9/19	Fri 1/3/20	0 days	113	116,117
115	Prepare Design Variations and Exceptions		20 days	Mon 12/9/19	Fri 1/3/20	0 days	113	116
116	Typical Section Selection	759	20 days	Mon 1/6/20	Fri 1/31/20	174 days	114,115	
117	FDOT Review - 2nd DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech, PER)		20 days	Mon 1/6/20	Fri 1/31/20	174 days	114	
118	ENVIRONMENTAL ANALYSIS		182 days	Fri 4/26/19	Mon 1/6/20	0 days		
119	Data Collection & Cultural Resources Assessment Survey		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,127
120	Data Collection & Noise Analysis		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,129
121	Data Collection & Contamination Screen Evaluation		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,128
122	Wetland Delineation and Evaluation		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,126
123	Data Collection & Wildlife Survey		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,126
124	Essential Fish Habitat Evaluation		40 days	Fri 4/26/19	Thu 6/20/19	0 days	104	107,126
125	Determination of Section 4(f)		15 days	Fri 4/26/19	Thu 5/16/19	0 days	104	130
126	Prepare 1st Draft Natural Resource Evaluation Report		30 days	Fri 6/21/19	Thu 8/1/19	0 days	122,123,124	131
127	Prepare 1st Draft Cultural Resources Assessment Survey		30 days	Fri 6/21/19	Thu 8/1/19	0 days	119	131
128	Prepare 1st Draft Contamination Screen Evaluation Report		30 days	Fri 6/21/19	Thu 8/1/19	0 days	121	131
129	Prepare 1st Draft Noise Study Report		30 days	Fri 6/21/19	Thu 8/1/19	0 days	120	131
130	Prepare Draft Section 4(f) Evaluation		30 days	Fri 5/17/19	Thu 6/27/19	25 days	125	131
131	FDOT Review 1st DRAFT Environmental Reports (NRE, CSER, CRAS, Noise, Section 4(f))		20 days	Fri 8/2/19	Thu 8/29/19	0 days	126,127,128,129,130	132
132	Update Environmental Reports		15 days	Fri 8/30/19	Thu 9/19/19	0 days	131	135,133,134
133	Finalize Cultural Resources Assessment Survey	333	10 days	Fri 9/20/19	Thu 10/3/19	46 days	132	135
134	Finalize Natural Resource Evaluation Report	761	10 days	Fri 9/20/19	Thu 10/3/19	46 days	132	137,138
135	Submit CRAS to OEM		20 days	Mon 12/9/19	Fri 1/3/20	0 days	132,113,133	136
136	SHPO Consultation Complete	762	1 day	Mon 1/6/20	Mon 1/6/20	0 days	135	143
137	Submit NRE to USFWS		1 day	Mon 12/9/19	Mon 12/9/19	0 days	113,134	139
138	Submit NRE to NMFS		1 day	Mon 12/9/19	Mon 12/9/19	0 days	113,134	140
139	Informal USFWS Consultation Complete	752	10 days	Tue 12/10/19	Mon 12/23/19	10 days	137	143
140	Informal NMFS Consultation Complete	763	10 days	Tue 12/10/19	Mon 12/23/19	10 days	138	143
141	Prepare Conceptual Relocation Plan		20 days	Mon 12/9/19	Fri 1/3/20	1 day	113	143
142	FINAL ENVIRONMENTAL ASSESSMENT DOCUMENTS		169 days	Tue 1/7/20	Fri 8/28/20	0 days		
143	Prepare 1st DRAFT Environmental Assessment		20 days	Tue 1/7/20	Mon 2/3/20	0 days	113,11,136,139,140,141,8	144
144	District Review DRAFT Environmental Assessment	713	20 days	Tue 2/4/20	Mon 3/2/20	0 days	143	145
145	Prepare 2nd DRAFT Environmental Assessment		20 days	Tue 3/3/20	Mon 3/30/20	0 days	144	146
146	OEM Review of 2nd DRAFT Environmental Assessment		20 days	Tue 3/31/20	Mon 4/27/20	0 days	145	147
147	Prepare 3rd DRAFT Environmental Asssessment		20 days	Tue 4/28/20	Mon 5/25/20	0 days	146	148,149,150,151,152,72
148	District submit Environmental Assessment to Cooperating Agencies		20 days	Tue 5/26/20	Mon 6/22/20	0 days	147	153
149	Finalize Engineering & Environmental Reports		10 days	Tue 5/26/20	Mon 6/8/20	10 days	147	153
150	Finalize Section 4(f) Evaluation	751	5 days	Tue 5/26/20	Mon 6/1/20	15 days	147	153
151	Finalize Noise Study Report	335	5 days	Tue 5/26/20	Mon 6/1/20	15 days	147	153
152	Finalize Preliminary Engineering Report	760	5 days	Tue 5/26/20	Mon 6/1/20	15 days	147	153
153	Prepare FINAL Environmental Assessment		10 days	Tue 6/23/20	Mon 7/6/20	0 days	150,151,148,149,152	154
154	FINAL Envrionmental Assessment to OEM	718	1 day	Tue 7/7/20	Tue 7/7/20	0 days	153	155
155	Environmental Assessment Approved by OEM	719	1 day	Wed 7/8/20	Wed 7/8/20	0 days	154	156,75
156	Prepare DRAFT FONSI		5 days	Thu 7/9/20	Wed 7/15/20	0 days	155	157
157	District Review DRAFT FONSI		5 days	Thu 7/16/20	Wed 7/22/20	0 days	156	158
158	Prepare 2nd DRAFT FONSI		5 days	Thu 7/23/20	Wed 7/29/20	0 days	157	159
159	OEM Review 2nd DRAFT FONSI		5 days	Thu 7/30/20	Wed 8/5/20	0 days	158	160
160	Prepare FINAL FONSI		5 days	Thu 8/6/20	Wed 8/12/20	0 days	159	161,163
161	OEM Approves FONSI	732	1 day	Thu 8/13/20	Thu 8/13/20	0 days	160	162
162	EA and FONSI uploaded to ETDM		1 day	Fri 8/14/20	Fri 8/14/20	34 days	161	
163	Location Design Concept Acceptance	263	1 day	Thu 8/13/20	Thu 8/13/20	0 days	160	165FS+10 days,164
164	Publish Notification of EA/FONSI Approval	736	1 day	Fri 8/14/20	Fri 8/14/20	9 days	163	165
165	Pass the Torch Meeting		1 day	Fri 8/28/20	Fri 8/28/20	24 days	163FS+10 days,164	

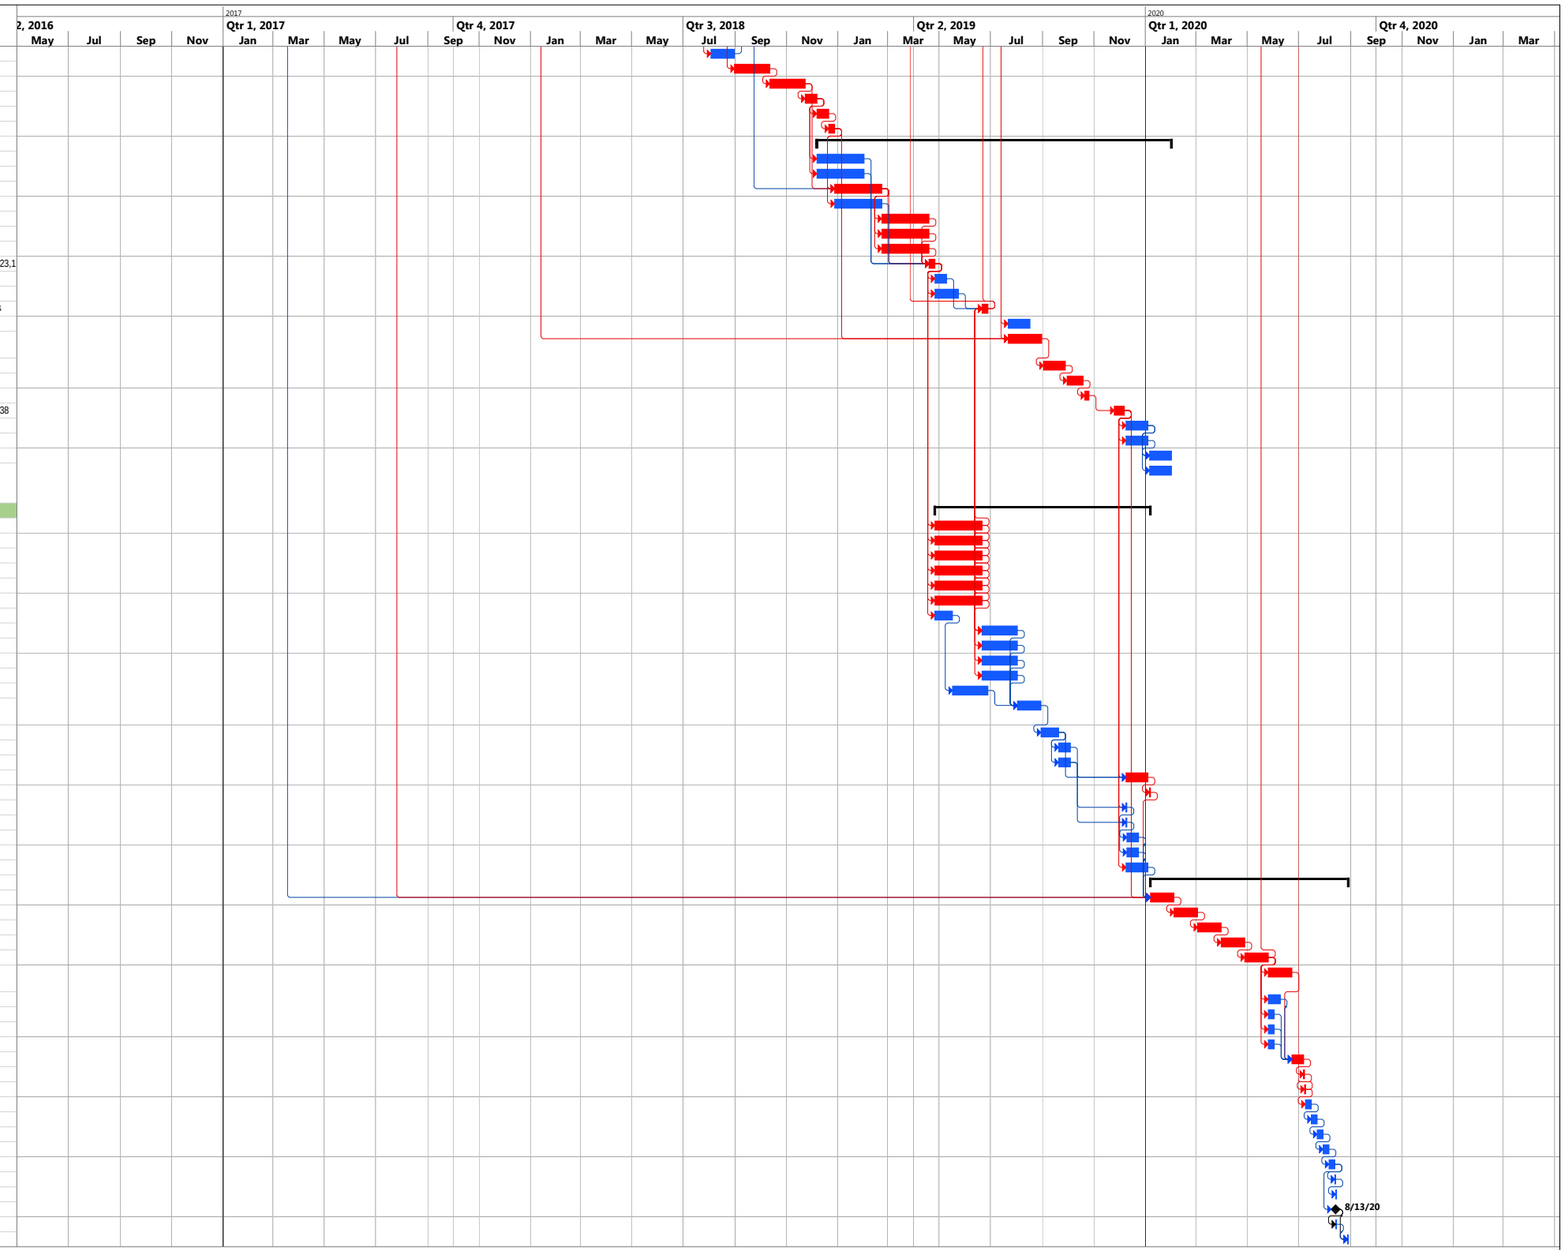

Project: Planning and PD&E (EA
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical
