


Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	RESPONSIBLE PART	2026	2027	2028
Phase 32 BRRP Phase 32 Bridge Repair / Rehab / Painting Template (8 Month		438	0	01-Jul-26	03-Mar-28				
No Project Manager		438	0	01-Jul-26	03-Mar-28				
No Work Mix		438	0	01-Jul-26	03-Mar-28				
No County		438	0	01-Jul-26	03-Mar-28				
PH 31: PRELIMINARYENGINEERING		31	0	01-Jul-26	12-Aug-26				
250010	PRELIMINARY ENGINEERING BEGIN	1	0	01-Jul-26	01-Jul-26	A.IVEY			
WBS250	Preliminary Engineering	31	0	01-Jul-26	12-Aug-26				
164032	PREPARE DESIGN SCOPE OF SERVICES	5	4	02-Jul-26	08-Jul-26				
197010	PAVEMENT DESIGN FOR ROADWAY RECONSTRUCTION (Approach Slab Or	30	0	02-Jul-26	12-Aug-26	W.CHEVILLO			
PH 32: DESIGN CONSULTANT ACQUISITION		6	4	30-Jul-26	06-Aug-26				
299032	DESIGN ENCUMBRANCE	1	4	30-Jul-26	30-Jul-26	R.DODSON			
WBS233	Design Consultant Acquisition	6	4	30-Jul-26	06-Aug-26				
233032	DESIGN CONTRACT EXECUTED (TWO)	1	4	06-Aug-26	06-Aug-26				
PH 3X: DESIGN PHASE II (60%)		80	0	06-Aug-26	25-Nov-26				
234032	NOTICE TO PROCEED	1	4	06-Aug-26	06-Aug-26				
WBS382	PH II (60%) Submittals	80	0	06-Aug-26	25-Nov-26				
382000	PREPARE PH II (60%) PLANS	60	0	13-Aug-26	04-Nov-26				
228010	RECEIVE SUNSHINE 811 DESIGN TICKET	1	58	14-Aug-26	14-Aug-26				
264010	UTILITY CONTACT	1	13	05-Nov-26	05-Nov-26				
302010	REVIEW PH II (60%) PLANS	15	0	05-Nov-26	25-Nov-26				
297060	PH II (60%) CONSTRUCTION ESTIMATE	5	10	05-Nov-26	11-Nov-26	UNASSIGNED			
PH 3X: DESIGN PHASE IV (100%)		161	70	05-Nov-26	17-Jun-27				
355010	PREPARE NON-MAJOR STATE ACTION (NMSA)	80	31	05-Nov-26	24-Feb-27	A.MARSHALL			
333032	PH 32 CULTURAL RESOURCES ASSESSMENT SURVEY	60	30	05-Nov-26	27-Jan-27	S.FOOR			
WBS384	PH IV (100%) Submittals	161	70	05-Nov-26	17-Jun-27				
265010	UTILITY DESIGN MEETING (if needed)	1	13	06-Nov-26	06-Nov-26				
384000	PREPARE PH IV (100%) PLANS	60	0	26-Nov-26	17-Feb-27				
272020	PERMITS APPLICATION RECEIVED	1	70	17-Dec-26	17-Dec-26	A.VANN			
145010	PERMITS	120	70	01-Jan-27	17-Jun-27	A.VANN			
126010	UTILITY WORK SCHEDULES (Update duartion at Initial Schedule)	30	104	18-Feb-27	31-Mar-27				
310010	REVIEW PH IV (100%) PLANS	15	0	18-Feb-27	10-Mar-27				
297100	PH IV (100%) CONSTRUCTION ESTIMATE	5	10	18-Feb-27	24-Feb-27	UNASSIGNED			
113070	PREPARE FINAL PLANS FOR SHELF	20	0	11-Mar-27	07-Apr-27				
PH 52: CONTRACT FILE INDEX (CFI)		122	4	08-Apr-27	24-Sep-27				
172010	NOTICE TO PROCEED PLANS UPDATE	1	0	08-Apr-27	08-Apr-27				
WBS172	Contract File Index (CFI)	122	4	08-Apr-27	24-Sep-27				
748	PREPARE / REVIEW / APPROVE REEV. FOR CONSTRUCTION	120	0	09-Apr-27	23-Sep-27	A.MARSHALL			
220010	PREPARE UPDATE PLANS / PH IV RESUBMITTAL (if needed)	80	15	09-Apr-27	29-Jul-27				
450052	PH 52 TIP / STIP AMENDMENT	60	0	05-Jul-27	24-Sep-27	A.SMITH			
222010	PERMITS TRANSMITTAL MEMO	1	40	30-Jul-27	30-Jul-27	A.VANN			
266010	UTILITY CERTIFICATION	20	18	30-Jul-27	26-Aug-27				
189010	ERC REVIEW FINAL UPDATE PLANS (if needed)	15	15	30-Jul-27	19-Aug-27				
279010	RAILROAD CLEAR LETTER	1	25	20-Aug-27	20-Aug-27	T.HINSON			

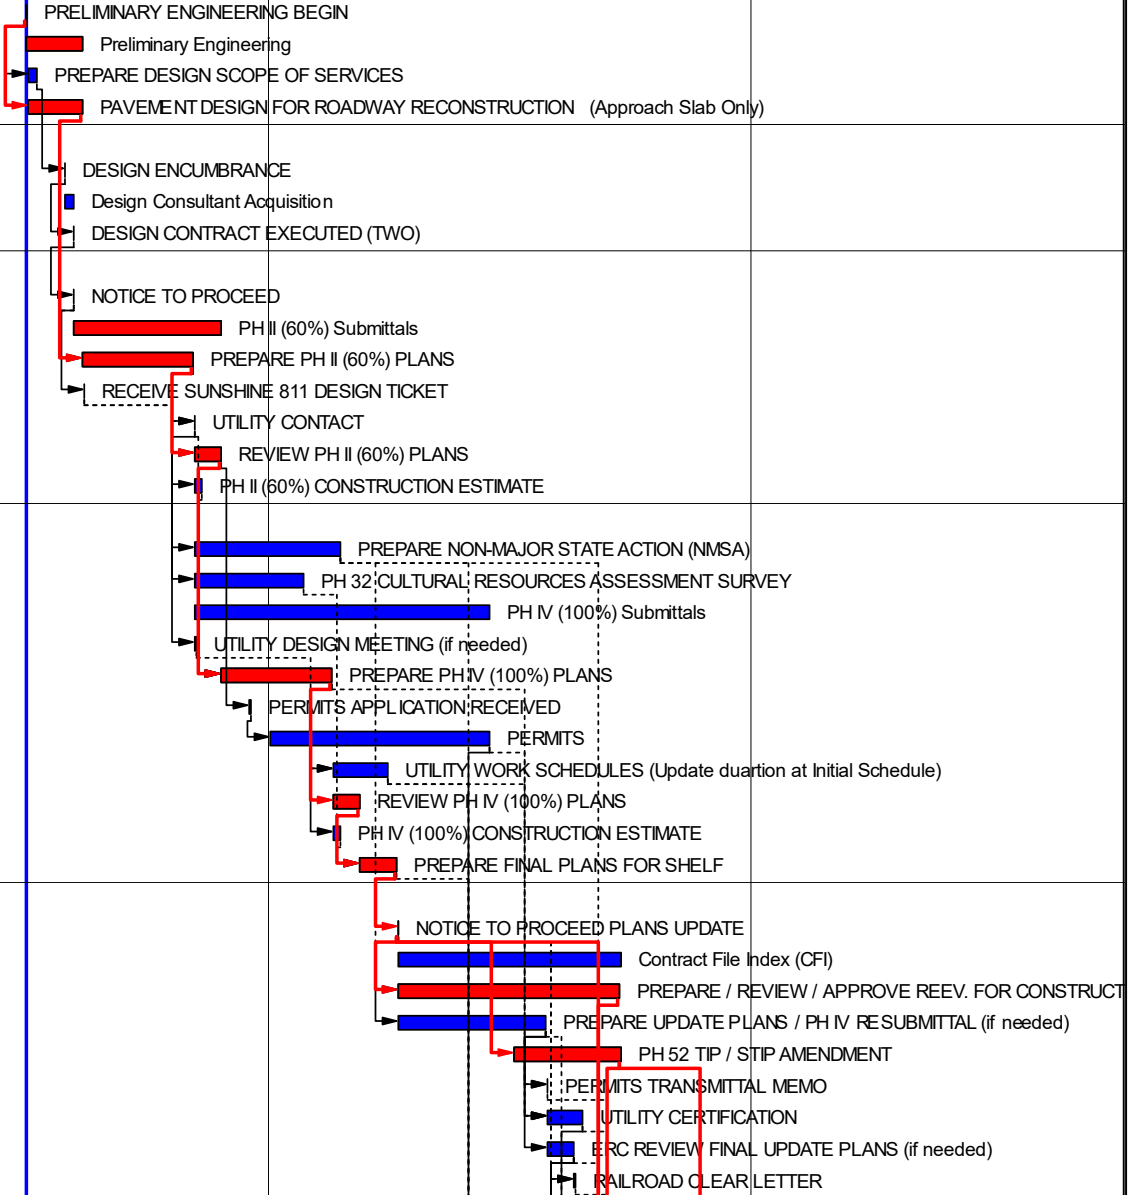

Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	RESPONSIBLE PART	2026	2027	2028
187010	R/W CERTIFICATION FOR CONSTRUCTION	1	25	20-Aug-27	20-Aug-27	H.BANAS			R/W CERTIFICATION FOR CONSTRUCTION
220020	MODIFY FINAL UPDATE PLANS (if needed)	15	15	20-Aug-27	09-Sep-27				MODIFY FINAL UPDATE PLANS (if needed)
171010	CALENDAR DAY RECOMMENDATION	3	18	27-Aug-27	31-Aug-27	E.BUSH			CALENDAR DAY RECOMMENDATION
376010	STATUS OF ENVIRONMENTAL CERTIFICATION	1	0	24-Sep-27	24-Sep-27	V.CARLISLE			STATUS OF ENVIRONMENTAL CERTIFICATION
248010	PRELIMINARY ENGINEERING CERTIFICATION	1	0	24-Sep-27	24-Sep-27				PRELIMINARY ENGINEERING CERTIFICATION
PH 52: PRODUCTION READY		75	0	18-Jun-27	30-Sep-27				
904010	PID	1	73	18-Jun-27	18-Jun-27	A.IVEY			PID
204010	PRODUCTION DATE	1	0	30-Sep-27	30-Sep-27	A.IVEY			PRODUCTION DATE
PH 52: PLANS PROCESSING		89	0	01-Oct-27	02-Feb-28				
226010	PS&E SUBMITTAL	1	0	01-Oct-27	01-Oct-27	A.IVEY			PS&E SUBMITTAL
242010	PS&E REVIEW I	15	0	01-Oct-27	21-Oct-27				PS&E REVIEW I
WBS226	Plans Processing	89	0	01-Oct-27	02-Feb-28				Plans Processing
242020	PS&E REVIEW II	10	0	05-Nov-27	18-Nov-27				PS&E REVIEW II
242030	PS&E REVIEW III	5	0	03-Dec-27	09-Dec-27				PS&E REVIEW III
297040	PREPARE AUTHORIZATION ESTIMATE	5	0	03-Dec-27	09-Dec-27	UNASSIGNED			PREPARE AUTHORIZATION ESTIMATE
370010	TRANSMIT PS&E PACKAGE TO DISTRICT CONTRACTS	1	0	09-Dec-27	09-Dec-27	J.SMALLEY			TRANSMIT PS&E PACKAGE TO DISTRICT CON
229070	ADVERTISE DISTRICT CONTRACT	39	0	10-Dec-27	02-Feb-28	R.DODSON			ADVERTISE DISTRICT CONTRACT
280TBD	LETTING DATE (TBD)	1	0	02-Feb-28	02-Feb-28				LETTING DATE (TBD)
PH 62: CEI CONSULTANT ACQUISITION		6	0	25-Feb-28	03-Mar-28				
408010	CEI ENCUMBERED	1	0	25-Feb-28	25-Feb-28	R.DODSON			CEI ENCUMBERED
WBS203	CEI Consultant Acquisition	6	0	25-Feb-28	03-Mar-28				CEI Consultant Acquisition
203010	CEI CONTRACT EXECUTED (TWO)	1	0	03-Mar-28	03-Mar-28				CEI CONTRACT EXECUTED (TW
