


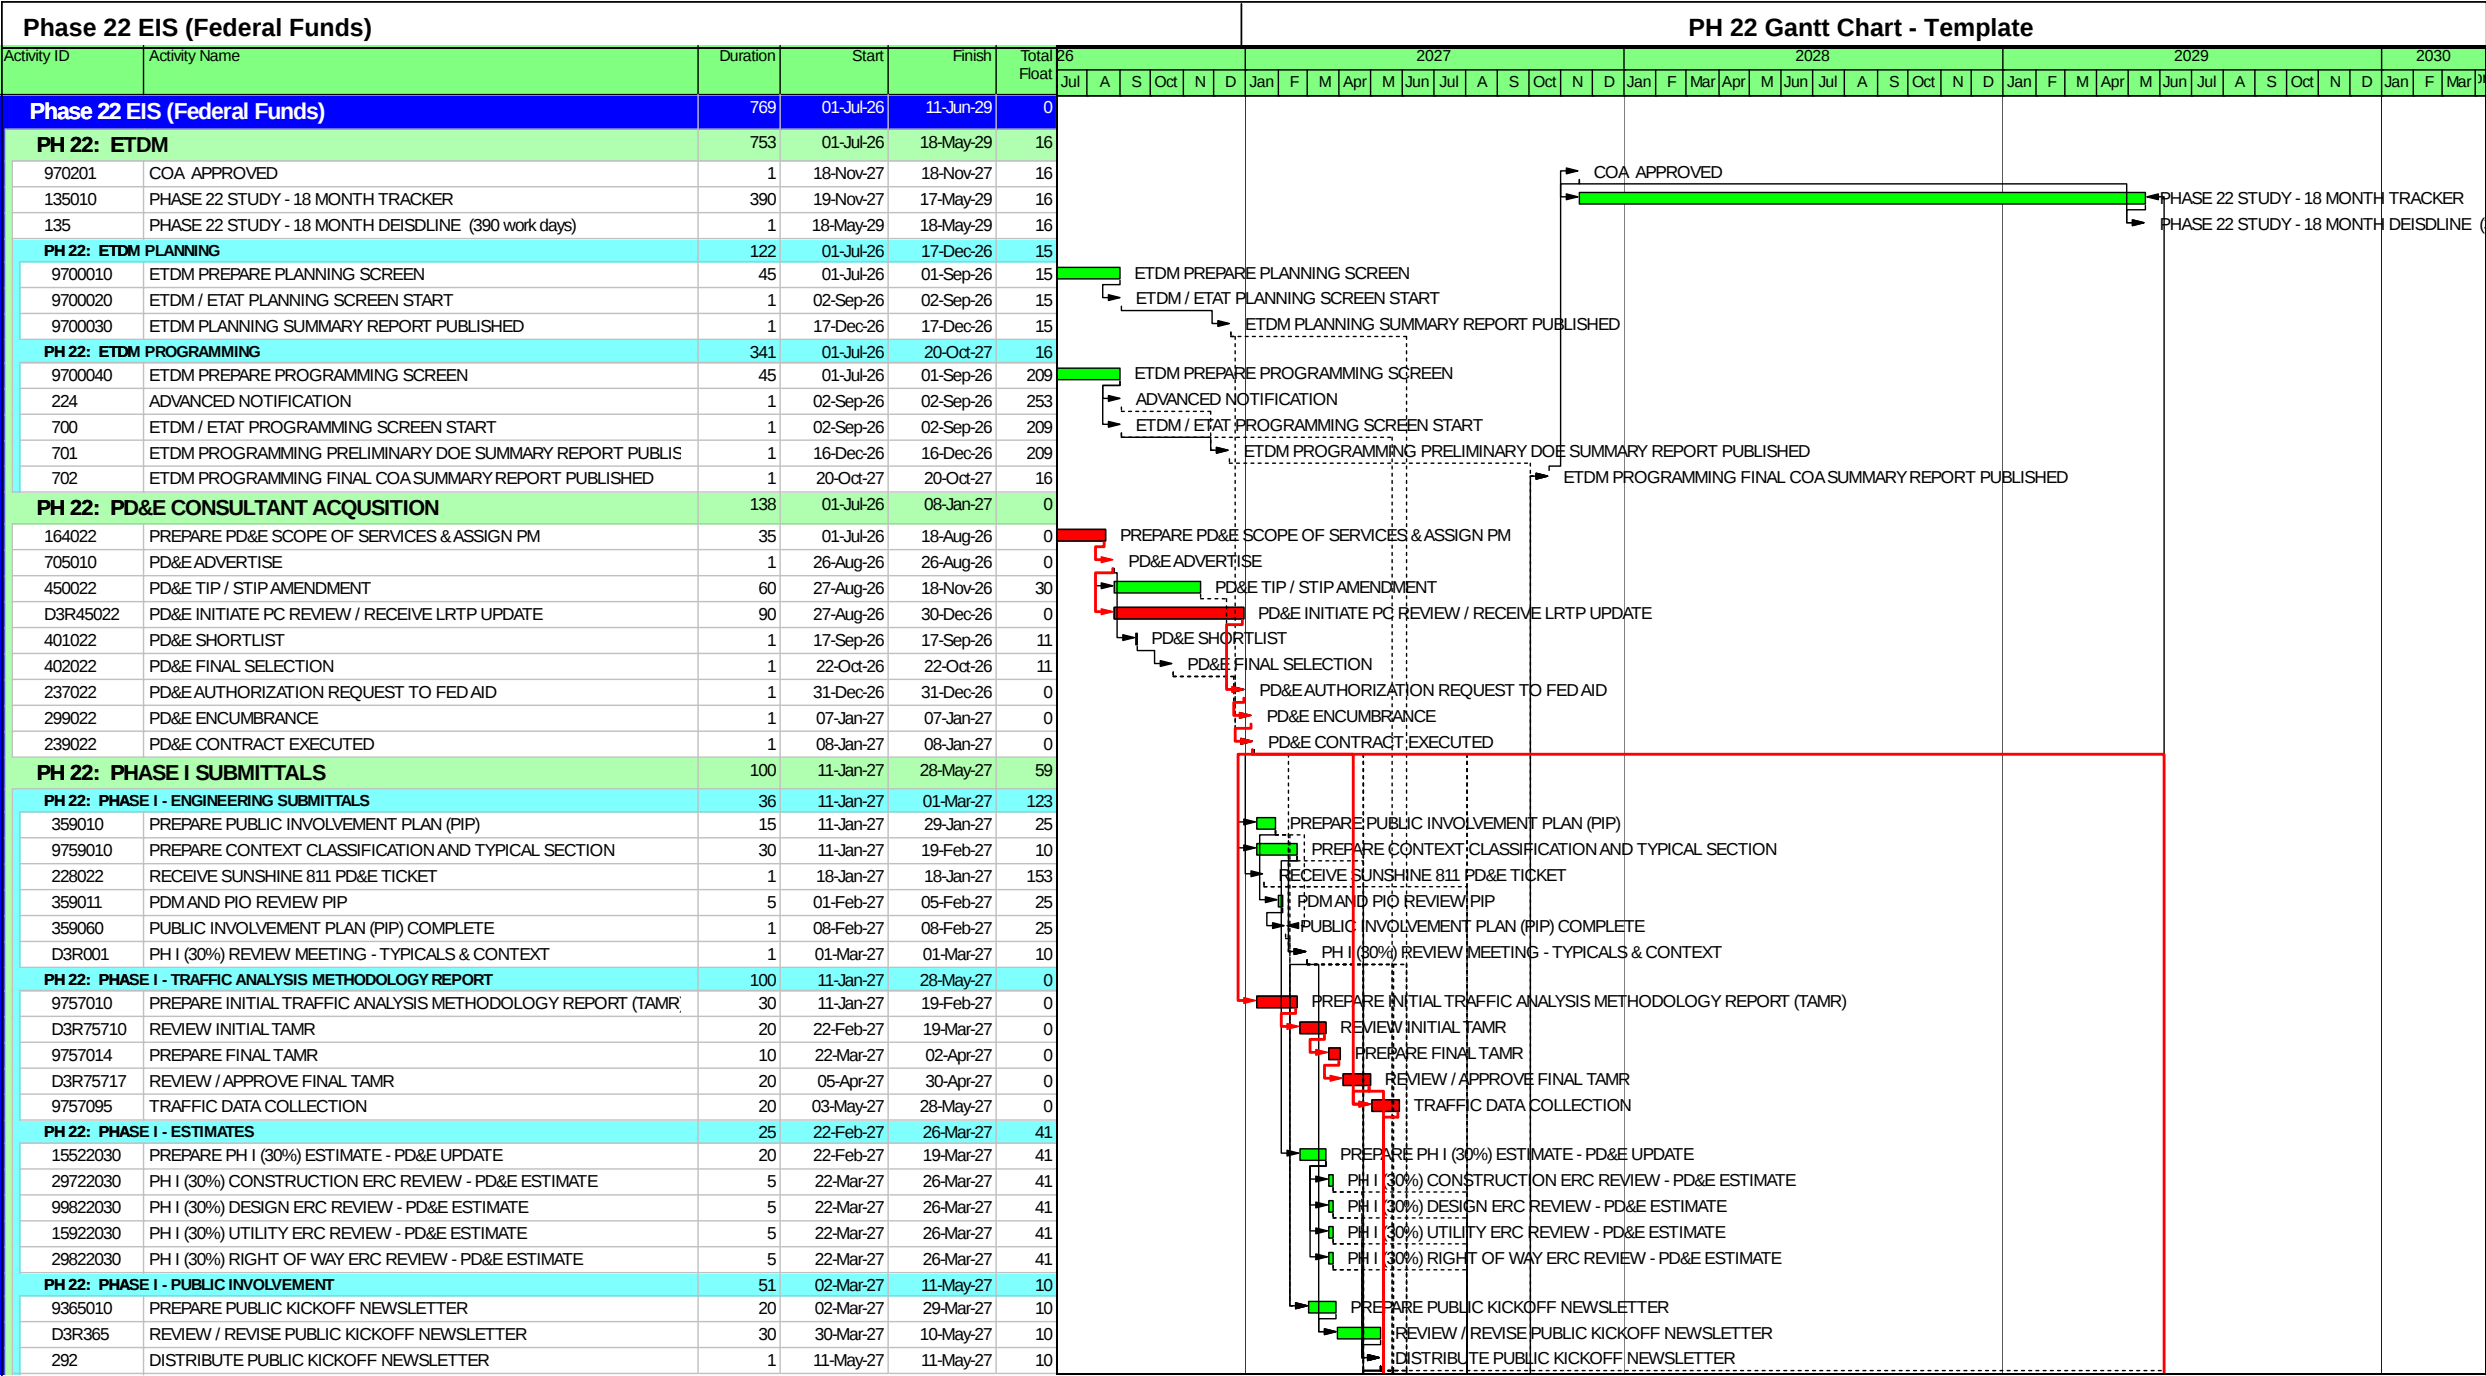

Phase 22 EIS (Federal Funds)						PH 22 Gantt Chart - Template																																															
Activity ID	Activity Name	Duration	Start	Finish	Total Float	2026							2027							2028							2029							2030																			
						Jul	A	S	O	N	D	Jan	F	M	Apr	M	Jun	Jul	A	S	O	N	D	Jan	F	Mar	Apr	M	Jun	Jul	A	S	O	N	D	Jan	F	M	Apr	M	Jun	Jul	A	S	O	N	D	Jan	F	Mar			
PH 22: PHASE II SUBMITTALS																																																					
PH 22: PHASE II - ENGINEERING SUBMITTALS																																																					
1002220	PREPARE HYDRAULIC REPORT(S) & SLIP STUDY	20	12-May-27	08-Jun-27	72																																																
2712210	PREPARE GEOTECH REPORT	20	12-May-27	08-Jun-27	72																																																
159000	PREPARE / SUBMIT UTILITY PACKAGE	20	12-May-27	08-Jun-27	72																																																
1092220	POND DATA COLLECTION	20	12-May-27	08-Jun-27	40																																																
1192210	PREPARE INITIAL CONCEPTUAL DESIGN PLANS	30	12-May-27	22-Jun-27	10																																																
1092210	STORMWATER MANAGEMENT ALTERNATIVES REPORT (SMART)	2	09-Jun-27	10-Jun-27	40																																																
1092230	PREPARE POND SITING REPORT (PSR) / CONCEPTUAL DRAINAGE DESIGN REPORT (CDDR)	30	11-Jun-27	22-Jul-27	40																																																
9710	PREPARE PLANNING CONSISTENCY REPORT	10	23-Jun-27	06-Jul-27	53																																																
D3R002	PH II (60%) REVIEW MEETING -TYPICALS & CONCEPTS	1	30-Jun-27	30-Jun-27	10																																																
9730	REVIEW PLANNING CONSISTENCY REPORT	20	07-Jul-27	03-Aug-27	70																																																
D3R3651	REVIEW / REVISE PHASE II - ENGINEERING SUBMITTAL	20	23-Jul-27	19-Aug-27	40																																																
274	BRIDGE HYDRAULIC REPORT COMPLETE	1	20-Aug-27	20-Aug-27	40																																																
100	LOCATION HYDRAULIC REPORT COMPLETE	1	20-Aug-27	20-Aug-27	40																																																
271	GEOTECH REPORT COMPLETE	1	20-Aug-27	20-Aug-27	40																																																
109	POND SITING REPORT COMPLETE	1	20-Aug-27	20-Aug-27	91																																																
PH 22: PHASE II - PROJECT TRAFFIC ANALYSIS REPORT (PTAR)																																																					
9757020	PREPARE INITIAL PROJECT TRAFFIC ANALYSIS REPORT (PTAR)	30	31-May-27	09-Jul-27	0																																																
D3R7571	REVIEW INITIAL PTAR	20	12-Jul-27	06-Aug-27	0																																																
9757011	PREPARE FINAL PTAR	20	09-Aug-27	03-Sep-27	46																																																
757	APPROVE FINAL PTAR	5	06-Sep-27	10-Sep-27	46																																																
PH 22: PHASE II - ESTIMATES																																																					
15522060	PREPARE PH II (60%) ESTIMATE - PD&E UPDATE	20	23-Jul-27	19-Aug-27	41																																																
29722060	PH II (60%) CONSTRUCTION ERC REVIEW - PD&E ESTIMATE	5	20-Aug-27	26-Aug-27	317																																																
15922060	PH II (60%) UTILITY ERC REVIEW - PD&E ESTIMATE	5	20-Aug-27	26-Aug-27	317																																																
29822060	PH II (60%) RIGHT OF WAY ERC REVIEW - PD&E ESTIMATE	5	20-Aug-27	26-Aug-27	317																																																
99822060	PH II (60%) DESIGN ERC REVIEW - PD&E ESTIMATE	5	20-Aug-27	26-Aug-27	317																																																
PH 22: PHASE II - ENVIRONMENTAL SUBMITTALS																																																					
3352200	NOISE METHODOLOGY MEETING (w/ D3 Noise)	1	02-Jun-27	02-Jun-27	37																																																
1412210	PREPARE CONCEPTUAL STAGE RELOCATION PLAN (CSRP)	20	23-Jun-27	20-Jul-27	38																																																
1742210	PREPARE CONTAMINATION SCREENING EVALUATION REPORT (CSER)	20	23-Jun-27	20-Jul-27	38																																																
D3R76001	REVIEW / REVISE PHASE II - ENVIRONMENTAL SUBMITTAL	20	21-Jul-27	17-Aug-27	38																																																
3352211	PREPARE / REVIEW NOISE TRAFFIC DATA SHEET (w/ D3 Noise)	20	26-Jul-27	20-Aug-27	0																																																
3352210	PREPARE INITIAL NOISE STUDY REPORT	20	23-Aug-27	17-Sep-27	0																																																
D3R3351	REVIEW INITIAL NOISE STUDY REPORT	20	20-Sep-27	15-Oct-27	0																																																
PH 22: PHASE II - ENVIRONMENTAL SUBMITTAL - INITIAL NRE																																																					
7612200	NATURAL RESOURCES EVALUATION (NRE) SURVEY	20	23-Jun-27	20-Jul-27	49																																																
7612210	PREPARE INITIAL NRE REPORT	20	21-Jul-27	17-Aug-27	49																																																
D3R7610	REVIEW INITIAL NRE REPORT	20	18-Aug-27	14-Sep-27	49																																																
PH 22: PHASE II - ENVIRONMENTAL SUBMITTAL- INITIAL CRAS																																																					
333000	CULTURAL RESOURCES ASSESSMENT SURVEY (CRAS)	20	23-Jun-27	20-Jul-27	195																																																
333010	PREPARE INITIAL CRAS	20	21-Jul-27	17-Aug-27	195																																																
D3R3331	REVIEW INITIAL CRAS	20	18-Aug-27	14-Sep-27	195																																																
PH 22: PHASE II - SECTION 4(f) DETERMINATION OF APPLICABILITY (DOA)																																																					
975100	SECTION 4(f) APPLICABLE (Y/N?)	1	12-May-27	12-May-27	37																																																
975105	PREPARE INITIAL SECTION 4(f) DETERMINATION OF APPLICABILITY (DOA) SWEPT	20	09-Jun-27	06-Jul-27	18																																																
D3R7511	REVIEW / REVISE INITIAL SECTION 4(f) DOA	20	07-Jul-27	03-Aug-27	18																																																
D3R7510	REVIEW SECTION 4(f) DOA IN SWEPT	10	04-Aug-27	17-Aug-27	18																																																
OEM7511	OEM REVIEW SECTION 4(f) DOA	30	17-Aug-27	28-Sep-27	18																																																

Data Date: 01-Jul-26
Run: 26-May-26

ALL SCHEDULES ARE PRELIMINARY AND SUBJECT TO CHANGE WITHOUT NOTICE

@Primavera Systems, Inc.

Page 2 of 5

[illegible]

