ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
0	PLANNING, PD&E (SEIR) and DESIGN		1282 days	Mon 8/1/16	Tue 6/29/21	0 days		
1	PLANNING ACTIVITIES		251 days	Mon 8/1/16	Mon 7/17/17	0 days		
2	District SWAT Planning Meeting (May take place 6 months to 5 years before SWAT Kickoff Meeting)	746	1 day	Mon 8/1/16	Mon 8/1/16	0 days		3FS+131 days
3	District SWAT Strategy Meeting (6 months after the SWAT Planning Meeting when the Tentative Work Program has been submitted)		2 days	Wed 2/1/17	Thu 2/2/17	0 days	2FS+131 days	6FS+20 days,7FS+20 days,8FS+20 days
4	ETDM PROGRAMMING SCREEN		97 days	Fri 3/3/17	Mon 7/17/17	0 days		
5	ETDM Programming Screen Meeting		20 days	Fri 3/3/17	Thu 3/30/17	0 days		
6	ETDM Programming Screen PED		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9
7	ETDM Programming Screen Purpose and Need		20 days	Fri 3/3/17	Thu 3/30/17	0 days	3FS+20 days	9,15,16
8	Planning Consistency Completion	710	5 days	Fri 3/3/17	Thu 3/9/17	15 days	3FS+20 days	9
9	ETDM PROGRAMMING SCREEN START/ADVANCE NOTIFICATION	700, 224	32 days	Fri 3/31/17	Mon 5/15/17	0 days	6,7,8	10,24
10	ETDM Programming Screen Responses		44 days	Tue 5/16/17	Fri 7/14/17	0 days	9	11
11	ETDM PROGRAMMING PRELIMINARY SUMMARY REPORT PUBLISHED	701	1 day	Mon 7/17/17	Mon 7/17/17	0 days	10	140,13FS+10 days,39
12	PRE-PD&E ACTIVITIES		261 days	Tue 8/1/17	Tue 7/31/18	0 days		
13	SWAT Kickoff Meeting	747	1 day	Tue 8/1/17	Tue 8/1/17	0 days	11FS+10 days	14,16
14	Assign PD&E Project Manager	704	1 day	Wed 8/2/17	Wed 8/2/17	0 days	13	16,24,35FS+30 days,36FS+30 d
15	TRAFFIC FORECAST ANALYSIS		116 days	Thu 8/3/17	Thu 1/11/18	0 days	7	
16	Traffic Methodology Meeting		1 day	Thu 8/3/17	Thu 8/3/17	0 days	7,14,13	17
17	Traffic Methodology Memorandum		10 days	Fri 8/4/17	Thu 8/17/17	0 days	16	18
18	Traffic Data Collection		20 days	Fri 8/18/17	Thu 9/14/17	0 days	17	19
19	Prepare Traffic Projections		40 days	Fri 9/15/17	Thu 11/9/17	0 days	18	20
20	Draft Project Traffic Forecast Report		20 days	Fri 11/10/17	Thu 12/7/17	0 days	19	21,27
21	FDOT Review - Draft Project Traffic Forecast Report		15 days	Fri 12/8/17	Thu 12/28/17	0 days	20	22
22	Final Project Traffic Forecast Report	757	10 days	Fri 12/29/17	Thu 1/11/18	0 days	21	105,39
23	INTERCHANGE ACCESS REQUEST		247 days	Thu 8/3/17	Fri 7/13/18	94 days		
24	Initiate IJR/IMR/SIMR or IOAR		1 day	Thu 8/3/17	Thu 8/3/17	0 days	9,14	25
25	Prepare MLOU		5 days	Fri 8/4/17	Thu 8/10/17	0 days	24	26
26	DIRC/SPO Review of MLOU		10 days	Fri 8/11/17	Thu 8/24/17	75 days	25	27
27	Develop Alternatives		30 days	Fri 12/8/17	Thu 1/18/18	0 days	20,26	28
28	Perform Operational Analysis		30 days	Fri 1/19/18	Thu 3/1/18	0 days	27	29
29	Prepare Preliminary IMR/IJR		45 days	Fri 3/2/18	Thu 5/3/18	0 days	28	30
30	DIRC/SPO Review of Preliminary IJR/IMR		10 days	Fri 5/4/18	Thu 5/17/18	0 days	29	31
31	Prepare Final IJR/IMR		30 days	Fri 5/18/18	Thu 6/28/18	0 days	30	32
32	DIRC/SPO Review of Final IJR/IMR		10 days	Fri 6/29/18	Thu 7/12/18	0 days	31	33
33	IJR/IMR Approval	765	1 day	Fri 7/13/18	Fri 7/13/18	94 days	32	76,95
34	DESIGN RELATED ACTIVITIES		80 days	Thu 9/14/17	Wed 1/3/18	6 days		
35	Design Survey and ROW Mapping		80 days	Thu 9/14/17	Wed 1/3/18	6 days	14FS+30 days	39
36	Geotechnical Investigations		80 days	Thu 9/14/17	Wed 1/3/18	6 days	14FS+30 days	39
37	Pavement Coring Evaluation Report		80 days	Thu 9/14/17	Wed 1/3/18	6 days	14FS+30 days	39
38	DEVELOP SCOPE AND SCHEDULE		21 days	Fri 1/12/18	Fri 2/9/18	0 days		
39	Begin PD&E Scope and Schedule		20 days	Fri 1/12/18	Thu 2/8/18	0 days	11,22,35,36,37	40
40	PD&E SCOPE AND SCHEDULE COMPLETION	703	1 day	Fri 2/9/18	Fri 2/9/18	0 days	39	43,42
41	PROCUREMENT		122 days	Mon 2/12/18	Tue 7/31/18	0 days		
42	PD&E Advertisement	705	1 day	Mon 2/12/18	Mon 2/12/18	0 days	40	43
43	Procurement		120 days	Tue 2/13/18	Mon 7/30/18	0 days	40,42	44
44	Notice to Proceed		1 day	Tue 7/31/18	Tue 7/31/18	0 days	43	47
45	PD&E STUDY		427 days	Wed 8/1/18	Thu 3/19/20	0 days		
46	PROJECT MANAGEMENT		7 days	Wed 8/1/18	Thu 8/9/18	0 days		
47	SEIR START	709	1 day	Wed 8/1/18	Wed 8/1/18	0 days	44	52,48,49
48	Prepare Project Management Plan		5 days	Thu 8/2/18	Wed 8/8/18	0 days	47	50
49	Prepare QC Plan		5 days	Thu 8/2/18	Wed 8/8/18	0 days	47	50
50	Project Kickoff Meeting with FDOT		1 day	Thu 8/9/18	Thu 8/9/18	0 days	48,49	81,82,53,83,84,86,87
51	PUBLIC INVOLVEMENT		389 days	Thu 8/2/18	Tue 1/28/20	68 days		
52	Prepare Public Involvement Plan		20 days	Thu 8/2/18	Wed 8/29/18	31 days	47	55
53	Public Involvement Data Collection		45 days	Fri 8/10/18	Thu 10/11/18	0 days	50	55
54	Prepare for Public Kickoff Meeting	365	47 days	Fri 10/12/18	Mon 12/17/18	62 days		
55	Site Review		1 day	Fri 10/12/18	Fri 10/12/18	0 days	84FS-60 days,52,53	56,57,58
56	Newsletter		20 days	Mon 10/15/18	Fri 11/9/18	0 days	55	59
57	Newspaper Ad		20 days	Mon 10/15/18	Fri 11/9/18	0 days	55	59
58	Elected/Appointed/Property Owner Letters		20 days	Mon 10/15/18	Fri 11/9/18	0 days	55	59
59	Presentation/Display Material Review		15 days	Mon 11/12/18	Fri 11/30/18	0 days	58,56,57	60
60	Public Kickoff Meeting		1 day	Mon 12/3/18	Mon 12/3/18	0 days	84,81,82,83,86,59	61
61	Public Comment Period		10 days	Tue 12/4/18	Mon 12/17/18	33 days	60	63
62	Prepare for Public Information Meeting	365	76 days	Fri 2/1/19	Fri 5/17/19	0 days		
63	Site Review		1 day	Fri 2/1/19	Fri 2/1/19	0 days	103FS-60 days,61	67,64,65,66
64	Newsletter		20 days	Mon 2/4/19	Fri 3/1/19	0 days	63	67
65	Newspaper Ad		20 days	Mon 2/4/19	Fri 3/1/19	0 days	63	67
66	Elected/Appointed/Property Owner Letters		20 days	Mon 2/4/19	Fri 3/1/19	0 days	63	67
67	Presentation/Display Material Review		15 days	Mon 3/4/19	Fri 3/22/19	29 days	63,64,65,66	68
68	Public Information Meeting	292	1 day	Fri 5/3/19	Fri 5/3/19	0 days	103FS+5 days,67	69
69	Public Comment Period		10 days	Mon 5/6/19	Fri 5/17/19	0 days	68	104,105,71
70	Prepare for Public Hearing	366	101 days	Tue 9/10/19	Tue 1/28/20	333 days		
71	Site Review		20 days	Tue 9/10/19	Mon 10/7/19	0 days	69,141FS-80 days	75,72,73,74
72	Newsletter		20 days	Tue 10/8/19	Mon 11/4/19	0 days	71	75
73	Newspaper Ad		20 days	Tue 10/8/19	Mon 11/4/19	0 days	71	75
74	Elected/Appointed/Property Owner Letters		20 days	Tue 10/8/19	Mon 11/4/19	0 days	71	75
75	Presentation/Display Material Review		15 days	Tue 11/5/19	Mon 11/25/19	20 days	71,72,73,74	76,77
76	Notice of Public Availability		15 days	Tue 12/24/19	Mon 1/13/20	0 days	75,141FS-5 days,113,177	
77	Public Hearing	262	1 day	Tue 1/14/20	Tue 1/14/20	0 days	76,75	78
78	Public Comment Period		10 days	Wed 1/15/20	Tue 1/28/20	0 days	77	142,146,143,144,145
79	ENGINEERING ANALYSIS		341 days	Fri 8/10/18	Fri 11/29/19	0 days		
80	Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	113 days		
81	Roadway Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	50	60
82	Drainage Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	50	60
83	Bridge Data Collection		30 days	Fri 8/10/18	Thu 9/20/18	51 days	50	60
84	Prepare Base Map		30 days	Fri 8/10/18	Thu 9/20/18	51 days	50	60,55FS-60 days
85	Traffic Analysis		95 days	Fri 8/10/18	Thu 12/20/18	0 days		
86	Crash Data and Analysis		20 days	Fri 8/10/18	Thu 9/6/18	61 days	50	60
87	Prepare Capacity Analysis		30 days	Fri 8/10/18	Thu 9/20/18	0 days	50	95,88
88	Draft Project Traffic Analysis Report		20 days	Fri 9/21/18	Thu 10/18/18	0 days	87	89,93,94
89	FDOT Review - Draft Project Traffic Analysis Report		15 days	Fri 10/19/18	Thu 11/8/18	0 days	88	90
90	Final Project Traffic Analysis Report	757	10 days	Fri 11/9/18	Thu 11/22/18	0 days	89	95,105,96,91
91	Prepare 18Kip ESALs Traffic Data		20 days	Fri 11/23/18	Thu 12/20/18	206 days	90	112
92	Alternative Analysis		291 days	Fri 10/19/18	Fri 11/29/19	25 days		
93	Typical Sections Analysis		30 days	Fri 10/19/18	Thu 11/29/18	65 days	88	100
94	Complete Streets/Multi Modal Analysis		30 days	Fri 10/19/18	Thu 11/29/18	65 days	88	100
95	Concept Development		40 days	Fri 11/23/18	Thu 1/17/19	0 days	87,90,33	100,97,98,99
96	Access Management Analysis		40 days	Fri 11/23/18	Thu 1/17/19	30 days	90	100
97	Drainage Analysis		30 days	Fri 1/18/19	Thu 2/28/19	0 days	95	100
98	Utility Coordination & Analysis		30 days	Fri 1/18/19	Thu 2/28/19	0 days	95	100
99	Railroad Coordination		30 days	Fri 1/18/19	Thu 2/28/19	0 days	95	100
100	Evaluation Matrix (1st Draft)		5 days	Fri 3/1/19	Thu 3/7/19	0 days	93,94,97,98,99,96,95	102,101,116,117,118,119,120,1
101	Construction Cost Estimates (LRE)		10 days	Fri 3/8/19	Thu 3/21/19	20 days	100	103
102	Right-of-Way Analysis		20 days	Fri 3/8/19	Thu 4/4/19	10 days	100	103
103	Evaluation Matrix (2nd Draft)		5 days	Fri 4/19/19	Thu 4/25/19	0 days	101,102,116,117,118,168FS+5 days,63FS-60 days	

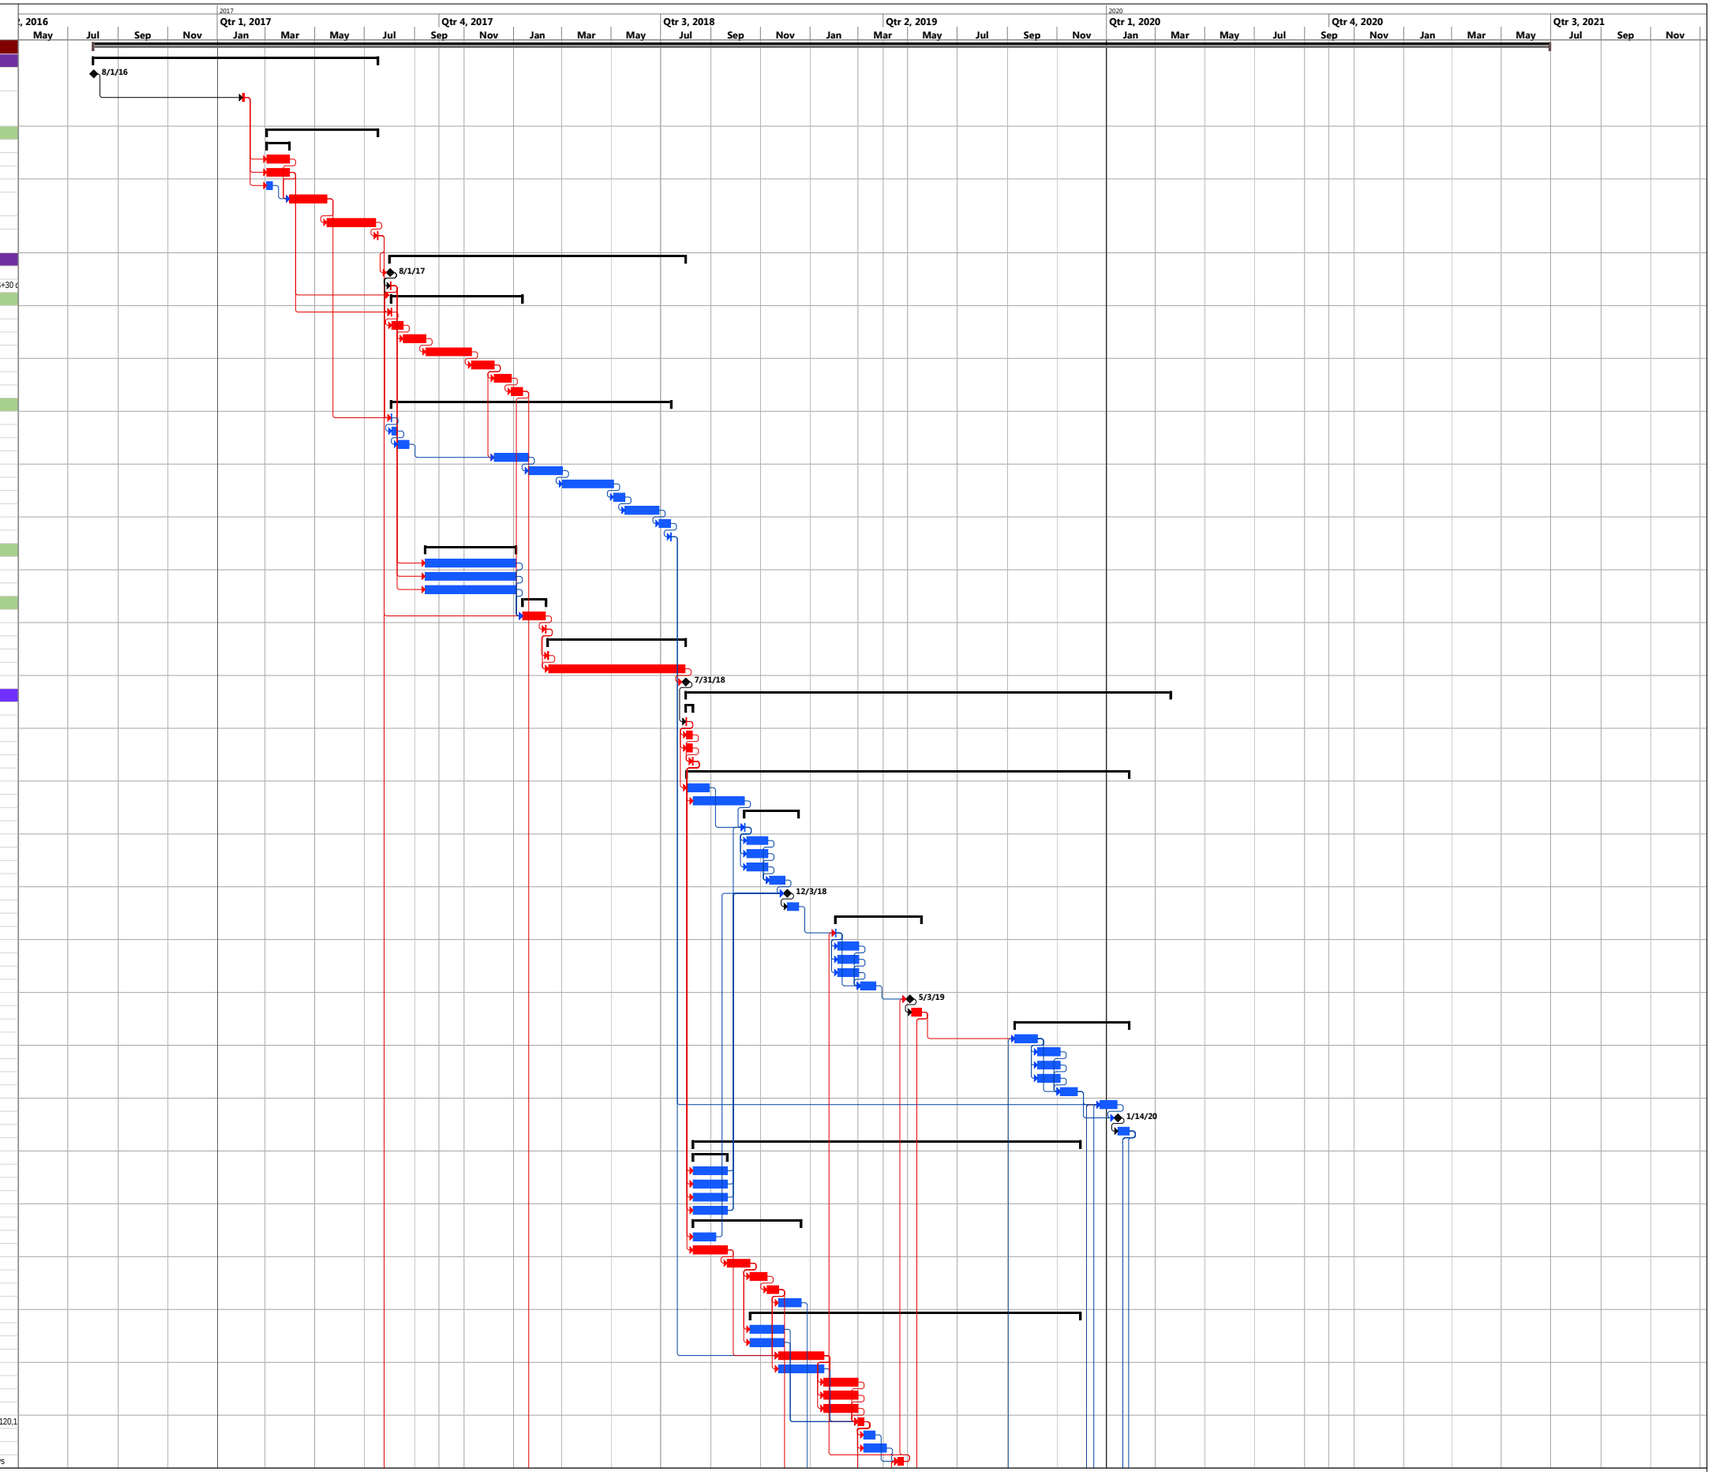

Project: Planning, PD&E (SEIR)
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical

ID	Task Name	PSM Codes	Duration	Start	Finish	Float	Predecessors	Successors
104	Refine Alternatives (based on public input)		20 days	Mon 5/20/19	Fri 6/14/19	532 days	69	
105	Prepare 1st DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech,		30 days	Mon 5/20/19	Fri 6/28/19	0 days	69,22,90	106
106	FDOT Review - 1st DRAFT Engineering Reports		20 days	Mon 7/1/19	Fri 7/26/19	0 days	105	107
107	Update DRAFT Engineering Reports		15 days	Mon 7/29/19	Fri 8/16/19	0 days	106	108
108	VE Study		5 days	Mon 8/19/19	Fri 8/23/19	0 days	107	109FS+20 days
109	VE Issues Resolution		10 days	Mon 9/23/19	Fri 10/4/19	0 days	108FS+20 days	134,132,110,138,140,111,135,1
110	Prepare Typical Section Package		20 days	Mon 10/7/19	Fri 11/1/19	0 days	109	113,114
111	Prepare Design Variations and Exceptions		20 days	Mon 10/7/19	Fri 11/1/19	0 days	109	113
112	Prepare Pavement Design Report		20 days	Mon 10/7/19	Fri 11/1/19	0 days	109,91	113
113	Typical Section Selection	759	20 days	Mon 11/4/19	Fri 11/29/19	0 days	110,111,112	76,151,168
114	FDOT Review - 2nd DRAFT Engineering Reports (Drainage, Utility, Roadway Plans, ITS, Lighting, Pavement, Geotech, PER)		20 days	Mon 11/4/19	Fri 11/29/19	16 days	110	76
115	ENVIRONMENTAL ANALYSIS		172 days	Fri 3/8/19	Mon 11/4/19	0 days		
116	Data Collection & Cultural Resources Assessment Survey		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,124
117	Data Collection & Noise Analysis		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,126
118	Data Collection & Contamination Screen Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,125
119	Wetland Delineation and Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,123
120	Data Collection & Wildlife Survey		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,123
121	Essential Fish Habitat Evaluation		30 days	Fri 3/8/19	Thu 4/18/19	0 days	100	103,123
122	Determination of Section 4(f)		15 days	Fri 3/8/19	Thu 3/28/19	0 days	100	127
123	Prepare 1st Draft Natural Resource Evaluation Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	119,120,121	128
124	Prepare 1st Draft Cultural Resources Assessment Survey		30 days	Fri 4/19/19	Thu 5/30/19	0 days	116	128
125	Prepare 1st Draft Contamination Screen Evaluation Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	118	128
126	Prepare 1st Draft Noise Study Report		30 days	Fri 4/19/19	Thu 5/30/19	0 days	117	128
127	Prepare Draft Section 4(f) Evaluation		30 days	Fri 3/29/19	Thu 5/9/19	15 days	122	128
128	FDOT Review 1st DRAFT Environmental Reports (NRE, CSER, CRAS, Noise, Section 4(f))		20 days	Fri 5/31/19	Thu 6/27/19	0 days	123,124,125,126,127	129
129	Update Environmental Reports		15 days	Fri 6/28/19	Thu 7/18/19	0 days	128	132,130,131
130	Finalize Cultural Resources Assessment Survey	333	10 days	Fri 7/19/19	Thu 8/1/19	46 days	129	132
131	Finalize Natural Resource Evaluation Report	761	10 days	Fri 7/19/19	Thu 8/1/19	46 days	129	134,135
132	Submit CRAS to OEM		20 days	Mon 10/7/19	Fri 11/1/19	0 days	129,109,130	133
133	SHPO Consultation Complete	762	1 day	Mon 11/4/19	Mon 11/4/19	0 days	132	140
134	Submit NRE to USFWS		1 day	Mon 10/7/19	Mon 10/7/19	0 days	109,131	136
135	Submit NRE to NMFS		1 day	Mon 10/7/19	Mon 10/7/19	0 days	109,131	137
136	Informal USFWS Consultation Complete	752	10 days	Tue 10/8/19	Mon 10/21/19	10 days	134	140
137	Informal NMFS Consultation Complete	763	10 days	Tue 10/8/19	Mon 10/21/19	10 days	135	140
138	Prepare Conceptual Relocation Plan		20 days	Mon 10/7/19	Fri 11/1/19	1 day	109	140
139	FINAL SEIR DOCUMENTS		98 days	Tue 11/5/19	Thu 3/19/20	333 days		
140	Prepare DRAFT SEIR		20 days	Tue 11/5/19	Mon 12/2/19	0 days	109,11,133,136,137,13	141
141	FDOT Review DRAFT SEIR	713	20 days	Tue 12/3/19	Mon 12/30/19	0 days	140	76FS-5 days,71FS-80 days
142	Finalize Engineering & Environmental Reports	756	10 days	Wed 1/29/20	Tue 2/11/20	5 days	78	147
143	Finalize Section 4(f) Evaluation	751	5 days	Wed 1/29/20	Tue 2/4/20	0 days	78	146
144	Finalize Noise Study Report	335	5 days	Wed 1/29/20	Tue 2/4/20	0 days	78	146
145	Finalize Preliminary Engineering Report	760	5 days	Wed 1/29/20	Tue 2/4/20	10 days	78	147
146	Prepare FINAL SEIR		10 days	Wed 2/5/20	Tue 2/18/20	0 days	78,143,144	147
147	Submit FINAL SEIR to District OEM		20 days	Wed 2/19/20	Tue 3/17/20	0 days	146,142,145	148FS+2 days
148	District Secretary Approval of SEIR	722	0 days	Thu 3/19/20	Thu 3/19/20	333 days	147FS+2 days	
149	FINAL DESIGN		412 days	Mon 12/2/19	Tue 6/29/21	0 days		
150	60% (PHASE II) PLANS		116 days	Mon 12/2/19	Mon 5/11/20	0 days		
151	Prepare 60% (Phase II) Plans		80 days	Mon 12/2/19	Fri 3/20/20	0 days	113	152
152	Submit 60% Plans & Quantities to FDOT	302	0 days	Fri 3/20/20	Fri 3/20/20	0 days	151	153,169
153	FDOT Review of Phase II Plans		20 days	Mon 3/23/20	Fri 4/17/20	0 days	152	155,154
154	Utility Review & Conflict Resolution		15 days	Mon 4/20/20	Fri 5/8/20	0 days	153	156
155	Prepare and Submit Permit Applications		15 days	Mon 4/20/20	Fri 5/8/20	1 day	153	158
156	ROW Coordination Meeting 60%		1 day	Mon 5/11/20	Mon 5/11/20	0 days	154	158
157	90% (PHASE III) PLANS		86 days	Tue 5/12/20	Tue 9/8/20	44 days		
158	Prepare 90% (Phase III) Plans & Quantities		50 days	Tue 5/12/20	Mon 7/20/20	0 days	155,156	159
159	Submit 90% Plans & Quantities to FDOT	303	0 days	Mon 7/20/20	Mon 7/20/20	0 days	158	160
160	FDOT Review of 90% Plans		20 days	Tue 7/21/20	Mon 8/17/20	0 days	159	161
161	Utility Review & Conflict Resolution		15 days	Tue 8/18/20	Mon 9/7/20	0 days	160	162
162	ROW Coordination Meeting 90%		1 day	Tue 9/8/20	Tue 9/8/20	0 days	161	164
163	100% (PHASE IV) PLANS		50 days	Wed 9/9/20	Tue 11/17/20	44 days		
164	Prepare 100% (Phase IV) Submittal		30 days	Wed 9/9/20	Tue 10/20/20	0 days	162	165
165	Submit 100% (Phase IV) Submittal to FDOT	306	0 days	Tue 10/20/20	Tue 10/20/20	0 days	164	166
166	FDOT Review of 100% (Phase IV) Submittal		20 days	Wed 10/21/20	Tue 11/17/20	0 days	165	179
167	RIGHT OF WAY ACQUISITION		376 days	Mon 12/2/19	Mon 5/10/21	0 days		
168	Determine and Submit ROW Requirements to R/W Office	322	60 days	Mon 12/2/19	Fri 2/21/20	20 days	113	169
169	Final ROW Map/Sketches and Legals to R/W Administration	139	20 days	Mon 3/23/20	Fri 4/17/20	0 days	152,168	170
170	Submit Documents to R/W Administration	268	0 days	Fri 4/17/20	Fri 4/17/20	0 days	169	171
171	Appraisals Review	143	1 day	Mon 4/20/20	Mon 4/20/20	0 days	170	172
172	Perform R/W Appraisals	120	120 days	Tue 4/21/20	Mon 10/5/20	0 days	171	173SS+60 days
173	Negotiations and Land Acquisition	121	120 days	Tue 7/14/20	Mon 12/28/20	0 days	172SS+60 days	174
174	Final ROW Order of Taking	273	0 days	Mon 12/28/20	Mon 12/28/20	0 days	173	175
175	Condemnation	122	60 days	Tue 12/29/20	Mon 3/22/21	0 days	174	176SS+30 days
176	ROW Demo & Clear	125	60 days	Tue 2/9/21	Mon 5/3/21	0 days	175SS+30 days	177FS+5 days
177	ROW Certified	255	0 days	Mon 5/10/21	Mon 5/10/21	0 days	176FS+5 days	187FS+5 days
178	FINAL PLANS		129 days	Wed 11/18/20	Mon 5/17/21	0 days		
179	Plans Completed	201	60 days	Wed 11/18/20	Tue 2/9/21	0 days	166	180
180	Review Final Plans by Estimate & Construction Office		20 days	Wed 2/10/21	Tue 3/9/21	0 days	179	181FS+5 days,182FS+5 days,1
181	ADA Certification		0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
182	All Permits Clear	222	0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
183	Utilities Clear	269	0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
184	Railroad Clear	279	0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
185	Construction Clear	375	0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
186	Environmental Clear	376	0 days	Tue 3/16/21	Tue 3/16/21	44 days	180FS+5 days	187
187	Production Date	204	0 days	Mon 5/17/21	Mon 5/17/21	0 days	181,182,183,184,185,1	190,189
188	SPECIFICATIONS PACKAGE		21 days	Mon 5/17/21	Tue 6/15/21	0 days		
189	Plans to Specs	226	0 days	Mon 5/17/21	Mon 5/17/21	0 days	187	190
190	Prepare Specifications Package	242	21 days	Tue 5/18/21	Tue 6/15/21	0 days	187,189	191FS+10 days
191	PLANS TO TALLAHASSEE	212	0 days	Tue 6/29/21	Tue 6/29/21	0 days	190FS+10 days	

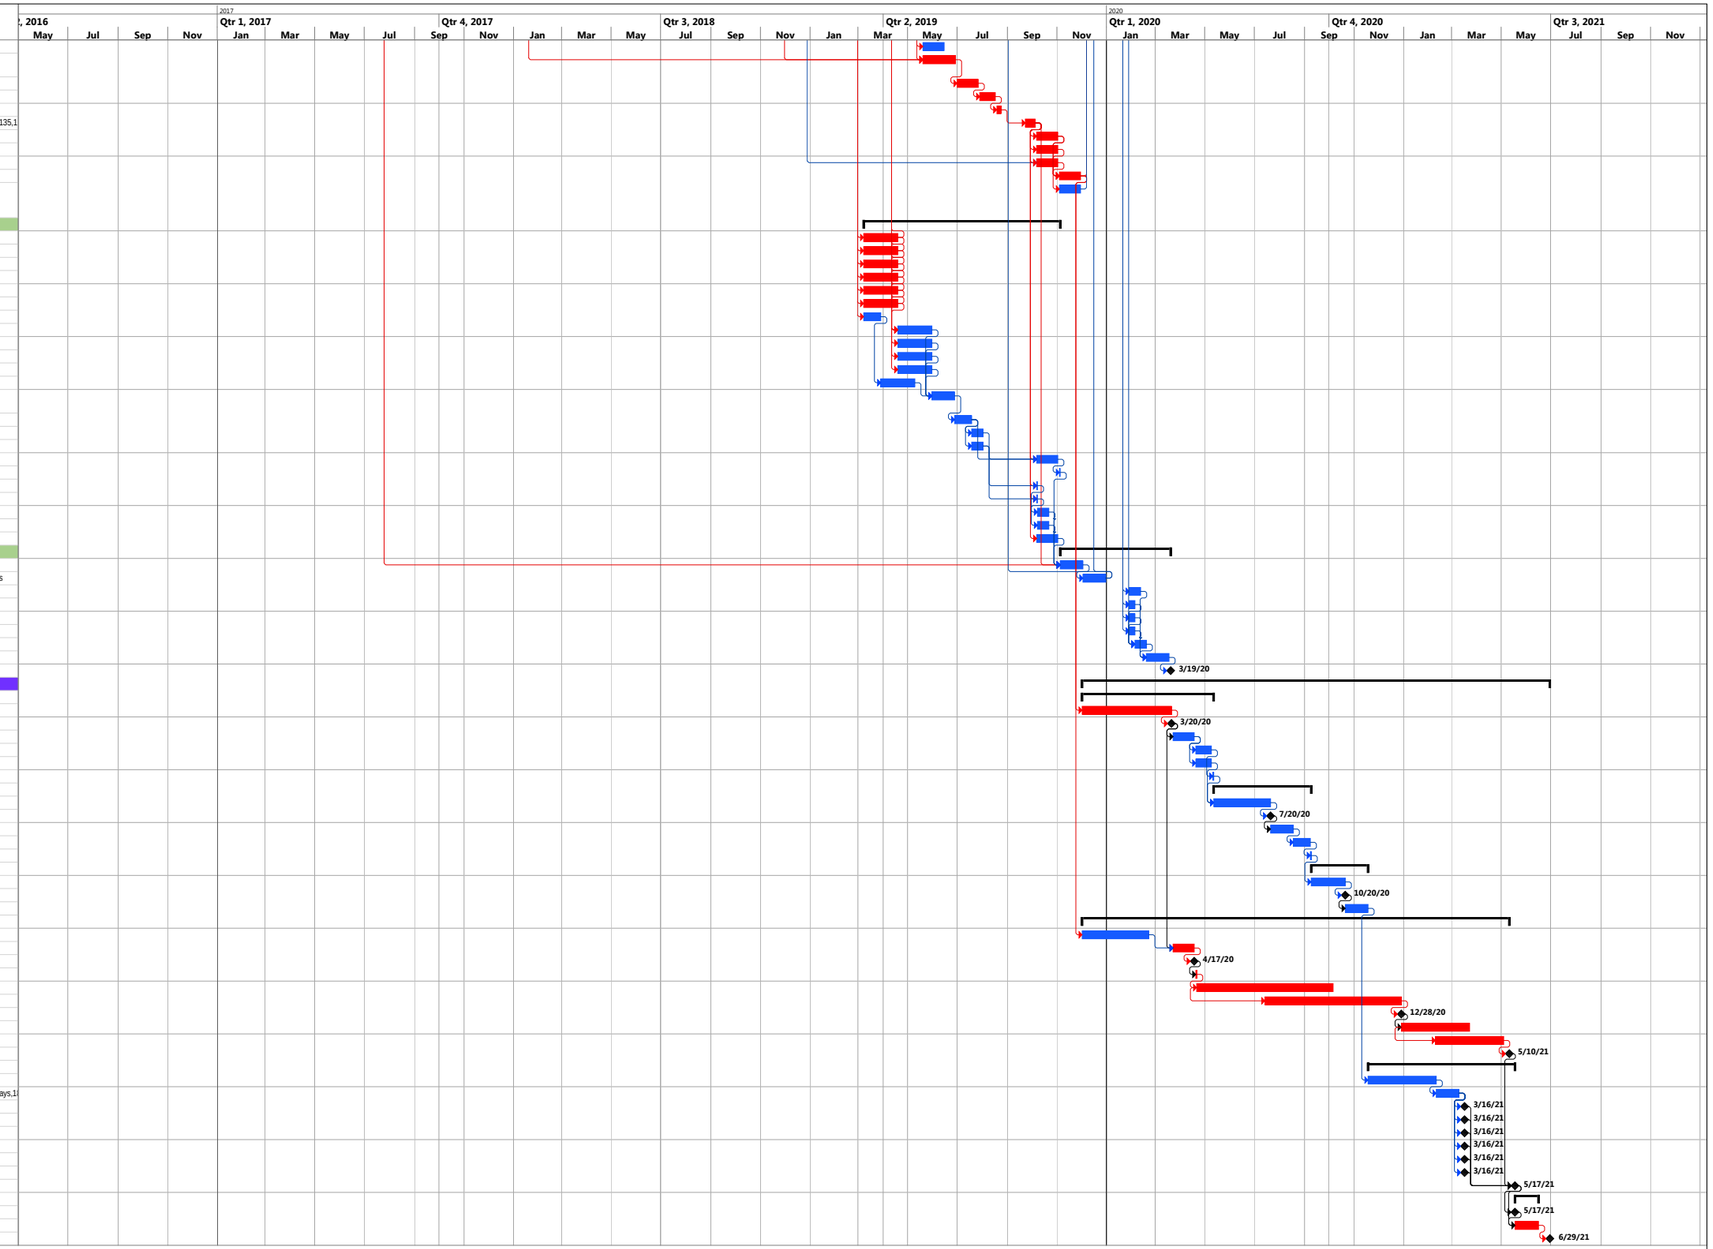

Project: Planning, PD&E (SEIR)
Date: Mon 11/14/16

Task | Milestone | Summary | Project Summary | Critical
